CONTRACT

THIS CONTRACT is dated as of the <u>13th</u> day of <u>April</u> in the year <u>2020</u> by and between <u>Nassau County</u> <u>Board of County Commissioners</u> (County) and <u>CPR Contracting, Inc.</u> (Contractor).

County and Contractor, in consideration of the mutual covenants hereinafter set forth, agree as follows:

ARTICLE 1 - WORK

1.01 Contractor shall complete all Work as specified or indicated in the Contract Documents. The Work is generally described as follows:

This project consists of repairing the Stokes Road bridge over St. Mary's River (Bridge no. 744001) in Nassau County, Florida. Bridge repairs consist of:

- Repair of spalls and delamination in the slab units.
- Installation of pile jackets to protect piles at Bents 4 thru 7 from abrasion damage.

All work shall be in accordance with the construction drawings, specifications, and contract documents.

ARTICLE 2 - THE PROJECT

2.01 The Project for which the Work under the Contract Documents may be the whole or only a part is generally described as follows:

Stokes Road Bridge Repair over St. Mary's River Bid Number NC19-027 Nassau County, Florida

ARTICLE 3 - ENGINEER OF RECORD

3.01 The Project has been designed by <u>Civil Services, Inc.</u>, who is to act as the County's representative, assume all duties and responsibilities, and have the rights and authority assigned to Engineer of Record in the Contract Documents in connection with completion of the Work in accordance with the Contract Documents.

ARTICLE 4 - CONTRACT TIMES

4.01 Time of the Essence

- A. All time limits for Milestones, if any, Substantial Completion, and completion and readiness for final payment as stated in the Contract Documents are of the essence of the Contract.
- B. The Contractor hereby agrees to commence work under this contract on a date to be specified in written "Notice to Proceed" of the County and to fully complete the project as specified in Section 4.02 of this Contract.

4.02 Days to Achieve Substantial Completion and Final Payment

The Work will be substantially completed within <u>60</u> days after the date when the Contract Times commence to run as provided in Paragraph 2.03 of the General Conditions and completed and ready for final payment in accordance with Paragraph 14.07 of the General Conditions within <u>30</u> calendar days from the date of substantial completion. Total contract time shall be <u>90</u> calendar days; for everyday the work goes beyond substantial completion, a day will be removed from final completion so the total days equal <u>90</u> calendar days.

4.03 Liquidated Damages

A. Contractor and the County recognize that time is of the essence of this Contract and that the County will suffer financial loss if the Work is not completed within the times specified in Paragraph 4.02 above, plus any extensions thereof allowed in accordance with Article 12 of the General Conditions. The parties also recognize the delays, expense, and difficulties involved in proving in legal or arbitration proceeding the actual loss suffered by the County if the Work is not completed on time. Accordingly, instead of requiring any such proof, the County and Contractor agree that as liquidated damages for delay (but not as a penalty) Contractor shall pay the County \$1,000.00 for each day that expires after the time specified in Paragraph 4.02 for Substantial Completion and until the Work is substantially complete. After Substantial Completion, if Contractor shall neglect, refuse, or fail to complete the remaining Work within the County \$500.00 for each day that expires after the time specified in Paragraph 4.02 for substantial neglect, refuse, or fail to complete the remaining Work within the County \$500.00 for each day that expires after the time specified in Paragraph 4.02 for substantial neglect, refuse, or fail to complete the remaining Work within the County \$500.00 for each day that expires after the time specified in Paragraph 4.02 for final payment until the Work is completed and ready for final payment.

ARTICLE 5 - CONTRACT PRICE

- **5.01** The County shall pay Contractor for completion of the Work in accordance with the Contract Documents an amount in current funds equal to the sum of the amounts determined pursuant to Paragraph 25 "Payments to Contractor" of the General Conditions and Paragraphs 5.01A below:
 - A. For all Work, at the price stated in the Contractor's Bid, attached hereto as Exhibit "2".

Lump Sum Price: \$217,000

As provided in Paragraph 11.03 of the General Conditions, estimated quantities are not guaranteed, and determinations of actual quantities and classification are to be made by Engineer of Record as provided in paragraph 9.07 of the General Conditions. The final payment for all Unit Price Work shall be an amount equal to the sum of the established unit price for each separately identified item of Unit Price Work times the actual completed and accepted quantity of each item. Unit prices have been computed as provided in Paragraph 11.03 of the General Conditions.

ARTICLE 6 - PAYMENT PROCEDURES

6.01 Submittal and Processing of Payments

A. Contractor shall submit Applications for Payment in accordance with Article 14 of the General Conditions. Applications for Payment will be processed by the County as provided in the General Conditions.

6.02 Progress Payments; Retainage

- A. The County shall make progress payments on account of the Contract Price on the basis of Contractor's Applications for Payment once each month during performance of the Work as provided in Paragraphs 6.02.A.1 and 6.02.A.2 below. All such payments will be measured by the schedule of values established as provided in Paragraph 2.07.A of the General Conditions (and in the case of Unit Price Work based on the number of units completed) or, in the event there is no schedule of values, as provided in the General Requirements:
 - 1. Prior to Substantial Completion, progress payments will be made in an amount equal to the percentage indicated below, but, in each case, less the aggregate of payments previously made and less such amounts as Engineer of Record may determine or the County may withhold, including but not limited to liquidated damages, in accordance with Paragraph 14.02 of the General Conditions:
 - a. <u>90%</u> percent of the Work completed (with the balance being retainage)
 - b. <u>90%</u> percent of cost of materials and equipment not incorporated in the Work (with the balance being retainage).
 - 2. Upon Substantial Completion, the County shall pay an amount sufficient to increase total payments to Contractor to <u>95%</u> percent of the Contract Price (with the balance being retainage), less such amounts as Engineer of Record shall determine or the County may withhold, for incomplete work and for other items in accordance with Paragraph 14.02 of the General Conditions.

6.03 Final Payment

- A. Upon final completion and acceptance of the Work in accordance with Paragraph 14.07 of the General Conditions, the County shall pay the remainder of the Contract Price as recommended by Engineer of Record as provided in said Paragraph 14.07.
- B. Final Release of Retainage and acceptance of the project must be approved by the Board of County Commissioners.

ARTICLE 7 - INTEREST

7.01 All moneys not paid when due as provided in Article 14 of the General Conditions shall bear interest at the rate of 0 percent per annum.

ARTICLE 8 - CONTRACTOR'S REPRESENTATIONS

- 8.01 In order to induce the County to enter into this Contract Contractor makes the following representations:
 - A. Contractor has examined and carefully studied the Contract Documents and the other related data identified in the Bidding Documents.
 - B. Contractor has visited the Site and become familiar with and is satisfied as to the general, local, and Site conditions that may affect cost, progress, and performance of the Work.
 - C. Contractor is familiar with and is satisfied as to all federal, state, and local Laws and Regulations that may affect cost, progress, and performance of the Work.
 - D. Contractor has carefully studied all: (1) reports of explorations and tests of subsurface conditions at or contiguous to the Site and all drawings of physical conditions in or relating to existing surface or subsurface structures at or contiguous to the Site (except Underground Facilities) which have been identified in the Supplementary Conditions as provided in Paragraph 4.02 of the General Conditions and (2) reports and drawings of a Hazardous Environmental Condition, if any, at the Site which has been identified in the Supplementary Conditions as provided in Paragraph 4.06 of the General Conditions.
 - E. Contractor has obtained and carefully studied (or assumes responsibility for having done so) all additional or supplementary examinations, investigations, explorations, tests, studies, and data concerning conditions (surface, subsurface, and Underground Facilities) at or contiguous to the Site which may affect cost, progress, or performance of the Work or which relate to any aspect of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor, including applying the specific means, methods, techniques, sequences, and procedures of construction, if any, expressly required by the Bidding Documents, and safety precautions and programs incident thereto.
 - F. Contractor does not consider that any additional examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Contract Price, within the Contract Times, and in accordance with the other terms and conditions of the Contract Documents.
 - G. Contractor is aware of the general nature of work to be performed by the County and others at the Site that relates to the Work as indicated in the Contract Documents.
 - H. Contractor has correlated the information known to Contractor, information and observations obtained from visits to the Site, reports and drawings identified in the Contract Documents, and all

additional examinations, investigations, explorations, tests, studies, and data with the Contract Documents.

- I. Contractor has given Engineer of Record written notice of all conflicts, errors, ambiguities, or discrepancies that Contractor has discovered in the Contract Documents, and the written resolution thereof by Engineer of Record is acceptable to Contractor.
- J. The Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance of the Work.

ARTICLE 9 - CONTRACT DOCUMENTS

9.01 Contents

- A. The Contract Documents consist of the following:
 - 1. This Contract
 - 2. Project Manual (enumerated as follows):
 - a. Project Manual Table of Contents
 - b. General Conditions
 - c. Supplementary Conditions
 - d. Technical Specifications
 - e. Appendices
 - f. Addenda, if any
 - 3. Exhibits to this Contract (enumerated as follows):
 - 1. General Information and Minimum Insurance Requirements
 - 2. Contractor's Bid
 - 4. Documentation submitted by Contractor prior to Notice of Award
 - 5. Drawing Index, if any (SEE APPENDICES)
 - 6. The following which may (if applicable) be delivered or issued on or after the Effective Date of the Contract and are not attached hereto:
 - a. Payment Bond
 - b. Performance Bond
 - c. Notice of Award
 - d. Application and Certificate for Progress Payment
 - e. Certificate of Insurance
 - f. Notice to Proceed
 - g. Work Change Directives
 - h. Change Orders
 - i. Certificate of Substantial Completion
 - j. Certificate of Final Inspection
 - k. Certificate of Engineer
 - I. Field Order
 - m. Certificate of Final Completion
 - n. CONTRACTOR'S release of Performance Bond
 - o. Construction Drawings and plans/As-Built Drawings

- p. Supplemental Contracts
- q. CONTRACTOR'S Waiver of Lien (Partial)
- r. CONTRACTOR'S Waiver of Lien (Final and Complete)
- s. Subcontractor/Vendor's Waiver of Lien (Final and Complete)
- t. Consent of Surety to Final Payment
- u. CONTRACTOR'S Request for Information
- B. The documents listed in Paragraph 9.01.A are attached to this Contract (except as expressly noted otherwise above).
- C. There are no Contract Documents other than those listed above in this Article 9
- D. The Contract Documents may only be amended, modified, or supplemented as provided in paragraph 3.04 of the General Conditions.

ARTICLE 10 - MISCELLANEOUS

10.01 Terms

A. Terms used in this Contract will have the meanings indicated in the General Conditions and the Supplementary Conditions.

10.02 Assignment of Contract

A. No assignment by a party hereto of any rights under or interests in the Contract will be binding on another party hereto without the written consent of the party sought to be bound; and, specifically but without limitation, moneys that may become due and moneys that are due may not be assigned without such consent (except to the extent that the effect of this restriction may be limited by law), and unless specifically stated to the contrary in any written consent to an assignment, no assignment will release or discharge the assignor from any duty or responsibility under the Contract Documents.

10.03 Successors and Assigns

A. The County and Contractor each binds itself, its partners, successors, assigns, and legal representatives to the other party hereto, its partners, successors, assigns, and legal representatives in respect to all covenants, Contracts, and obligations contained in the Contract Documents.

10.04 Severability

A. Any provision or part of the Contract Documents held to be void or unenforceable under any Law or Regulation shall be deemed stricken, and all remaining provisions shall continue to be valid and binding upon the County and Contractor, who agree that the Contract Documents shall be reformed to replace such stricken provision or part thereof with a valid and enforceable provision that comes as close as possible to expressing the intention of the stricken provision.

10.05 Other Provisions

A. Public Records Requirement:

The County is a public agency subject to Chapter 119, Florida Statutes. IF THE CONTRACTOR HAS QUESTIONS REGARDING THE APPLICATION OF CHAPTER 119, FLORIDA STATUTES, TO THE CONTRACTOR'S DUTY TO PROVIDE PUBLIC RECORDS RELATING TO THIS CONTRACT, CONTACT THE CUSTODIAN OF PUBLIC RECORDS AT (904) 530-6250, DMOODY@NASSAUCOUNTYFL.COM, 96161 NASSAU PLACE, YULEE, FLORIDA 32097. Under this Contract, to the extent that the contractor is providing services to the County, and pursuant to Section 119.0701, Florida Statutes, the contractor shall;

- a. Keep and maintain public records required by the public agency to perform the service.
- b. Upon request from the public agency's custodian of public records, provide the public agency with a copy of the requested records or allow the records to be inspected or copied within a reasonable time at a cost that does not exceed the cost provided in this chapter or as otherwise provided by law.
- c. Ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law for the duration of the contract term and following completion of the contract if the contractor does not transfer the records to the public agency.
- d. Upon completion of the contract, transfer, at no cost, to the public agency all public records in possession of the contractor or keep and maintain public records required by the public agency to perform the service. If the contractor transfers all public records to the public agency upon completion of the contract, the contractor shall destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. If the contractor keeps and maintains public records upon completion of the contract, the contraction shall destroy approach disclosure requirements. If the contractor keeps and maintains public records upon completion of the contract, the contractor shall meet all applicable requirements for retaining public records. All records stored electronically must be provided to the public agency, upon request from the public agency's custodian of public records, in a format that is compatible with the information technology systems of the public agency

[Remainder of page intentionally left blank]

IN WITNESS WHEREOF, the County and Contractor have signed this Contract in whole with copies each being delivered to the County, Contractor, and Engineer of Record. All portions of the Contract Documents have been signed or identified by the County and Contractor or identified by Engineer of Record on their behalf.

This Contract will be effective on the date on which the Contract is signed and delivered by the last of the two parties to sign and deliver (which is the Effective Date of the Contract).

COUNTY	CONTRACTOR
Nassau County Board of County Commissioners	CPR Contracting, Inc.
Signed: Kan Dave	Signed:
Title: Chairman	Title: MGMK Downer
Date: 4-17-20	Date: 476 2020 [CORPORATE SEAL]
Attest:	Attest:
Title: Ex-Officio Clerk	Title: troject Ildnagor
Address for giving notices	Address for giving notices:
96135 Nassau Place, Suite 1	11468 Nas Barlin Ld
Yulee, FL 32097	TACKSONVILLE, Fr. 32226
Phone: <u>904–530–6010</u> FAX: <u>904–321–5784</u>	Phone: 701-733-3500 FAX: 904-723-3505
	License <u>CGC 1518320</u>
	(Where applicable)
Approved as to form by County Attorney Agent for service of process	

(If County is a corporation, attach evidence of authority to sign. If County is a public body, attach evidence of authority to sign and resolution or other documents authorizing execution of County-Contractor Contract.)

(If Contractor is a corporation or a partnership, attach evidence of authority to sign.)

Signature

PROJECT MANUAL

STOKES ROAD BRIDGE REPAIR OVER ST. MARY'S RIVER

TABLE OF CONTENTS

DIVISION 00 - PROCUREMENT AND CONTRACTING REQUIREMENTS

- Section 00 11 10 Advertisement for Bids
- Section 00 21 15 Instructions to Bidders
- Section 00 41 15 Bid Form
- Section 00 43 15 Bid Bond
- Section 00 43 35 Tabulation of Subcontractors & Suppliers
- Section 00 44 55 Florida Trench Safety Act Certification
- Section 00 45 13 Statement of Bidder's Qualifications
- Section 00 45 19 Non-collusion Affidavit
- Section 00 45 20 Drug-Free Workplace Certificate
- Section 00 45 30 Sworn Statement under Section 287.133(3)(a), Florida Statutes, on Public Entity Crimes
- Section 00 45 35 Bidder's Statement of Disputes, Litigation, Arbitration, and Surety Completion, Last Three (3) Years
- Section 00 51 00 Notice of Award
- Section 00 52 15 Agreement
- Section 00 55 00 Notice to Proceed
- Section 00 61 15 Performance Bond
- Section 00 61 16 Payment Bond
- Section 00 62 76 Application and Certificate for Progress Payment
- Section 00 63 15 Contractor's Request for Information
- Section 00 63 36 Field Order
- Section 00 63 49 Work Change Directive
- Section 00 63 63 Change Order Request Form
- Section 00 65 16 Certificate of Substantial Completion
- Section 00 65 19 Certificate of Final Completion
- Section 00 65 20 Waiver and Release of Lien upon Progress Payment
- Section 00 65 21 Waiver and Release of Lien upon Final Payment
- Section 00 72 15 General Conditions
- Section 00 73 15 Supplementary Conditions

DIVISION 01 - GENERAL REQUIREMENTS

- Section 01 11 00 Summary of Work
- Section 01 22 50 Measurement and Payment
- Section 01 31 19 Project Meetings
- Section 01 33 00 Submittal Procedures
- Section 01 41 23 Permits and Fees
- Section 01 45 00 Quality Control
- Section 01 50 00 Temporary Facilities and Controls
- Section 01 55 26 Traffic Control
- Section 01 60 00 Product Requirements
- Section 01 71 23 Field Engineering

Section 01 77 00 - Closeout Procedures

DIVISION 32 - EXTERIOR IMPROVEMENTS Section 32 12 01 – Mobilization Section 32 12 02 – Maintenance of Traffic Section 32 12 03 – Site Preparation Section 32 12 04 - Erosion and Sedimentation Control Section 32 12 15 - Standard Integral Pile Jacket, Non-Structural Up To 16"

APPENDIX A Nassau County - Road Closure Policy

APPENDIX B Nassau County As-Builts Requirement Check List

APPENDIX C Plans and Drawings

EXHIBIT 1 General Information and Minimum Insurance Requirements

GENERAL CONDITIONS

the amount or extent, if any, of any such adjustment, a Claim may be made therefor as provided in Paragraph 10.05.

- 6.10 Taxes
 - A. Contractor/Bidder shall pay all sales, consumer, use, and other similar taxes required to be paid by Contractor/Bidder in accordance with the Laws and Regulations of the place of the Project which are applicable during the performance of the Work.
- 6.11 Use of Site and Other Areas
 - A. Limitation on Use of Site and Other Areas:
 - 1. Contractor/Bidder shall confine construction equipment, the storage of materials and equipment, and the operations of workers to the Site and other areas permitted by Laws and Regulations, and shall not unreasonably encumber the Site and other areas with construction equipment or other materials or equipment. Contractor/Bidder shall assume full responsibility for any damage to any such land or area, or to the County or occupant thereof, or of any adjacent land or areas resulting from the performance of the Work.
 - 2. Should any claim be made by any such County or occupant because of the performance of the Work, Contractor/Bidder shall promptly settle with such other party by negotiation or otherwise resolve the claim by arbitration or other dispute resolution proceeding or at law.
 - 3. To the fullest extent permitted by Laws and Regulations, Contractor/Bidder shall indemnify and hold harmless County and Engineer, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any claim or action, legal or equitable, brought by any such County or occupant against County, Engineer, or any other party indemnified hereunder to the extent caused by or based upon Contractor/Bidder's performance of the Work.
 - B. *Removal of Debris During Performance of the Work:* During the progress of the Work Contractor/Bidder shall keep the Site and other areas free from accumulations of waste materials, rubbish, and other debris. Removal and disposal of such waste materials, rubbish, and other debris shall conform to applicable Laws and Regulations.
 - C. *Cleaning:* Prior to Substantial Completion of the Work Contractor/Bidder shall clean the Site and the Work and make it ready for utilization by County. At the completion of the Work Contractor/Bidder shall remove from the Site all tools, appliances, construction equipment and machinery, and surplus materials and shall restore to original condition all property not designated for alteration by the Contract Documents.
 - D. *Loading Structures:* Contractor/Bidder shall not load nor permit any part of any structure to be loaded in any manner that will endanger the structure, nor shall Contractor/Bidder subject any part of the Work or adjacent property to stresses or pressures that will endanger it.

C. To the fullest extent permitted by Laws and Regulations, Contractor/Bidder shall indemnify and hold harmless County and Engineer, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device not specified in the Contract Documents.

6.08 Permits

A. Unless otherwise provided in the Supplementary Conditions, Contractor/Bidder shall obtain and pay for all construction permits and licenses. County shall assist Contractor/Bidder, when necessary, in obtaining such permits and licenses. Contractor/Bidder shall pay all governmental charges and inspection fees necessary for the prosecution of the Work which are applicable at the time of opening of Bids, or, if there are no Bids, on the Effective Date of the Agreement. County shall pay all charges of utility Countys for connections for providing permanent service to the Work. <u>Permits, licenses, and easements for permanent structures or permanent changes in existing facilities shall be secured and paid for by County, unless otherwise specified. (see SC-6.08.A)</u>

6.09 Laws and Regulations

- A. Contractor/Bidder shall give all notices required by and shall comply with all Laws and Regulations applicable to the performance of the Work. Except where otherwise expressly required by applicable Laws and Regulations, neither County nor Engineer shall be responsible for monitoring Contractor/Bidder's compliance with any Laws or Regulations. <u>Contractor/Bidder shall also cause all SubContractors to comply with all federal, state, county, and municipal laws, ordinances, rules, and regulations bearing on the conduct of the Work. (see SC-6.09.A)</u>
- B. If Contractor/Bidder performs any Work knowing or having reason to know that it is contrary to Laws or Regulations, Contractor/Bidder shall bear all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such Work. However, it shall not be Contractor/Bidder's responsibility to make certain that the Specifications and Drawings are in accordance with Laws and Regulations, but this shall not relieve Contractor/Bidder of Contractor/Bidder's obligations under Paragraph 3.03. If Contractor/Bidder observes that the Contract Documents are at variance with said laws, ordinances, rates, or regulations, Contractor/Bidder shall promptly notify Engineer of Record and the County in writing, and any necessary changes shall be adjusted as provided in the Contract Documents. Contractor/Bidder shall not proceed with the Work until so instructed by County. (see SC-6.09.B)
- C. Changes in Laws or Regulations not known at the time of opening of Bids (or, on the Effective Date of the Agreement if there were no Bids) having an effect on the cost or time of performance of the Work shall be the subject of an adjustment in Contract Price or Contract Times. If County and Contractor/Bidder are unable to agree on entitlement to or on

- D. Contractor/Bidder shall be solely responsible for scheduling and coordinating the Work of SubContractors, Suppliers, and other individuals or entities performing or furnishing any of the Work under a direct or indirect contract with Contractor/Bidder.
- E. Contractor/Bidder shall require all SubContractors, Suppliers, and such other individuals or entities performing or furnishing any of the Work to communicate with Engineer through Contractor/Bidder.
- F. The divisions and sections of the Specifications and the identifications of any Drawings shall not control Contractor/Bidder in dividing the Work among SubContractors or Suppliers or delineating the Work to be performed by any specific trade.
- G. All Work performed for Contractor/Bidder by a SubContractor or Supplier will be pursuant to an appropriate agreement between Contractor/Bidder and the SubContractor or Supplier which specifically binds the SubContractor or Supplier to the applicable terms and conditions of the Contract Documents for the benefit of County and Engineer. Whenever any such agreement is with a SubContractor or Supplier who is listed as a loss payee on the property insurance provided in Paragraph 5.06, the agreement between the Contractor/Bidder and the SubContractor or Supplier will contain provisions whereby the SubContractor or Supplier waives all rights against County, Contractor/Bidder, Engineer, and all other individuals or entities identified in the Supplementary Conditions to be listed as insureds or loss payees (and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them) for all losses and damages caused by, arising out of, relating to, or resulting from any of the perils or causes of loss covered by such policies require separate waiver forms to be signed by any SubContractor or Supplier, Contractor/Bidder will obtain the same.

6.07 Patent Fees and Royalties

- A. Contractor/Bidder shall pay all license fees and royalties and assume all costs incident to the use in the performance of the Work or the incorporation in the Work of any invention, design, process, product, or device which is the subject of patent rights or copyrights held by others. If a particular invention, design, process, product, or device is specified in the Contract Documents for use in the performance of the Work and if, to the actual knowledge of County or Engineer, its use is subject to patent rights or copyrights calling for the payment of any license fee or royalty to others, the existence of such rights shall be disclosed by County in the Contract Documents.
- B. To the fullest extent permitted by Laws and Regulations, County shall indemnify and hold harmless Contractor/Bidder, and its officers, directors, members, partners, employees, agents, consultants, and SubContractors from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals, and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device specified in the Contract Documents, but not identified as being subject to payment of any license fee or royalty to others required by patent rights or copyrights.

6.06 Concerning SubContractors, Suppliers, and Others

- A. Contractor/Bidder shall not employ any SubContractor, Supplier, or other individual or entity (including those acceptable to County as indicated in Paragraph 6.06.B), whether initially or as a replacement, against whom County may have reasonable objection. Contractor/Bidder shall not be required to employ any SubContractor, Supplier, or other individual or entity to furnish or perform any of the Work against whom Contractor/Bidder has reasonable objection. Contractor/Bidder shall not subcontract part(s) or the work, the aggregate cost of which is greater than 50 percent of the contract price, without prior written approval by County. Contractor/Bidder shall cause appropriate provisions to be inserted in all subcontracts relative to the Work that bind SubContractors to Contractor/Bidder by the terms of the Contract Documents insofar as applicable to the work of SubContractors and to give Contractor/Bidder the same power as regards terminating any subcontract that County may exercise over Contractor/Bidder under any provision of the Contract Documents. Nothing contained in the subcontract shall create any contractual relationship between SubContractor and County. Each SubContractor shall discharge all duties and responsibilities of Contractor/Bidder to County covered by his subcontract. (see SC-6.06.A)
- B. If the Supplementary Conditions require the identity of certain SubContractors, Suppliers, or other individuals or entities to be submitted to County in advance for acceptance by County by a specified date prior to the Effective Date of the Agreement, and if Contractor/Bidder has submitted a list thereof in accordance with the Supplementary Conditions, County's acceptance (either in writing or by failing to make written objection thereto by the date indicated for acceptance or objection in the Bidding Documents or the Contract Documents) of any such SubContractor, Supplier, or other individual or entity so identified may be revoked on the basis of reasonable objection after due investigation. Contractor/Bidder shall submit an acceptable replacement for the rejected SubContractor, Supplier, or other individual or entity, and the Contract Price will be adjusted by the difference in the cost occasioned by such replacement, and an appropriate Change Order will be issued. No acceptance by County of any such SubContractor, Supplier, or other individual or entity of any such SubContractor, Supplier, or other individual or entity are replacement, shall constitute a waiver of any right of County or Engineer to reject defective Work. <u>SubContractors and Suppliers shall be identified on the form provided in the Bidding Requirements. (see SC-6.06.B)</u>
- C. Contractor/Bidder shall be fully responsible to County and Engineer for all acts and omissions of the SubContractors, Suppliers, and other individuals or entities performing or furnishing any of the Work just as Contractor/Bidder is responsible for Contractor/Bidder's own acts and omissions. Nothing in the Contract Documents:
 - 1. shall create for the benefit of any such SubContractor, Supplier, or other individual or entity any contractual relationship between County or Engineer and any such SubContractor, Supplier or other individual or entity; nor
 - 2. shall create any obligation on the part of County or Engineer to pay or to see to the payment of any moneys due any such SubContractor, Supplier, or other individual or entity except as may otherwise be required by Laws and Regulations.

- b) available engineering, sales, maintenance, repair, and replacement services; and
- 4) shall contain an itemized estimate of all costs or credits that will result directly or indirectly from use of such substitute item, including costs of redesign and claims of other Contractor/Bidders affected by any resulting change.
- e. Each action mentioned above required for review of proposed substitute items of material or equipment shall be followed in the order given. Failure to do so shall be cause for rejection of the proposed substitution. (see SC-6.05.A.2.e)
- f. <u>Contractor/Bidder shall reimburse County for the charges of Engineer or Engineer's</u> <u>Consultants for evaluation of substitutions.</u> <u>County's reimbursement for the charges</u> <u>shall be a deduction from the Contractor/Bidder's Partial Payment(s).</u> (see SC-<u>6.05.A.2.f)</u>
- B. Substitute Construction Methods or Procedures: If a specific means, method, technique, sequence, or procedure of construction is expressly required by the Contract Documents, Contractor/Bidder may furnish or utilize a substitute means, method, technique, sequence, or procedure of construction approved by Engineer. Contractor/Bidder shall submit sufficient information to allow Engineer, in Engineer's sole discretion, to determine that the substitute proposed is equivalent to that expressly called for by the Contract Documents. The requirements for review by Engineer will be similar to those provided in Paragraph 6.05.A.2.
- C. *Engineer's Evaluation:* Engineer will be allowed a reasonable time within which to evaluate each proposal or submittal made pursuant to Paragraphs 6.05.A and 6.05.B. Engineer may require Contractor/Bidder to furnish additional data about the proposed substitute item. Engineer will be the sole judge of acceptability. No "or equal" or substitute will be ordered, installed or utilized until Engineer's review is complete, which will be evidenced by a Change Order in the case of a substitute and an approved Shop Drawing for an "or equal." Engineer will advise Contractor/Bidder in writing of any negative determination.
- D. *Special Guarantee:* County may require Contractor/Bidder to furnish at Contractor/Bidder's expense a special performance guarantee or other surety with respect to any substitute.
- E. *Engineer's Cost Reimbursement*: Engineer will record Engineer's costs in evaluating a substitute proposed or submitted by Contractor/Bidder pursuant to Paragraphs 6.05.A.2 and 6.05.B. Whether or not Engineer approves a substitute so proposed or submitted by Contractor/Bidder, Contractor/Bidder shall reimburse County for the reasonable charges of Engineer for evaluating each such proposed substitute. Contractor/Bidder shall also reimburse County for the reasonable charges of Engineer for making changes in the Contract Documents (or in the provisions of any other direct contract with County) resulting from the acceptance of each proposed substitute.
- F. *Contractor/Bidder's Expense*: Contractor/Bidder shall provide all data in support of any proposed substitute or "or-equal" at Contractor/Bidder's expense.

- 2) it will conform substantially to the detailed requirements of the item named in the Contract Documents.
- 2. Substitute Items:
 - a. If in Engineer's sole discretion an item of material or equipment proposed by Contractor/Bidder does not qualify as an "or-equal" item under Paragraph 6.05.A.1, it will be considered a proposed substitute item.
 - b. Contractor/Bidder shall submit sufficient information as provided below to allow Engineer to determine if the item of material or equipment proposed is essentially equivalent to that named and an acceptable substitute therefor. Requests for review of proposed substitute items of material or equipment will not be accepted by Engineer from anyone other than Contractor/Bidder.
 - c. The requirements for review by Engineer will be as set forth in Paragraph 6.05.A.2.d, as supplemented by the General Requirements, and as Engineer may decide is appropriate under the circumstances.
 - d. Contractor/Bidder shall make written application to Engineer for review of a proposed substitute item of material or equipment that Contractor/Bidder seeks to furnish or use. The application:
 - 1) shall certify that the proposed substitute item will:
 - a) perform adequately the functions and achieve the results called for by the general design,
 - b) be similar in substance to that specified, and
 - c) be suited to the same use as that specified;
 - 2) will state:
 - a) the extent, if any, to which the use of the proposed substitute item will prejudice Contractor/Bidder's achievement of Substantial Completion on time,
 - b) whether use of the proposed substitute item in the Work will require a change in any of the Contract Documents (or in the provisions of any other direct contract with County for other work on the Project) to adapt the design to the proposed substitute item, and
 - c) whether incorporation or use of the proposed substitute item in connection with the Work is subject to payment of any license fee or royalty;
 - 3) will identify:
 - a) all variations of the proposed substitute item from that specified, and

6.04 Progress Schedule

- A. Contractor/Bidder shall adhere to the Progress Schedule established in accordance with Paragraph 2.07 as it may be adjusted from time to time as provided below.
 - 1. Contractor/Bidder shall submit to Engineer for acceptance (to the extent indicated in Paragraph 2.07) proposed adjustments in the Progress Schedule that will not result in changing the Contract Times. Such adjustments will comply with any provisions of the General Requirements applicable thereto.
 - 2. Proposed adjustments in the Progress Schedule that will change the Contract Times shall be submitted in accordance with the requirements of Article 12. Adjustments in Contract Times may only be made by a Change Order.

6.05 Substitutes and "Or-Equals"

- A. Whenever an item of material or equipment is specified or described in the Contract Documents by using the name of a proprietary item or the name of a particular Supplier, the specification or description is intended to establish the type, function, appearance, and quality required. Unless the specification or description contains or is followed by words reading that no like, equivalent, or "or-equal" item or no substitution is permitted, other items of material or equipment or material or equipment of other Suppliers may be submitted to Engineer for review under the circumstances described below.
 - 1. "Or-Equal" Items: If in Engineer's sole discretion an item of material or equipment proposed by Contractor/Bidder is functionally equal to that named and sufficiently similar so that no change in related Work will be required, it may be considered by Engineer as an "or-equal" item, in which case review and approval of the proposed item may, in Engineer's sole discretion, be accomplished without compliance with some or all of the requirements for approval of proposed substitute items. For the purposes of this Paragraph 6.05.A.1, a proposed item of material or equipment will be considered functionally equal to an item so named if:
 - a. in the exercise of reasonable judgment Engineer determines that:
 - 1) it is at least equal in materials of construction, quality, durability, appearance, strength, and design characteristics;
 - it will reliably perform at least equally well the function and achieve the results imposed by the design concept of the completed Project as a functioning whole; and
 - 3) it has a proven record of performance and availability of responsive service.
 - b. Contractor/Bidder certifies that, if approved and incorporated into the Work:
 - 1) there will be no increase in cost to the County or increase in Contract Times; and

2. will not produce finished work in accordance with the terms of the contract Documents.

County's failure to exercise his right to reject such means, methods, techniques, sequences or procedures shall not relieve the Contractor/Bidder of his obligation to accomplish the result intended in the Contract Documents nor shall the exercise of such right create a cause of action for damages. (see SC-6.01.A)

- B. At all times during the progress of the Work, Contractor/Bidder shall assign a competent resident superintendent who shall not be replaced without written notice to County and Engineer except under extraordinary circumstances.
- 6.02 Labor; Working Hours
 - A. Contractor/Bidder shall provide competent, suitably qualified personnel to survey and lay out the Work and perform construction as required by the Contract Documents. Contractor/Bidder shall at all times maintain good discipline and order at the Site.
 - B. Except as otherwise required for the safety or protection of persons or the Work or property at the Site or adjacent thereto, and except as otherwise stated in the Contract Documents, all Work at the Site shall be performed during regular working hours. Contractor/Bidder will not permit the performance of Work on a Saturday, Sunday, or any legal holiday without County's written consent (which will not be unreasonably withheld) given after prior written notice to Engineer.
 - C. Engineer shall record time and costs required by Engineer and Engineer's Consultants to provide inspection services due to Contractor/Bidder's working beyond regular working hours as defined in the General Requirements. County's reimbursement for the charges shall be a deduction from Contractor/Bidder's Partial Payment(s) in accordance with Section 01 11 00 Part 2.02. (see SC-6.02.C)
- 6.03 Services, Materials, and Equipment
 - A. Unless otherwise specified in the Contract Documents, Contractor/Bidder shall provide and assume full responsibility for all services, materials, equipment, labor, transportation, construction equipment and machinery, tools, appliances, fuel, power, light, heat, telephone, water, sanitary facilities, temporary facilities, and all other facilities and incidentals necessary for the performance, testing, start-up, and completion of the Work.
 - B. All materials and equipment incorporated into the Work shall be as specified or, if not specified, shall be of good quality and new, except as otherwise provided in the Contract Documents. All special warranties and guarantees required by the Specifications shall expressly run to the benefit of County. If required by Engineer, Contractor/Bidder shall furnish satisfactory evidence (including reports of required tests) as to the source, kind, and quality of materials and equipment.
 - C. All materials and equipment shall be stored, applied, installed, connected, erected, protected, used, cleaned, and conditioned in accordance with instructions of the applicable Supplier, except as otherwise may be provided in the Contract Documents.

5.09 Acceptance of Bonds and Insurance; Option to Replace

- A. If either County or Contractor/Bidder has any objection to the coverage afforded by or other provisions of the bonds or insurance required to be purchased and maintained by the other party in accordance with Article 5 on the basis of non conformance with the Contract Documents, the objecting party shall so notify the other party in writing within 10 days after receipt of the certificates (or other evidence requested) required by Paragraph 2.01.B. County and Contractor/Bidder shall each provide to the other such additional information in respect of insurance provided as the other may reasonably request. If either party does not purchase or maintain all of the bonds and insurance required of such party by the Contract Documents, such party shall notify the other party in writing of such failure to purchase prior to the start of the Work, or of such failure to maintain prior to any change in the required coverage. Without prejudice to any other right or remedy, the other party may elect to obtain equivalent bonds or insurance to protect such other party's interests at the expense of the party who was required to provide such coverage, and a Change Order shall be issued to adjust the Contract Price accordingly. If County has any objection to the coverage afforded by or other provisions of Bonds or insurance required to be purchased and maintained by Contractor/Bidder in accordance with Article 5 on the basis of non-conformance with the Contract Documents, County shall so notify Contractor/Bidder in writing within ten days after receipt of the certificates (or other evidence requested) required by paragraph 2.05.C. Contractor/Bidder shall provide to County such additional information in respect of insurance provided as County may reasonably request. (see SC-5.09.A)
- 5.10 Partial Utilization, Acknowledgment of Property Insurer
 - A. If County finds it necessary to occupy or use a portion or portions of the Work prior to Substantial Completion of all the Work as provided in Paragraph 14.05, no such use or occupancy shall commence before the insurers providing the property insurance pursuant to Paragraph 5.06 have acknowledged notice thereof and in writing effected any changes in coverage necessitated thereby. The insurers providing the property insurance shall consent by endorsement on the policy or policies, but the property insurance shall not be canceled or permitted to lapse on account of any such partial use or occupancy.

ARTICLE 6 – CONTRACTOR/BIDDER'S RESPONSIBILITIES

6.01 Supervision and Superintendence

- A. Contractor/Bidder shall supervise, inspect, and direct the Work competently and efficiently, devoting such attention thereto and applying such skills and expertise as may be necessary to perform the Work in accordance with the Contract Documents. Contractor/Bidder shall be solely responsible for the means, methods, techniques, sequences, and procedures of construction. Contractor/Bidder shall not be responsible for the negligence of County or Engineer in the design or specification of a specific means, method, technique, sequence, or procedure of construction which is shown or indicated in and expressly required by the Contract Documents. <u>County reserves the right to reject any means, methods, techniques, sequences, sequences or procedures proposed by Contractor/Bidder which:</u>
 - 1. <u>will constitute or create a hazard to the Work or to the persons or damage to property or</u> <u>existing utilities; or</u>

or resulting from any of the perils or causes of loss covered by such policies and any other property insurance applicable to the Work; and, in addition, waive all such rights against SubContractors and Engineer, and all other individuals or entities identified in the Supplementary Conditions as loss payees (and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them) under such policies for losses and damages so caused. None of the above waivers shall extend to the rights that any party making such waiver may have to the proceeds of insurance held by County as trustee or otherwise payable under any policy so issued.

- B. County waives all rights against Contractor/Bidder, SubContractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them for:
 - 1. loss due to business interruption, loss of use, or other consequential loss extending beyond direct physical loss or damage to County's property or the Work caused by, arising out of, or resulting from fire or other perils whether or not insured by County; and
 - 2. loss or damage to the completed Project or part thereof caused by, arising out of, or resulting from fire or other insured peril or cause of loss covered by any property insurance maintained on the completed Project or part thereof by County during partial utilization pursuant to Paragraph 14.05, after Substantial Completion pursuant to Paragraph 14.07.
- C. Any insurance policy maintained by County covering any loss, damage or consequential loss referred to in Paragraph 5.07.B shall contain provisions to the effect that in the event of payment of any such loss, damage, or consequential loss, the insurers will have no rights of recovery against Contractor/Bidder, SubContractors, or Engineer, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them.

5.08 Receipt and Application of Insurance Proceeds

- A. Any insured loss under the policies of insurance required by Paragraph 5.06 will be adjusted with County and made payable to County as fiduciary for the loss payees, as their interests may appear, subject to the requirements of any applicable mortgage clause and of Paragraph 5.08.B. County shall deposit in a separate account any money so received and shall distribute it in accordance with such agreement as the parties in interest may reach. If no other special agreement is reached, the damaged Work shall be repaired or replaced, the moneys so received applied on account thereof, and the Work and the cost thereof covered by an appropriate Change Order.
- B. County as fiduciary shall have power to adjust and settle any loss with the insurers unless one of the parties in interest shall object in writing within 15 days after the occurrence of loss to County's exercise of this power. If such objection be made, County as fiduciary shall make settlement with the insurers in accordance with such agreement as the parties in interest may reach. If no such agreement among the parties in interest is reached, County as fiduciary shall adjust and settle the loss with the insurers and, if required in writing by any party in interest, County as fiduciary shall give bond for the proper performance of such duties.

- 6. include testing and startup; and
- 7. be maintained in effect until final payment is made unless otherwise agreed to in writing by County, Contractor/Bidder, and Engineer with 30 days written notice to each other loss payee to whom a certificate of insurance has been issued.
- B. County shall purchase and maintain such equipment breakdown insurance or additional property insurance as may be required by the Supplementary Conditions or Laws and Regulations which will include the interests of County, Contractor/Bidder, SubContractors, and Engineer, and any other individuals or entities identified in the Supplementary Conditions, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them, each of whom is deemed to have an insurable interest and shall be listed as a loss payee.
- C. All the policies of insurance (and the certificates or other evidence thereof) required to be purchased and maintained in accordance with this Paragraph 5.06 will contain a provision or endorsement that the coverage afforded will not be canceled or materially changed or renewal refused until at least 30 days prior written notice has been given to County and Contractor/Bidder and to each other loss payee to whom a certificate of insurance has been issued and will contain waiver provisions in accordance with Paragraph 5.07.
- D. County shall not be responsible for purchasing and maintaining any property insurance specified in this Paragraph 5.06 to protect the interests of Contractor/Bidder, SubContractors, or others in the Work to the extent of any deductible amounts that are identified in the Supplementary Conditions. The risk of loss within such identified deductible amount will be borne by Contractor/Bidder, SubContractors, or others suffering any such loss, and if any of them wishes property insurance coverage within the limits of such amounts, each may purchase and maintain it at the purchaser's own expense.
- E. If Contractor/Bidder requests in writing that other special insurance be included in the property insurance policies provided under this Paragraph 5.06, County shall, if possible, include such insurance, and the cost thereof will be charged to Contractor/Bidder by appropriate Change Order. Prior to commencement of the Work at the Site, County shall in writing advise Contractor/Bidder whether or not such other insurance has been procured by County.

5.07 Waiver of Rights

A. County and Contractor/Bidder intend that all policies purchased in accordance with Paragraph 5.06 will protect County, Contractor/Bidder, SubContractors, and Engineer, and all other individuals or entities identified in the Supplementary Conditions as loss payees (and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them) in such policies and will provide primary coverage for all losses and damages caused by the perils or causes of loss covered thereby. All such policies shall contain provisions to the effect that in the event of payment of any loss or damage the insurers will have no rights of recovery against any of the insureds or loss payees thereunder. County and Contractor/Bidder waive all rights against each other and their respective officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them for all losses and damages caused by arising out of

- 6. include completed operations coverage:
 - a. Such insurance shall remain in effect for two years after final payment.
 - b. Contractor/Bidder shall furnish County and each other additional insured identified in the Supplementary Conditions, to whom a certificate of insurance has been issued, evidence satisfactory to County and any such additional insured of continuation of such insurance at final payment and one year thereafter.
- C. <u>Contractor/Bidder shall purchase and maintain coverages listed on Appendix D of Contract</u> <u>Documents.</u>
- 5.05 County's Liability Insurance
 - A. In addition to the insurance required to be provided by Contractor/Bidder under Paragraph 5.04, County, at County's option, may purchase and maintain at County's expense County's own liability insurance as will protect County against claims which may arise from operations under the Contract Documents.
- 5.06 Property Insurance
 - A. Unless otherwise provided in the Supplementary Conditions, County shall purchase and maintain property insurance upon the Work at the Site in the amount of the full replacement cost thereof (subject to such deductible amounts as may be provided in the Supplementary Conditions or required by Laws and Regulations). This insurance shall:
 - 1. include the interests of County, Contractor/Bidder, SubContractors, and Engineer, and any other individuals or entities identified in the Supplementary Conditions, and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them, each of whom is deemed to have an insurable interest and shall be listed as a loss payee;
 - 2. be written on a Builder's Risk "all-risk" policy form that shall at least include insurance for physical loss or damage to the Work, temporary buildings, falsework, and materials and equipment in transit, and shall insure against at least the following perils or causes of loss: fire, lightning, extended coverage, theft, vandalism and malicious mischief, earthquake, collapse, debris removal, demolition occasioned by enforcement of Laws and Regulations, water damage (other than that caused by flood), and such other perils or causes of loss as may be specifically required by the Supplementary Conditions.
 - 3. include expenses incurred in the repair or replacement of any insured property (including but not limited to fees and charges of engineers and architects);
 - 4. cover materials and equipment stored at the Site or at another location that was agreed to in writing by County prior to being incorporated in the Work, provided that such materials and equipment have been included in an Application for Payment recommended by Engineer;
 - 5. allow for partial utilization of the Work by County;

- 3. claims for damages because of bodily injury, sickness or disease, or death of any person other than Contractor/Bidder's employees;
- 4. claims for damages insured by reasonably available personal injury liability coverage which are sustained:
 - a. by any person as a result of an offense directly or indirectly related to the employment of such person by Contractor/Bidder, or
 - b. by any other person for any other reason;
- 5. claims for damages, other than to the Work itself, because of injury to or destruction of tangible property wherever located, including loss of use resulting therefrom; and
- 6. claims for damages because of bodily injury or death of any person or property damage arising out of the Countyship, maintenance or use of any motor vehicle.
- B. The policies of insurance required by this Paragraph 5.04 shall:
 - 1. with respect to insurance required by Paragraphs 5.04.A.3 through 5.04.A.6 inclusive, be written on an occurrence basis, include as additional insureds (subject to any customary exclusion regarding professional liability) County and Engineer, and any other individuals or entities identified in the Supplementary Conditions, all of whom shall be listed as additional insureds, and include coverage for the respective officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of all such additional insureds, and the insurance afforded to these additional insureds shall provide primary coverage for all claims covered thereby;
 - 2. include at least the specific coverages and be written for not less than the limits of liability provided in the Supplementary Conditions or required by Laws or Regulations, whichever is greater;
 - 3. include contractual liability insurance covering Contractor/Bidder's indemnity obligations under Paragraphs 6.11 and 6.20;
 - 4. contain a provision or endorsement that the coverage afforded will not be canceled, materially changed or renewal refused until at least 30 days prior written notice has been given to County and Contractor/Bidder and to each other additional insured identified in the Supplementary Conditions to whom a certificate of insurance has been issued (and the certificates of insurance furnished by the Contractor/Bidder pursuant to Paragraph 5.03 will so provide);
 - 5. remain in effect at least until final payment and at all times thereafter when Contractor/Bidder may be correcting, removing, or replacing defective Work in accordance with Paragraph 13.07; and

Certificate(s) will not constitute a delay beyond Contractor/Bidder's control as defined in paragraph 12.03. (see SC-5.03.G)

- H. Contractor/Bidder shall arrange for its insurers' policies to include, or be endorsed to include, a severability or interest/cross liability provision, so that County will be treated as if a separate policy were in existence, but without increasing the policy limits. (see SC-5.03.H)
- I. <u>Contractor/Bidder's deductibles/self-insured retentions shall be disclosed to County and</u> may be disapproved by the latter. They shall be reduced or eliminated at the option of <u>County</u>. <u>Contractor/Bidder is responsible for the amount of any deductible or self-insured</u> retention. (see SC-6.03.I)
- J. <u>These insurance requirements shall not relieve or limit the liability of Contractor/Bidder.</u> <u>County does not in any way represent that these types or amounts of insurance are sufficient</u> <u>or adequate to protect Contractor/Bidder's interests or liabilities, but are merely minimums.</u> <u>(see SC-5.03.J)</u>
- K. <u>Insurance required of Contractor/Bidder or any other insurance of Contractor/Bidder shall</u> be considered primary, and insurance or self-insurance of County shall be considered excess, as may be applicable to claims that arise out of this contract. (see SC-5.03.K)
- L. Receipt of Certificates or other documentation of insurance or policies or copies of policies by County, or by any of its representatives, which indicate less coverage than required does not constitute a waiver of the Contractor/Bidder's obligation to fulfill the insurance requirements herein. (see SC-5.03.L)
- M. <u>The Contractor/Bidder shall either (a) require each SubContractor to produce and maintain</u> the same coverage as required of the Contractor/Bidder, or (b) insure the activities of <u>SubContractors in his own policy. (see SC-5.03.M)</u>
- N. These insurance requirements are minimums and may not be adequate to cover Contractor/Bidder exposures. (see SC-5.03.N)

5.04 Contractor/Bidder's Insurance

- A. Contractor/Bidder shall purchase and maintain such insurance as is appropriate for the Work being performed and as will provide protection from claims set forth below which may arise out of or result from Contractor/Bidder's performance of the Work and Contractor/Bidder's other obligations under the Contract Documents, whether it is to be performed by Contractor/Bidder, any SubContractor or Supplier, or by anyone directly or indirectly employed by any of them to perform any of the Work, or by anyone for whose acts any of them may be liable:
 - 1. claims under workers' compensation, disability benefits, and other similar employee benefit acts;
 - 2. claims for damages because of bodily injury, occupational sickness or disease, or death of Contractor/Bidder's employees;

5.02 Licensed Sureties and Insurers

A. All bonds and insurance required by the Contract Documents to be purchased and maintained by County or Contractor/Bidder shall be obtained from surety or insurance companies that are duly licensed or authorized in the jurisdiction in which the Project is located to issue bonds or insurance policies for the limits and coverages so required. Such surety and insurance companies shall also meet such additional requirements and qualifications as may be provided in the Supplementary Conditions. <u>Certificates of insurance shall be issued by a company with a Best's rating of at least B+ authorized to do business in the State of Florida. County must approve non-rated insurers. If used, County shall be shown as Certificate Holder, Engineer as Additional Insured and provide a 30-day cancellation notice.</u>

5.03 Certificates of Insurance

- A. Contractor/Bidder shall deliver to County, with copies to each additional insured and loss payee identified in the Supplementary Conditions, certificates of insurance (and other evidence of insurance requested by County or any other additional insured) which Contractor/Bidder is required to purchase and maintain per requirements attached hereto as Appendix D.
- B. County shall deliver to Contractor/Bidder, with copies to each additional insured and loss payee identified in the Supplementary Conditions, certificates of insurance (and other evidence of insurance requested by Contractor/Bidder or any other additional insured) which County is required to purchase and maintain. Insurance policies written on a "Claims Made" form is not acceptable without County's approval. (see SC-5.03.B)
- C. Failure of County to demand such certificates or other evidence of Contractor/Bidder's full compliance with these insurance requirements or failure of County to identify a deficiency in compliance from the evidence provided shall not be construed as a waiver of Contractor/Bidder's obligation to maintain such insurance.
- D. County does not represent that insurance coverage and limits established in this Contract necessarily will be adequate to protect Contractor/Bidder.
- E. The insurance and insurance limits required herein shall not be deemed as a limitation on Contractor/Bidder's liability under the indemnities granted to County in the Contract Documents.
- F. Umbrella Liability insurance is preferred, but an Excess Liability equivalent is acceptable. Whichever type of coverage is provided, it shall not be more restrictive than the underlying insurance policy coverages, including, but not limited to the coverage Trigger, defense, notice of occurrence/accident/circumstances, notice of claim and extended reporting period. (see SC-5.03.F)
- G. <u>No work shall commence under this contract until the required Certificate(s) have been</u> provided. Work shall not continue after expiration (or cancellation) until new Certificate(s) have been provided. Non-continuance of work after expiration (or cancellation) of

against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to a Hazardous Environmental Condition created by Contractor/Bidder or by anyone for whom Contractor/Bidder is responsible. Nothing in this Paragraph 4.06.H shall obligate Contractor/Bidder to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.

I. The provisions of Paragraphs 4.02, 4.03, and 4.04 do not apply to a Hazardous Environmental Condition uncovered or revealed at the Site.

ARTICLE 5 – BONDS AND INSURANCE

5.01 Performance, Payment, and Other Bonds

- A. Contractor/Bidder shall furnish performance and payment bonds, each in an amount at least equal to the Contract Price as security for the faithful performance and payment of all of Contractor/Bidder's obligations under the Contract Documents. These bonds shall remain in effect until one year after the date when final payment becomes due or until completion of the correction period specified in Paragraph 13.07, whichever is later, except as provided otherwise by Laws or Regulations or by the Contract Documents. Contractor/Bidder shall also furnish such other bonds as are required by the Contract Documents.
- B. All bonds shall be in the form prescribed by the Contract Documents except as provided otherwise by Laws or Regulations, and shall be executed by such sureties as are named in the list of "Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies" as published in Circular 570 (amended) by the Financial Management Service, Surety Bond Branch, U.S. Department of the Treasury. All bonds signed by an agent or attorney in-fact must be accompanied by a certified copy of that individual's authority to bind the surety. The evidence of authority shall show that it is effective on the date the agent or attorney-in-fact signed each bond. All Bonds shall be in the form prescribed by the contract Documents or other form approved by County. All else notwithstanding, the terms of all Bonds shall be substantially in the form prescribed by Chapter 255, Florida Statutes. All Bonds shall be executed by Contractor/Bidder and a corporate bonding company licensed to transact such business in the State of Florida and named on the current list of "Surety Companies Acceptable on Federal Bonds" as published in the Treasury Department Circular Number 570. Contractor/Bidder will cause the Bonds to be recorded with the Clerk of the Circuit Court in the county in which the Work is to be performed. Failure to execute bonds in the form prescribed may constitute non-responsiveness on the part of the Contractor/Bidder. The expense for all Bonds shall be the Contractor/Bidder's responsibility. (see SC-5.01.B)
- C. If the surety on any bond furnished by Contractor/Bidder is declared bankrupt or becomes insolvent or its right to do business is terminated in any state where any part of the Project is located or it ceases to meet the requirements of Paragraph 5.01.B, Contractor/Bidder shall promptly notify County and Engineer and shall, within 20 days after the event giving rise to such notification, provide another bond and surety, both of which shall comply with the requirements of Paragraphs 5.01.B and 5.02.

- D. If Contractor/Bidder encounters a Hazardous Environmental Condition or if Contractor/Bidder or anyone for whom Contractor/Bidder is responsible creates a Hazardous Environmental Condition, Contractor/Bidder shall immediately: (i) secure or otherwise isolate such condition; (ii) stop all Work in connection with such condition and in any area affected thereby (except in an emergency as required by Paragraph 6.16.A); and (iii) notify County and Engineer (and promptly thereafter confirm such notice in writing). County shall promptly consult with Engineer concerning the necessity for County to retain a qualified expert to evaluate such condition or take corrective action, if any. Promptly after consulting with Engineer, County shall take such actions as are necessary to permit County to timely obtain required permits and provide Contractor/Bidder the written notice required by Paragraph 4.06.E.
- E. Contractor/Bidder shall not be required to resume Work in connection with such condition or in any affected area until after County has obtained any required permits related thereto and delivered written notice to Contractor/Bidder: (i) specifying that such condition and any affected area is or has been rendered safe for the resumption of Work; or (ii) specifying any special conditions under which such Work may be resumed safely. If County and Contractor/Bidder cannot agree as to entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times, or both, as a result of such Work stoppage or such special conditions under which Work is agreed to be resumed by Contractor/Bidder, either party may make a Claim therefor as provided in Paragraph 10.05.
- F. If after receipt of such written notice Contractor/Bidder does not agree to resume such Work based on a reasonable belief it is unsafe, or does not agree to resume such Work under such special conditions, then County may order the portion of the Work that is in the area affected by such condition to be deleted from the Work. If County and Contractor/Bidder cannot agree as to entitlement to or on the amount or extent, if any, of an adjustment in Contract Price or Contract Times as a result of deleting such portion of the Work, then either party may make a Claim therefor as provided in Paragraph 10.05. County may have such deleted portion of the Work performed by County's own forces or others in accordance with Article 7.
- G. To the fullest extent permitted by Laws and Regulations, County shall indemnify and hold harmless Contractor/Bidder, SubContractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to a Hazardous Environmental Condition, provided that such Hazardous Environmental Condition: (i) was not shown or indicated in the Drawings or Specifications or identified in the Contract Documents to be included within the scope of the Work, and (ii) was not created by Contractor/Bidder or by anyone for whom Contractor/Bidder is responsible. Nothing in this Paragraph 4.06.G shall obligate County to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.
- H. To the fullest extent permitted by Laws and Regulations, Contractor/Bidder shall indemnify and hold harmless County and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and SubContractors of each and any of them from and

reasonable accuracy in the Contract Documents and that Contractor/Bidder did not know of and could not reasonably have been expected to be aware of or to have anticipated. If County and Contractor/Bidder are unable to agree on entitlement to or on the amount or extent, if any, of any such adjustment in Contract Price or Contract Times, County or Contractor/Bidder may make a Claim therefor as provided in Paragraph 10.05.

4.05 Reference Points

A. County shall provide engineering surveys to establish reference points for construction which in Engineer's judgment are necessary to enable Contractor/Bidder to proceed with the Work. Contractor/Bidder shall be responsible for laying out the Work, shall protect and preserve the established reference points and property monuments, and shall make no changes or relocations without the prior written approval of County. Contractor/Bidder shall report to Engineer whenever any reference point or property monument is lost or destroyed or requires relocation because of necessary changes in grades or locations, and shall be responsible for the accurate replacement or relocation of such reference points or property monuments by professionally qualified personnel.

4.06 Hazardous Environmental Condition at Site

- A. *Reports and Drawings:* The Supplementary Conditions identify those reports and drawings known to County relating to Hazardous Environmental Conditions that have been identified at the Site.
- B. Limited Reliance by Contractor/Bidder on Technical Data Authorized: Contractor/Bidder may rely upon the accuracy of the "technical data" contained in such reports and drawings, but such reports and drawings are not Contract Documents. Such "technical data" is identified in the Supplementary Conditions. Except for such reliance on such "technical data," Contractor/Bidder may not rely upon or make any claim against County or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or SubContractors with respect to:
 - 1. the completeness of such reports and drawings for Contractor/Bidder's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences and procedures of construction to be employed by Contractor/Bidder and safety precautions and programs incident thereto; or
 - 2. other data, interpretations, opinions and information contained in such reports or shown or indicated in such drawings; or
 - 3. any Contractor/Bidder interpretation of or conclusion drawn from any "technical data" or any such other data, interpretations, opinions or information.
- C. Contractor/Bidder shall not be responsible for any Hazardous Environmental Condition uncovered or revealed at the Site which was not shown or indicated in Drawings or Specifications or identified in the Contract Documents to be within the scope of the Work. Contractor/Bidder shall be responsible for a Hazardous Environmental Condition created with any materials brought to the Site by Contractor/Bidder, SubContractors, Suppliers, or anyone else for whom Contractor/Bidder is responsible.

consultants, or SubContractors and Engineer's Consultants shall not be liable to Contractor/Bidder for any claims, costs, losses, or damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) sustained by Contractor/Bidder on or in connection with any other project or anticipated project. (see SC-4.03.C.3)

4.04 Underground Facilities

- A. *Shown or Indicated:* The information and data shown or indicated in the Contract Documents with respect to existing Underground Facilities at or contiguous to the Site is based on information and data furnished to County or Engineer by the County's of such Underground Facilities, including County, or by others. Unless it is otherwise expressly provided in the Supplementary Conditions:
 - 1. County and Engineer shall not be responsible for the accuracy or completeness of any such information or data provided by others; and
 - 2. the cost of all of the following will be included in the Contract Price, and Contractor/Bidder shall have full responsibility for:
 - a. reviewing and checking all such information and data;
 - b. locating all Underground Facilities shown or indicated in the Contract Documents;
 - c. coordination of the Work with the County's of such Underground Facilities, including County, during construction; and
 - d. the safety and protection of all such Underground Facilities and repairing any damage thereto resulting from the Work.
- B. Not Shown or Indicated:
 - 1. If an Underground Facility is uncovered or revealed at or contiguous to the Site which was not shown or indicated, or not shown or indicated with reasonable accuracy in the Contract Documents, Contractor/Bidder shall, promptly after becoming aware thereof and before further disturbing conditions affected thereby or performing any Work in connection therewith (except in an emergency as required by Paragraph 6.16.A), identify the County of such Underground Facility and give written notice to that County and to County and Engineer. Engineer will promptly review the Underground Facility and determine the extent, if any, to which a change is required in the Contract Documents to reflect and document the consequences of the existence or location of the Underground Facility. During such time, Contractor/Bidder shall be responsible for the safety and protection of such Underground Facility.
 - 2. If Engineer concludes that a change in the Contract Documents is required, a Work Change Directive or a Change Order will be issued to reflect and document such consequences. An equitable adjustment shall be made in the Contract Price or Contract Times, or both, to the extent that they are attributable to the existence or location of any Underground Facility that was not shown or indicated or not shown or indicated with

4. is of an unusual nature, and differs materially from conditions ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract Documents;

then Contractor/Bidder shall, promptly after becoming aware thereof and before further disturbing the subsurface or physical conditions or performing any Work in connection therewith (except in an emergency as required by Paragraph 6.16.A), notify County and Engineer in writing about such condition. Contractor/Bidder shall not further disturb such condition or perform any Work in connection therewith (except as aforesaid) until receipt of written order to do so.

- B. *Engineer's Review*: After receipt of written notice as required by Paragraph 4.03.A, Engineer will promptly review the pertinent condition, determine the necessity of County's obtaining additional exploration or tests with respect thereto, and advise County in writing (with a copy to Contractor/Bidder) of Engineer's findings and conclusions.
- C. Possible Price and Times Adjustments:
 - 1. The Contract Price or the Contract Times, or both, will be equitably adjusted to the extent that the existence of such differing subsurface or physical condition causes an increase or decrease in Contractor/Bidder's cost of, or time required for, performance of the Work; subject, however, to the following:
 - a. such condition must meet any one or more of the categories described in Paragraph 4.03.A; and
 - b. with respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraphs 9.07 and 11.03.
 - 2. Contractor/Bidder shall not be entitled to any adjustment in the Contract Price or Contract Times if:
 - a. Contractor/Bidder knew of the existence of such conditions at the time Contractor/Bidder made a final commitment to County with respect to Contract Price and Contract Times by the submission of a Bid or becoming bound under a negotiated contract; or
 - b. the existence of such condition could reasonably have been discovered or revealed as a result of any examination, investigation, exploration, test, or study of the Site and contiguous areas required by the Bidding Requirements or Contract Documents to be conducted by or for Contractor/Bidder prior to Contractor/Bidder's making such final commitment; or
 - c. Contractor/Bidder failed to give the written notice as required by Paragraph 4.03.A.
 - 3. If County and Contractor/Bidder are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in the Contract Price or Contract Times, or both, a Claim may be made therefor as provided in Paragraph 10.05. However, neither County, or Engineer, or any of their officers, directors, members, partners, employees, agents,

the County. Contractor/Bidder shall not enter upon private property without first obtaining written permission from the rightful property County (see SC-4.01.C)

- 4.02 Subsurface and Physical Conditions
 - A. Reports and Drawings: The Supplementary Conditions identify:
 - 1. those reports known to County of explorations and tests of subsurface conditions at or contiguous to the Site; and
 - 2. those drawings known to County of physical conditions relating to existing surface or subsurface structures at the Site (except Underground Facilities).
 - B. Limited Reliance by Contractor/Bidder on Technical Data Authorized: Contractor/Bidder may rely upon the accuracy of the "technical data" contained in such reports and drawings, but such reports and drawings are not Contract Documents. Such "technical data" is identified in the Supplementary Conditions. Except for such reliance on such "technical data," Contractor/Bidder may not rely upon or make any claim against County or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or SubContractors with respect to:
 - 1. the completeness of such reports and drawings for Contractor/Bidder's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor/Bidder, and safety precautions and programs incident thereto; or
 - 2. other data, interpretations, opinions, and information contained in such reports or shown or indicated in such drawings; or
 - 3. any Contractor/Bidder interpretation of or conclusion drawn from any "technical data" or any such other data, interpretations, opinions, or information.
 - C. In the preparation of Drawings and Specifications, Engineer or Engineer's Consultant relied upon the following reports(s) of explorations and tests of subsurface conditions at the site: Appendix A. (see SC-4.02.C)
- 4.03 Differing Subsurface or Physical Conditions
 - A. *Notice:* If Contractor/Bidder believes that any subsurface or physical condition that is uncovered or revealed either:
 - 1. is of such a nature as to establish that any "technical data" on which Contractor/Bidder is entitled to rely as provided in Paragraph 4.02 is materially inaccurate; or
 - 2. is of such a nature as to require a change in the Contract Documents; or
 - 3. differs materially from that shown or indicated in the Contract Documents; or

B. The prohibitions of this Paragraph 3.05 will survive final payment, or termination of the Contract. Nothing herein shall preclude Contractor/Bidder from retaining copies of the Contract Documents for record purposes.

3.06 Electronic Data

- A. Unless otherwise stated in the Supplementary Conditions, the data furnished by County or Engineer to Contractor/Bidder, or by Contractor/Bidder to County or Engineer, that may be relied upon are limited to the printed copies (also known as hard copies). Files in electronic media format of text, data, graphics, or other types are furnished only for the convenience of the receiving party. Any conclusion or information obtained or derived from such electronic files will be at the user's sole risk. If there is a discrepancy between the electronic files and the hard copies, the hard copies govern.
- B. Because data stored in electronic media format can deteriorate or be modified inadvertently or otherwise without authorization of the data's creator, the party receiving electronic files agrees that it will perform acceptance tests or procedures within 60 days, after which the receiving party shall be deemed to have accepted the data thus transferred. Any errors detected within the 60-day acceptance period will be corrected by the transferring party.
- C. When transferring documents in electronic media format, the transferring party makes no representations as to long term compatibility, usability, or readability of documents resulting from the use of software application packages, operating systems, or computer hardware differing from those used by the data's creator.

ARTICLE 4 – AVAILABILITY OF LANDS; SUBSURFACE AND PHYSICAL CONDITIONS; HAZARDOUS ENVIRONMENTAL CONDITIONS; REFERENCE POINTS

- 4.01 Availability of Lands
 - A. County shall furnish the Site. County shall notify Contractor/Bidder of any encumbrances or restrictions not of general application but specifically related to use of the Site with which Contractor/Bidder must comply in performing the Work. County will obtain in a timely manner and pay for easements for permanent structures or permanent changes in existing facilities. If Contractor/Bidder and County are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in the Contract Price or Contract Times, or both, as a result of any delay in County's furnishing the Site or a part thereof, Contractor/Bidder may make a Claim therefor as provided in Paragraph 10.05.
 - B. Upon reasonable written request, County shall furnish Contractor/Bidder with a current statement of record legal title and legal description of the lands upon which the Work is to be performed and County's interest therein as necessary for giving notice of or filing a mechanic's or construction lien against such lands in accordance with applicable Laws and Regulations.
 - C. Contractor/Bidder shall provide for all additional lands and access thereto that may be required for temporary construction facilities or storage of materials and equipment. Contractor/Bidder shall obtain said land rights at his own expense and without liability to

Work affected thereby (except in an emergency as required by Paragraph 6.16.A) until an amendment or supplement to the Contract Documents has been issued by one of the methods indicated in Paragraph 3.04.

- 3. Contractor/Bidder shall not be liable to County or Engineer for failure to report any conflict, error, ambiguity, or discrepancy in the Contract Documents unless Contractor/Bidder had actual knowledge thereof.
- B. Resolving Discrepancies:
 - 1. Except as may be otherwise specifically stated in the Contract Documents, the provisions of the Contract Documents shall take precedence in resolving any conflict, error, ambiguity, or discrepancy between the provisions of the Contract Documents and:
 - a. the provisions of any standard, specification, manual, or code, or the instruction of any Supplier (whether or not specifically incorporated by reference in the Contract Documents); or
 - b. the provisions of any Laws or Regulations applicable to the performance of the Work (unless such an interpretation of the provisions of the Contract Documents would result in violation of such Law or Regulation).

3.04 Amending and Supplementing Contract Documents

- A. The Contract Documents may be amended to provide for additions, deletions, and revisions in the Work or to modify the terms and conditions thereof by either a Change Order or a Work Change Directive.
- B. The requirements of the Contract Documents may be supplemented, and minor variations and deviations in the Work may be authorized, by one or more of the following ways:
 - 1. A Field Order;
 - 2. Engineer's approval of a Shop Drawing or Sample (subject to the provisions of Paragraph 6.17.D.3); or
 - 3. Engineer's written interpretation or clarification.

3.05 *Reuse of Documents*

- A. Contractor/Bidder and any SubContractor or Supplier shall not:
 - 1. have or acquire any title to or ownership rights in any of the Drawings, Specifications, or other documents (or copies of any thereof) prepared by or bearing the seal of Engineer or its consultants, including electronic media editions; or
 - 2. reuse any such Drawings, Specifications, other documents, or copies thereof on extensions of the Project or any other project without written consent of County and Engineer and specific written verification or adaptation by Engineer.

- B. It is the intent of the Contract Documents to describe a functionally complete project (or part thereof) to be constructed in accordance with the Contract Documents. Any labor, documentation, services, materials, or equipment that reasonably may be inferred from the Contract Documents or from prevailing custom or trade usage as being required to produce the indicated result will be provided whether or not specifically called for, at no additional cost to County.
- C. Clarifications and interpretations of the Contract Documents shall be issued by Engineer as provided in Article 9.
- 3.02 *Reference Standards*
 - A. Standards, Specifications, Codes, Laws, and Regulations
 - 1. Reference to standards, specifications, manuals, or codes of any technical society, organization, or association, or to Laws or Regulations, whether such reference be specific or by implication, shall mean the standard, specification, manual, code, or Laws or Regulations in effect at the time of opening of Bids (or on the Effective Date of the Agreement if there were no Bids), except as may be otherwise specifically stated in the Contract Documents.
 - 2. No provision of any such standard, specification, manual, or code, or any instruction of a Supplier, shall be effective to change the duties or responsibilities of County, Contractor/Bidder, or Engineer, or any of their SubContractors, consultants, agents, or employees, from those set forth in the Contract Documents. No such provision or instruction shall be effective to assign to County, Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or SubContractors, any duty or authority to supervise or direct the performance of the Work or any duty or authority to undertake responsibility inconsistent with the provisions of the Contract Documents.
- 3.03 Reporting and Resolving Discrepancies
 - A. Reporting Discrepancies:
 - 1. Contractor/Bidder's Review of Contract Documents Before Starting Work: Before undertaking each part of the Work, Contractor/Bidder shall carefully study and compare the Contract Documents and check and verify pertinent figures therein and all applicable field measurements. Contractor/Bidder shall promptly report in writing to Engineer any conflict, error, ambiguity, or discrepancy which Contractor/Bidder discovers, or has actual knowledge of, and shall obtain a written interpretation or clarification from Engineer before proceeding with any Work affected thereby.
 - 2. Contractor/Bidder's Review of Contract Documents During Performance of Work: If, during the performance of the Work, Contractor/Bidder discovers any conflict, error, ambiguity, or discrepancy within the Contract Documents, or between the Contract Documents and (a) any applicable Law or Regulation, (b) any standard, specification, manual, or code, or (c) any instruction of any Supplier, then Contractor/Bidder shall promptly report it to Engineer in writing. Contractor/Bidder shall not proceed with the

procedures for handling Shop Drawings and other submittals, processing Applications for Payment, and maintaining required records.

- B. At this conference County and Contractor/Bidder each shall designate, in writing, a specific individual to act as its authorized representative with respect to the services and responsibilities under the Contract. Such individuals shall have the authority to transmit instructions, receive information, render decisions relative to the Contract, and otherwise act on behalf of each respective party.
- C. <u>County may issue Notice to Proceed at the Preconstruction Conference</u>. <u>Contractor/Bidder</u> <u>shall begin the Work within twenty-four (24) hours of the date given in the Notice to</u> <u>Proceed</u>. If the Contractor/Bidder does not start the Work within fourteen (14) calendar days <u>after this date</u>, <u>County may</u>, at his discretion, terminate Contractor/Bidder in accordance with paragraph 15.02. (see SC-2.06.C)

2.07 Initial Acceptance of Schedules

- A. At least 10 days before submission of the first Application for Payment a conference attended by Contractor/Bidder, Engineer, and others as appropriate will be held to review for acceptability to Engineer as provided below the schedules submitted in accordance with Paragraph 2.05.A. Contractor/Bidder shall have an additional 10 days to make corrections and adjustments and to complete and resubmit the schedules. No progress payment shall be made to Contractor/Bidder until acceptable schedules are submitted to Engineer. A schedule in accordance with Article 5 shall be submitted and accepted by the County and engineer within 30 days of NTP. Should a schedule not be accepted within 30 days of the NTP, it will be considered a breach of contract and reason for termination of the contract for cause in accordance with the General Conditions, Section 15.02. (see SC-2.07.A)
 - 1. The Progress Schedule will be acceptable to Engineer if it provides an orderly progression of the Work to completion within the Contract Times. Such acceptance will not impose on Engineer responsibility for the Progress Schedule, for sequencing, scheduling, or progress of the Work, nor interfere with or relieve Contractor/Bidder from Contractor/Bidder's full responsibility therefor.
 - 2. Contractor/Bidder's Schedule of Submittals will be acceptable to Engineer if it provides a workable arrangement for reviewing and processing the required submittals.
 - 3. Contractor/Bidder's Schedule of Values will be acceptable to Engineer as to form and substance if it provides a reasonable allocation of the Contract Price to component parts of the Work.

ARTICLE 3 – CONTRACT DOCUMENTS: INTENT, AMENDING, REUSE

3.01 Intent

A. The Contract Documents are complementary; what is required by one is as binding as if required by all.

2.02 Copies of Documents

A. County shall furnish to Contractor/Bidder up to ten <u>five</u> printed or hard copies of the Drawings and Project Manual. Additional copies will be furnished upon request at the cost of reproduction. (see SC-2.02.A)

2.03 Commencement of Contract Times; Notice to Proceed

A. The Contract Times will commence to run on the thirtieth day after the Effective Date of the Agreement or, if a Notice to Proceed is given, on the day indicated in the Notice to Proceed. A Notice to Proceed may be given at any time within 30 days after the Effective Date of the Agreement. In no event will the Contract Times commence to run later than the sixtieth day after the day of Bid opening or the thirtieth day after the Effective Date of the Agreement, whichever date is earlier.

2.04 *Starting the Work*

- A. Contractor/Bidder shall start to perform the Work on the date when the Contract Times commence to run. No Work shall be done at the Site prior to the date on which the Contract Times commence to run.
- 2.05 Before Starting Construction
 - A. *Preliminary Schedules:* Within 10 days after the Effective Date of the Agreement <u>At the</u> <u>Preconstruction Conference</u> (unless otherwise specified in the General Requirements), Contractor/Bidder shall submit to Engineer for timely review (see SC-2.05.A):
 - 1. a preliminary Progress Schedule indicating the times (numbers of days or dates) for starting and completing the various stages of the Work, including any Milestones specified in the Contract Documents;
 - 2. a preliminary Schedule of Submittals; and
 - 3. a preliminary Schedule of Values for all of the Work which includes quantities and prices of items which when added together equal the Contract Price and subdivides the Work into component parts in sufficient detail to serve as the basis for progress payments during performance of the Work. Such prices will include an appropriate amount of overhead and profit applicable to each item of Work.
 - B. Before any Work at the Site is started, Contractor/Bidder shall deliver to the County, certificates of insurance that Contractor/Bidder is required to purchase and maintain in accordance with Article 5. (see SC-2.05.B)
- 2.06 Preconstruction Conference; Designation of Authorized Representatives
 - A. Before any Work at the Site is started, a conference attended by County, Contractor/Bidder, Engineer, and others as appropriate will be held to establish a working understanding among the parties as to the Work and to discuss the schedules referred to in Paragraph 2.05.A,

- 1. The word "defective," when modifying the word "Work," refers to Work that is unsatisfactory, faulty, or deficient in that it:
 - a. does not conform to the Contract Documents; or
 - b. does not meet the requirements of any applicable inspection, reference standard, test, or approval referred to in the Contract Documents; or
 - c. has been damaged prior to Engineer's recommendation of final payment (unless responsibility for the protection thereof has been assumed by County at Substantial Completion in accordance with Paragraph 14.04 or 14.05).
- E. Furnish, Install, Perform, Provide:
 - 1. The word "furnish," when used in connection with services, materials, or equipment, shall mean to supply and deliver said services, materials, or equipment to the Site (or some other specified location) ready for use or installation and in usable or operable condition.
 - 2. The word "install," when used in connection with services, materials, or equipment, shall mean to put into use or place in final position said services, materials, or equipment complete and ready for intended use.
 - 3. The words "perform" or "provide," when used in connection with services, materials, or equipment, shall mean to furnish and install said services, materials, or equipment complete and ready for intended use.
 - 4. When "furnish," "install," "perform," or "provide" is not used in connection with services, materials, or equipment in a context clearly requiring an obligation of Contractor/Bidder, "provide" is implied.
- F. Unless stated otherwise in the Contract Documents, words or phrases that have a well-known technical or construction industry or trade meaning are used in the Contract Documents in accordance with such recognized meaning.

ARTICLE 2 – PRELIMINARY MATTERS

- 2.01 Delivery of Bonds and Evidence of Insurance
 - A. When Contractor/Bidder delivers the executed counterparts of the Agreement to County, Contractor/Bidder shall also deliver to County such bonds as Contractor/Bidder may be required to furnish.
 - B. *Evidence of Insurance:* Before any Work at the Site is started, Contractor/Bidder and County shall each deliver to the other, with copies to each additional insured identified in the Supplementary Conditions, certificates of insurance (and other evidence of insurance which either of them or any additional insured may reasonably request) which Contractor/Bidder and County respectively are required to purchase and maintain in accordance with Article 5.

- 49. Unit Price Work—Work to be paid for on the basis of unit prices.
- 50. *Work*—The entire construction or the various separately identifiable parts thereof required to be provided under the Contract Documents. Work includes and is the result of performing or providing all labor, services, and documentation necessary to produce such construction, and furnishing, installing, and incorporating all materials and equipment into such construction, all as required by the Contract Documents.
- 51. Work Change Directive—A written statement to Contractor/Bidder issued on or after the Effective Date of the Agreement and signed by County and recommended by Engineer ordering an addition, deletion, or revision in the Work, or responding to differing or unforeseen subsurface or physical conditions under which the Work is to be performed or to emergencies. A Work Change Directive will not change the Contract Price or the Contract Times but is evidence that the parties expect that the change ordered or documented by a Work Change Directive will be incorporated in a subsequently issued Change Order following negotiations by the parties as to its effect, if any, on the Contract Price or Contract Times.
- 52. <u>Surety- The person, firm, or corporation which is bound by the contract bonds with and for Contractor/Bidder (Principal); and which is held and firmly bound unto County for the conditions of obligations set forth in said bonds (see SC-1.01.52).</u>

1.02 Terminology

- A. The words and terms discussed in Paragraph 1.02.B through F are not defined but, when used in the Bidding Requirements or Contract Documents, have the indicated meaning.
- B. Intent of Certain Terms or Adjectives:
 - 1. The Contract Documents include the terms "as allowed," "as approved," "as ordered," "as directed" or terms of like effect or import to authorize an exercise of professional judgment by Engineer. In addition, the adjectives "reasonable," "suitable," "acceptable," "proper," "satisfactory," or adjectives of like effect or import are used to describe an action or determination of Engineer as to the Work. It is intended that such exercise of professional judgment, action, or determination will be solely to evaluate, in general, the Work for compliance with the information in the Contract Documents and with the design concept of the Project as a functioning whole as shown or indicated in the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective is not intended to and shall not be effective to assign to Engineer any duty or authority to supervise or direct the performance of the Work, or any duty or authority to undertake responsibility contrary to the provisions of Paragraph 9.09 or any other provision of the Contract Documents.
- C. Day:
 - 1. The word "day" means a calendar day of 24 hours measured from midnight to the next midnight.
- D. Defective:

- 38. *Schedule of Submittals*—A schedule, prepared and maintained by Contractor/Bidder, of required submittals and the time requirements to support scheduled performance of related construction activities.
- 39. *Schedule of Values*—A schedule, prepared and maintained by Contractor/Bidder, allocating portions of the Contract Price to various portions of the Work and used as the basis for reviewing Contractor/Bidder's Applications for Payment.
- 40. *Shop Drawings*—All drawings, diagrams, illustrations, schedules, and other data or information which are specifically prepared or assembled by or for Contractor/Bidder and submitted by Contractor/Bidder to illustrate some portion of the Work.
- 41. *Site*—Lands or areas indicated in the Contract Documents as being furnished by County upon which the Work is to be performed, including rights-of-way and easements for access thereto, and such other lands furnished by County which are designated for the use of Contractor/Bidder.
- 42. *Specifications*—That part of the Contract Documents consisting of written requirements for materials, equipment, systems, standards and workmanship as applied to the Work, and certain administrative requirements and procedural matters applicable thereto.
- 43. *SubContractor*—An individual or entity having a direct contract with Contractor/Bidder or with any other SubContractor for the performance of a part of the Work at the Site.
- 44. *Substantial Completion*—The time at which the Work (or a specified part thereof) has progressed to the point where, in the opinion of Engineer, the Work (or a specified part thereof) is sufficiently complete, in accordance with the Contract Documents, so that the Work (or a specified part thereof) can be utilized for the purposes for which it is intended. The terms "substantially complete" and "substantially completed" as applied to all or part of the Work refer to Substantial Completion thereof.
- 45. *Successful Bidder*—The Bidder submitting a responsive Bid to whom County makes an award.
- 46. *Supplementary Conditions*—That part of the Contract Documents which amends or supplements these General Conditions.
- 47. Supplier—A manufacturer, fabricator, supplier, distributor, materialman, or vendor having a direct contract with Contractor/Bidder or with any SubContractor to furnish materials or equipment to be incorporated in the Work by Contractor/Bidder or SubContractor.
- 48. Underground Facilities—All underground pipelines, conduits, ducts, cables, wires, manholes, vaults, tanks, tunnels, or other such facilities or attachments, and any encasements containing such facilities, including those that convey electricity, gases, steam, liquid petroleum products, telephone or other communications, cable television, water, wastewater, storm water, other liquids or chemicals, or traffic or other control systems.

- 25. *Laws and Regulations; Laws or Regulations*—Any and all applicable laws, rules, regulations, ordinances, codes, and orders of any and all governmental bodies, agencies, authorities, and courts having jurisdiction.
- 26. *Liens*—Charges, security interests, or encumbrances upon Project funds, real property, or personal property.
- 27. *Milestone*—A principal event specified in the Contract Documents relating to an intermediate completion date or time prior to Substantial Completion of all the Work.
- 28. *Notice of Award*—The written notice by County to the Successful Bidder stating that upon timely compliance by the Successful Bidder with the conditions precedent listed therein, County will sign and deliver the Agreement.
- 29. Notice to Proceed—A written notice given by County to Contractor/Bidder/Bidder fixing the date on which the Contract Times will commence to run and on which Contractor/Bidder/Bidder shall start to perform the Work under the Contract Documents.
- 30. PCBs—Polychlorinated biphenyls.
- 31. *Petroleum*—Petroleum, including crude oil or any fraction thereof which is liquid at standard conditions of temperature and pressure (60 degrees Fahrenheit and 14.7 pounds per square inch absolute), such as oil, petroleum, fuel oil, oil sludge, oil refuse, gasoline, kerosene, and oil mixed with other non-Hazardous Waste and crude oils.
- 32. *Progress Schedule*—A schedule, prepared and maintained by Contractor/Bidder, describing the sequence and duration of the activities comprising the Contractor/Bidder's plan to accomplish the Work within the Contract Times.
- 33. *Project*—The total construction of which the Work to be performed under the Contract Documents may be the whole, or a part.
- 34. *Project Manual*—The bound documentary information prepared for bidding and constructing the Work. A listing of the contents of the Project Manual, which may be bound in one or more volumes, is contained in the table(s) of contents.
- 35. *Radioactive Material*—Source, special nuclear, or byproduct material as defined by the Atomic Energy Act of 1954 (42 USC Section 2011 et seq.) as amended from time to time.
- 36. *Resident Project Representative*—The authorized representative of Engineer who may be assigned to the Site or any part thereof.
- 37. *Samples*—Physical examples of materials, equipment, or workmanship that are representative of some portion of the Work and which establish the standards by which such portion of the Work will be judged.

- 12. Contract Documents—Those items so designated in the Agreement. Only printed or hard copies of the items listed in the Agreement are Contract Documents. Approved Shop Drawings, other Contractor/Bidder submittals, and the reports and drawings of subsurface and physical conditions are not Contract Documents.
- 13. *Contract Price*—The moneys payable by County to Contractor/Bidder for completion of the Work in accordance with the Contract Documents as stated in the Agreement (subject to the provisions of Paragraph 11.03 in the case of Unit Price Work).
- 14. *Contract Times*—The number of days or the dates stated in the Agreement to: (i) achieve Milestones, if any; (ii) achieve Substantial Completion; and (iii) complete the Work so that it is ready for final payment as evidenced by Engineer's written recommendation of final payment.
- 15. *Contractor/Bidder/Bidder*—The individual or entity with whom County has entered into the Agreement.
- 16. Cost of the Work-See Paragraph 11.01 for definition.
- 17. *County-* The individual or entity with whom Contractor/Bidder has entered into the Agreement and for whom the Work is to be performed.
- 18. Drawings—That part of the Contract Documents prepared or approved by Engineer which graphically shows the scope, extent, and character of the Work to be performed by Contractor/Bidder. Shop Drawings and other Contractor/Bidder submittals are not Drawings as so defined.
- 19. *Effective Date of the Agreement*—The date indicated in the Agreement on which it becomes effective, but if no such date is indicated, it means the date on which the Agreement is signed and delivered by the last of the two parties to sign and deliver.
- 20. Engineer—The individual or entity named as such in the Agreement.
- 21. *Field Order*—A written order issued by Engineer which requires minor changes in the Work but which does not involve a change in the Contract Price or the Contract Times.
- 22. General Requirements Sections of Division 1 of the Specifications The General Requirements pertain to all Sections of the specifications. (see SC-1.01.21)
- 23. *Hazardous Environmental Condition*—The presence at the Site of Asbestos, PCBs, Petroleum, Hazardous Waste, or Radioactive Material in such quantities or circumstances that may present a substantial danger to persons or property exposed thereto.
- 24. *Hazardous Waste*—The term Hazardous Waste shall have the meaning provided in Section 1004 of the Solid Waste Disposal Act (42 USC Section 6903) as amended from time to time.

ARTICLE 1 – DEFINITIONS AND TERMINOLOGY

1.01 Defined Terms

- A. Wherever used in the Bidding Requirements or Contract Documents and printed with initial capital letters, the terms listed below will have the meanings indicated which are applicable to both the singular and plural thereof. In addition to terms specifically defined, terms with initial capital letters in the Contract Documents include references to identified articles and paragraphs, and the titles of other documents or forms.
 - 1. Addenda—Written or graphic instruments issued prior to the opening of Bids which clarify, correct, or change the Bidding Requirements or the proposed Contract Documents.
 - 2. *Agreement*—The written instrument which is evidence of the agreement between County and Contractor/Bidder covering the Work.
 - 3. *Application for Payment*—The form acceptable to Engineer which is to be used by Contractor/Bidder during the course of the Work in requesting progress or final payments and which is to be accompanied by such supporting documentation as is required by the Contract Documents.
 - 4. *Asbestos*—Any material that contains more than one percent asbestos and is friable or is releasing asbestos fibers into the air above current action levels established by the United States Occupational Safety and Health Administration.
 - 5. *Bid*—The offer or proposal of a Bidder submitted on the prescribed form setting forth the prices for the Work to be performed.
 - 6. *Bidder*—The individual or entity who submits a Bid directly to County.
 - 7. *Bidding Documents*—The Bidding Requirements and the proposed Contract Documents (including all Addenda).
 - 8. *Bidding Requirements*—The advertisement or invitation to bid, Instructions to Bidders, Bid security of acceptable form, if any, and the Bid Form with any supplements.
 - 9. *Change Order*—A document recommended by Engineer which is signed by Contractor/Bidder and County and authorizes an addition, deletion, or revision in the Work or an adjustment in the Contract Price or the Contract Times, issued on or after the Effective Date of the Agreement.
 - 10. *Claim*—A demand or assertion by County or Contractor/Bidder seeking an adjustment of Contract Price or Contract Times, or both, or other relief with respect to the terms of the Contract. A demand for money or services by a third party is not a Claim.
 - 11. *Contract*—The entire and integrated written agreement between the County and Contractor/Bidder concerning the Work. The Contract supersedes prior negotiations, representations, or agreements, whether written or oral.

Article 16 – Dispute Resolution

16.01 Methods and Procedures

Article 17 – Miscellaneous

- 17.01 Giving Notice
- 17.02 Computation of Times
- 17.03 Cumulative Remedies
- 17.04 Survival of Obligations
- 17.05 Controlling Law
- 17.06 Headings

- 11.01 Cost of the Work
- 11.02 Allowances
- 11.03 Unit Price Work

Article 12 - Change of Contract Price; Change of Contract Times

- 12.01 Change of Contract Price
- 12.02 Change of Contract Times
- 12.03 Delays

Article 13 – Tests and Inspections; Correction, Removal or Acceptance of Defective Work

- 13.01 Notice of Defects
- 13.02 Access to Work
- 13.03 Tests and Inspections
- 13.04 Uncovering Work
- 13.05 County May Stop the Work
- 13.06 Correction or Removal of Defective Work
- 13.07 Correction Period
- 13.08 Acceptance of Defective Work
- 13.09 County May Correct Defective Work

Article 14 – Payments to Contractor/Bidder and Completion

- 14.01 Schedule of Values
- 14.02 Progress Payments
- 14.03 Contractor/Bidder's Warranty of Title
- 14.04 Substantial Completion
- 14.05 Partial Utilization
- 14.06 Final Inspection
- 14.07 Final Payment
- 14.08 Final Completion Delayed
- 14.09 Waiver of Claims

Article 15 – Suspension of Work and Termination

- 15.01 County May Suspend Work
- 15.02 County May Terminate for Cause
- 15.03 County May Terminate For Convenience
- 15.04 Contractor/Bidder May Stop Work or Terminate

- 7.02 Coordination
- 7.03 Legal Relationships

Article 8 – County's Responsibilities

- 8.01 Communications to Contractor/Bidder
- 8.02 Replacement of Engineer
- 8.03 Furnish Data
- 8.04 Pay When Due
- 8.05 Lands and Easements; Reports and Tests
- 8.06 Insurance
- 8.07 Change Orders
- 8.08 Inspections, Tests, and Approvals
- 8.09 Limitations on County's Responsibilities
- 8.10 Undisclosed Hazardous Environmental Condition
- 8.11 Evidence of Financial Arrangements
- 8.12 Compliance with Safety Program

Article 9 – Engineer's Status During Construction

- 9.01 County's Representative
- 9.02 Visits to Site
- 9.03 Project Representative
- 9.04 Authorized Variations in Work
- 9.05 Rejecting Defective Work
- 9.06 Shop Drawings, Change Orders and Payments
- 9.07 Determinations for Unit Price Work
- 9.08 Decisions on Requirements of Contract Documents and Acceptability of Work
- 9.09 Limitations on Engineer's Authority and Responsibilities
- 9.10 Compliance with Safety Program

Article 10 - Changes in the Work; Claims

- 10.01 Authorized Changes in the Work
- 10.02 Unauthorized Changes in the Work
- 10.03 Execution of Change Orders
- 10.04 Notification to Surety
- 10.05 Claims

Article 11 – Cost of the Work; Allowances; Unit Price Work

- 5.02 Licensed Sureties and Insurers
- 5.03 Certificates of Insurance
- 5.04 Contractor/Bidder's Insurance
- 5.05 County's Liability Insurance
- 5.06 Property Insurance
- 5.07 Waiver of Rights
- 5.08 Receipt and Application of Insurance Proceeds
- 5.09 Acceptance of Bonds and Insurance; Option to Replace
- 5.10 Partial Utilization, Acknowledgment of Property Insurer

Article 6 - Contractor/Bidder's Responsibilities

- 6.01 Supervision and Superintendence
- 6.02 Labor; Working Hours
- 6.03 Services, Materials, and Equipment
- 6.04 Progress Schedule
- 6.05 Substitutes and "Or-Equals"
- 6.06 Concerning SubContractors, Suppliers, and Others
- 6.07 Patent Fees and Royalties
- 6.08 Permits
- 6.09 Laws and Regulations
- 6.10 Taxes
- 6.11 Use of Site and Other Areas
- 6.12 Record Documents
- 6.13 Safety and Protection
- 6.14 Safety Representative
- 6.15 Hazard Communication Programs
- 6.16 Emergencies
- 6.17 Shop Drawings and Samples
- 6.18 Continuing the Work
- 6.19 Contractor/Bidder's General Warranty and Guarantee
- 6.20 Indemnification
- 6.21 Delegation of Professional Design Services

Article 7 – Other Work at the Site

7.01 Related Work at Site

STANDARD GENERAL CONDITIONS OF THE CONSTRUCTION CONTRACT

TABLE OF CONTENTS

Article 1 – Definitions and Terminology

- 1.01 Defined Terms
- 1.02 Terminology

Article 2 – Preliminary Matters

- 2.01 Delivery of Bonds and Evidence of Insurance
- 2.02 Copies of Documents
- 2.03 Commencement of Contract Times; Notice to Proceed
- 2.04 Starting the Work
- 2.05 Before Starting Construction
- 2.06 Preconstruction Conference; Designation of Authorized Representatives
- 2.07 Initial Acceptance of Schedules

Article 3 - Contract Documents: Intent, Amending, Reuse

- 3.01 Intent
- 3.02 Reference Standards
- 3.03 Reporting and Resolving Discrepancies
- 3.04 Amending and Supplementing Contract Documents
- 3.05 Reuse of Documents
- 3.06 Electronic Data

Article 4 – Availability of Lands; Subsurface and Physical Conditions; Hazardous Environmental Conditions; Reference Points

- 4.01 Availability of Lands
- 4.02 Subsurface and Physical Conditions
- 4.03 Differing Subsurface or Physical Conditions
- 4.04 Underground Facilities
- 4.05 Reference Points
- 4.06 Hazardous Environmental Condition at Site

Article 5 – Bonds and Insurance

5.01 Performance, Payment, and Other Bonds

Copyright © 2007 National Society of Professional Engineers 1420 King Street, Alexandria, VA 22314-2794 (703) 684-2882 www.nspe.org

> American Council of Engineering Companies 1015 15th Street N.W., Washington, DC 20005 (202) 347-7474 www.acec.org

American Society of Civil Engineers 1801 Alexander Bell Drive, Reston, VA 20191-4400 (800) 548-2723 www.asce.org

Associated General Contractor/Bidders of America 2300 Wilson Boulevard, Suite 400, Arlington, VA 22201-3308 (703) 548-3118 www.agc.org

The copyright for this EJCDC document is owned jointly by the four EJCDC sponsoring organizations and held in trust for their benefit by NSPE.

Contract CM2831



CONSTRUCTION SPECIFICATIONS INSTITUTE

These General Conditions have been prepared for use with the Suggested Forms of Agreement Between County and Contractor/Bidder (EJCDC C-520 or C-525, 2007 Editions). Their provisions are interrelated and a change in one may necessitate a change in the other. Comments concerning their usage are contained in the Narrative Guide to the EJCDC Construction Documents (EJCDC C-001, 2007 Edition). For guidance in the preparation of Supplementary Conditions, see Guide to the Preparation of Supplementary Conditions (EJCDC C-800, 2007 Edition).

STANDARD GENERAL CONDITIONS

OF THE CONSTRUCTION CONTRACT

Prepared by

ENGINEERS JOINT CONTRACT DOCUMENTS COMMITTEE

and

Issued and Published Jointly by









AMERICAN COUNCIL OF ENGINEERING COMPANIES

ASSOCIATED GENERAL CONTRACTOR/BIDDERS OF AMERICA

AMERICAN SOCIETY OF CIVIL ENGINEERS

PROFESSIONAL ENGINEERS IN PRIVATE PRACTICE

A Practice Division of the

NATIONAL SOCIETY OF PROFESSIONAL ENGINEERS

Endorsed by

6.12 Record Documents

A. Contractor/Bidder shall maintain in a safe place at the Site one record copy of all Drawings, Specifications, Addenda, Change Orders, Work Change Directives, Field Orders, and written interpretations and clarifications in good order and annotated to show changes made during construction. These record documents together with all approved Samples and a counterpart of all approved Shop Drawings will be available to Engineer for reference. Upon completion of the Work, these record documents, Samples, and Shop Drawings will be delivered to Engineer for County. <u>Annotations of record documents shall be legible, precise,</u> and complete as determined by Engineer of Record and the County. (see SC-6.12.A)

6.13 Safety and Protection

- A. Contractor/Bidder shall be solely responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the Work. Such responsibility does not relieve SubContractors of their responsibility for the safety of persons or property in the performance of their work, nor for compliance with applicable safety Laws and Regulations. Contractor/Bidder shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury or loss to:
 - 1. all persons on the Site or who may be affected by the Work;
 - 2. all the Work and materials and equipment to be incorporated therein, whether in storage on or off the Site; and
 - 3. other property at the Site or adjacent thereto, including trees, shrubs, lawns, walks, pavements, roadways, structures, utilities, and Underground Facilities not designated for removal, relocation, or replacement in the course of construction.
- B. Contractor/Bidder shall comply with all applicable Laws and Regulations relating to the safety of persons or property, or to the protection of persons or property from damage, injury, or loss; and shall erect and maintain all necessary safeguards for such safety and protection. Contractor/Bidder shall notify Countys of adjacent property and of Underground Facilities and other utility Countys when prosecution of the Work may affect them, and shall cooperate with them in the protection, removal, relocation, and replacement of their property.
- C. Contractor/Bidder shall comply with the applicable requirements of County's safety programs, if any. The Supplementary Conditions identify any County's safety programs that are applicable to the Work.
- D. Contractor/Bidder shall inform County and Engineer of the specific requirements of Contractor/Bidder's safety program with which County's and Engineer's employees and representatives must comply while at the Site.
- E. All damage, injury, or loss to any property referred to in Paragraph 6.13.A.2 or 6.13.A.3 caused, directly or indirectly, in whole or in part, by Contractor/Bidder, any SubContractor, Supplier, or any other individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, shall be remedied by Contractor/Bidder (except damage or loss attributable to the fault of Drawings

or Specifications or to the acts or omissions of County or Engineer or anyone employed by any of them, or anyone for whose acts any of them may be liable, and not attributable, directly or indirectly, in whole or in part, to the fault or negligence of Contractor/Bidder or any SubContractor, Supplier, or other individual or entity directly or indirectly employed by any of them).

- F. Contractor/Bidder's duties and responsibilities for safety and for protection of the Work shall continue until such time as all the Work is completed and Engineer has issued a notice to County and Contractor/Bidder in accordance with Paragraph 14.07.B that the Work is acceptable (except as otherwise expressly provided in connection with Substantial Completion).
- G. Contractor/Bidder shall be responsible at all times for precautions to achieve the protection of all persons, including employees and property. Contractor/Bidder shall make special effort to detect hazardous conditions and shall take prompt action where necessary to avoid accident, injury, or property damage. OSHA and all other applicable safety laws and ordinances shall be followed as well as American National Standards Institute Safety Standards. All accidents, injuries, claims, or potential claims shall be reported promptly to County. (see SC-6.13.G)

6.14 Safety Representative

- A. Contractor/Bidder shall designate a qualified and experienced safety representative at the Site whose duties and responsibilities shall be the prevention of accidents and the maintaining and supervising of safety precautions and programs.
- 6.15 Hazard Communication Programs
 - A. Contractor/Bidder shall be responsible for coordinating any exchange of material safety data sheets or other hazard communication information required to be made available to or exchanged between or among employers at the Site in accordance with Laws or Regulations.

6.16 Emergencies

A. In emergencies affecting the safety or protection of persons or the Work or property at the Site or adjacent thereto, Contractor/Bidder is obligated to act to prevent threatened damage, injury, or loss. Contractor/Bidder shall give Engineer prompt written notice if Contractor/Bidder believes that any significant changes in the Work or variations from the Contract Documents have been caused thereby or are required as a result thereof. If Engineer determines that a change in the Contract Documents is required because of the action taken by Contractor/Bidder in response to such an emergency, a Work Change Directive or Change Order will be issued.

6.17 Shop Drawings and Samples

A. Contractor/Bidder shall submit Shop Drawings and Samples to Engineer for review and approval in accordance with the accepted Schedule of Submittals (as required by Paragraph 2.07). Each submittal will be identified as Engineer may require.

- 1. Shop Drawings:
 - a. Submit number of copies specified in the General Requirements.
 - b. Data shown on the Shop Drawings will be complete with respect to quantities, dimensions, specified performance and design criteria, materials, and similar data to show Engineer the services, materials, and equipment Contractor/Bidder proposes to provide and to enable Engineer to review the information for the limited purposes required by Paragraph 6.17.D.
- 2. Samples:
 - a. Submit number of Samples specified in the Specifications.
 - b. Clearly identify each Sample as to material, Supplier, pertinent data such as catalog numbers, the use for which intended and other data as Engineer may require to enable Engineer to review the submittal for the limited purposes required by Paragraph 6.17.D.
- B. Where a Shop Drawing or Sample is required by the Contract Documents or the Schedule of Submittals, any related Work performed prior to Engineer's review and approval of the pertinent submittal will be at the sole expense and responsibility of Contractor/Bidder.
- C. Submittal Procedures:
 - 1. Before submitting each Shop Drawing or Sample, Contractor/Bidder shall have:
 - a. reviewed and coordinated each Shop Drawing or Sample with other Shop Drawings and Samples and with the requirements of the Work and the Contract Documents;
 - b. determined and verified all field measurements, quantities, dimensions, specified performance and design criteria, installation requirements, materials, catalog numbers, and similar information with respect thereto;
 - c. determined and verified the suitability of all materials offered with respect to the indicated application, fabrication, shipping, handling, storage, assembly, and installation pertaining to the performance of the Work; and
 - d. determined and verified all information relative to Contractor/Bidder's responsibilities for means, methods, techniques, sequences, and procedures of construction, and safety precautions and programs incident thereto.
 - 2. Each submittal shall bear a stamp or specific written certification that Contractor/Bidder has satisfied Contractor/Bidder's obligations under the Contract Documents with respect to Contractor/Bidder's review and approval of that submittal.
 - 3. With each submittal, Contractor/Bidder shall give Engineer specific written notice of any variations that the Shop Drawing or Sample may have from the requirements of the Contract Documents. This notice shall be both a written communication separate from the Shop Drawings or Sample submittal; and, in addition, by a specific notation made

on each Shop Drawing or Sample submitted to Engineer for review and approval of each such variation.

- D. Engineer's Review:
 - 1. Engineer will provide timely review of Shop Drawings and Samples in accordance with the Schedule of Submittals acceptable to Engineer. Engineer's review and approval will be only to determine if the items covered by the submittals will, after installation or incorporation in the Work, conform to the information given in the Contract Documents and be compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents.
 - 2. Engineer's review and approval will not extend to means, methods, techniques, sequences, or procedures of construction (except where a particular means, method, technique, sequence, or procedure of construction is specifically and expressly called for by the Contract Documents) or to safety precautions or programs incident thereto. The review and approval of a separate item as such will not indicate approval of the assembly in which the item functions.
 - 3. Engineer's review and approval shall not relieve Contractor/Bidder from responsibility for any variation from the requirements of the Contract Documents unless Contractor/Bidder has complied with the requirements of Paragraph 6.17.C.3 and Engineer has given written approval of each such variation by specific written notation thereof incorporated in or accompanying the Shop Drawing or Sample. Engineer's review and approval shall not relieve Contractor/Bidder from responsibility for complying with the requirements of Paragraph 6.17.C.1.
- E. Resubmittal Procedures:
 - 1. Contractor/Bidder shall make corrections required by Engineer and shall return the required number of corrected copies of Shop Drawings and submit, as required, new Samples for review and approval. Contractor/Bidder shall direct specific attention in writing to revisions other than the corrections called for by Engineer on previous submittals.
 - Contractor/Bidder shall reimburse County for the charges of the County and the County's Consultants for costs generated as a result of more than two submittals of any one Shop Drawing or Sample being required for evaluation due to rejection for noncompliance of the original submittal or lace of information required by the Contract Documents. County's reimbursement for the charges shall be a deduction from Contractor/Bidder's Partial Payment(s). (see SC-6.17.E.2)

6.18 Continuing the Work

A. Contractor/Bidder shall carry on the Work and adhere to the Progress Schedule during all disputes or disagreements with County. No Work shall be delayed or postponed pending resolution of any disputes or disagreements, except as permitted by Paragraph 15.04 or as County and Contractor/Bidder may otherwise agree in writing.

6.19 Contractor/Bidder's General Warranty and Guarantee

- A. Contractor/Bidder warrants and guarantees to County that all Work will be in accordance with the Contract Documents and will not be defective. Engineer and its officers, directors, members, partners, employees, agents, consultants, and SubContractors shall be entitled to rely on representation of Contractor/Bidder's warranty and guarantee.
- B. Contractor/Bidder's warranty and guarantee hereunder excludes defects or damage caused by:
 - 1. abuse, modification, or improper maintenance or operation by persons other than Contractor/Bidder, SubContractors, Suppliers, or any other individual or entity for whom Contractor/Bidder is responsible; or
 - 2. normal wear and tear under normal usage.
- C. Contractor/Bidder's obligation to perform and complete the Work in accordance with the Contract Documents shall be absolute. None of the following will constitute an acceptance of Work that is not in accordance with the Contract Documents or a release of Contractor/Bidder's obligation to perform the Work in accordance with the Contract Documents:
 - 1. observations by Engineer;
 - 2. recommendation by Engineer or payment by County of any progress or final payment;
 - 3. the issuance of a certificate of Substantial Completion by Engineer or any payment related thereto by County;
 - 4. use or occupancy of the Work or any part thereof by County;
 - 5. any review and approval of a Shop Drawing or Sample submittal or the issuance of a notice of acceptability by Engineer;
 - 6. any inspection, test, or approval by others; or
 - 7. any correction of defective Work by County.

6.20 Indemnification

A. To the fullest extent permitted by Laws and Regulations, Contractor/Bidder shall indemnify and hold harmless County and Engineer, and the officers, directors, members, partners, employees, agents, consultants and SubContractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to the performance of the Work, provided that any such claim, cost, loss, or damage is attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom but only to the extent caused by any negligent act or omission of Contractor/Bidder, any SubContractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work or anyone for whose acts any of them may be liable . (see SC-6.20.A)

- 1. Five percent of the Contract Price is given as consideration for this indemnification. (see SC-6.20.A.1)
- B. In any and all claims against County or Engineer or any of their officers, directors, members, partners, employees, agents, consultants, or SubContractors by any employee (or the survivor or personal representative of such employee) of Contractor/Bidder, any SubContractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, the indemnification obligation under Paragraph 6.20.A shall not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Contractor/Bidder or any such SubContractor, Supplier, or other individual or entity under workers' compensation acts, disability benefit acts, or other employee benefit acts.
- C. The indemnification obligations of Contractor/Bidder under Paragraph 6.20.A shall not extend to the liability of Engineer and Engineer's officers, directors, members, partners, employees, agents, consultants and SubContractors arising out of:
 - 1. the preparation or approval of, or the failure to prepare or approve maps, Drawings, opinions, reports, surveys, Change Orders, designs, or Specifications; or
 - 2. giving directions or instructions, or failing to give them, if that is the primary cause of the injury or damage.
- D. <u>Neither Contractor/Bidder nor County shall sell, transfer, assign, or otherwise dispose of the</u> <u>contract or any portion thereof, or any right, title, or interest therein, or any obligations</u> <u>thereunder</u>, without written consent of the other party. (see SC-6.20.D)
- 6.21 Delegation of Professional Design Services
 - A. Contractor/Bidder will not be required to provide professional design services unless such services are specifically required by the Contract Documents for a portion of the Work or unless such services are required to carry out Contractor/Bidder's responsibilities for construction means, methods, techniques, sequences and procedures. Contractor/Bidder shall not be required to provide professional services in violation of applicable law.
 - B. If professional design services or certifications by a design professional related to systems, materials or equipment are specifically required of Contractor/Bidder by the Contract Documents, County and Engineer will specify all performance and design criteria that such services must satisfy. Contractor/Bidder shall cause such services or certifications to be provided by a properly licensed professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to Engineer.

- C. County and Engineer shall be entitled to rely upon the adequacy, accuracy and completeness of the services, certifications or approvals performed by such design professionals, provided County and Engineer have specified to Contractor/Bidder all performance and design criteria that such services must satisfy.
- D. Pursuant to this Paragraph 6.21, Engineer's review and approval of design calculations and design drawings will be only for the limited purpose of checking for conformance with performance and design criteria given and the design concept expressed in the Contract Documents. Engineer's review and approval of Shop Drawings and other submittals (except design calculations and design drawings) will be only for the purpose stated in Paragraph 6.17.D.1.
- E. Contractor/Bidder shall not be responsible for the adequacy of the performance or design criteria required by the Contract Documents.

ARTICLE 7 – OTHER WORK AT THE SITE

- 7.01 Related Work at Site
 - A. County may perform other work related to the Project at the Site with County's employees, or through other direct contracts therefor, or have other work performed by utility Countys. If such other work is not noted in the Contract Documents, then:
 - 1. written notice thereof will be given to Contractor/Bidder prior to starting any such other work; and
 - 2. if County and Contractor/Bidder are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in the Contract Price or Contract Times that should be allowed as a result of such other work, a Claim may be made therefor as provided in Paragraph 10.05.
 - B. Contractor/Bidder shall afford each other Contractor/Bidder who is a party to such a direct contract, each utility County, and County, if County is performing other work with County's employees, proper and safe access to the Site, provide a reasonable opportunity for the introduction and storage of materials and equipment and the execution of such other work, and properly coordinate the Work with theirs. Contractor/Bidder shall do all cutting, fitting, and patching of the Work that may be required to properly connect or otherwise make its several parts come together and properly integrate with such other work. Contractor/Bidder shall not endanger any work of others by cutting, excavating, or otherwise altering such work; provided, however, that Contractor/Bidder may cut or alter others' work with the written consent of Engineer and the others whose work will be affected. The duties and responsibilities of Contractor/Bidder under this Paragraph are for the benefit of such utility Countys and other Contractor/Bidder in said direct contracts between County and such utility Countys and other Contractor/Bidder in said direct contracts between County and such utility Countys and other Contractor/Bidders.
 - C. If the proper execution or results of any part of Contractor/Bidder's Work depends upon work performed by others under this Article 7, Contractor/Bidder shall inspect such other work and promptly report to Engineer in writing any delays, defects, or deficiencies in such

other work that render it unavailable or unsuitable for the proper execution and results of Contractor/Bidder's Work. Contractor/Bidder's failure to so report will constitute an acceptance of such other work as fit and proper for integration with Contractor/Bidder's Work except for latent defects and deficiencies in such other work.

7.02 Coordination

- A. If County intends to contract with others for the performance of other work on the Project at the Site, the following will be set forth in Supplementary Conditions:
 - 1. the individual or entity who will have authority and responsibility for coordination of the activities among the various Contractor/Bidders will be identified;
 - 2. the specific matters to be covered by such authority and responsibility will be itemized; and
 - 3. the extent of such authority and responsibilities will be provided.
- B. Unless otherwise provided in the Supplementary Conditions, County shall have sole authority and responsibility for such coordination.
- 7.03 Legal Relationships
 - A. Paragraphs 7.01.A and 7.02 are not applicable for utilities not under the control of County.
 - B. Each other direct contract of County under Paragraph 7.01.A shall provide that the other Contractor/Bidder is liable to County and Contractor/Bidder for the reasonable direct delay and disruption costs incurred by Contractor/Bidder as a result of the other Contractor/Bidder's wrongful actions or inactions.
 - C. Contractor/Bidder shall be liable to County and any other Contractor/Bidder under direct contract to County for the reasonable direct delay and disruption costs incurred by such other Contractor/Bidder as a result of Contractor/Bidder's wrongful action or inactions.

ARTICLE 8 – COUNTY'S RESPONSIBILITIES

- 8.01 Communications to Contractor/Bidder
 - A. Except as otherwise provided in these General Conditions, County shall issue all communications to Contractor/Bidder through Engineer.
- 8.02 Replacement of Engineer
 - A. In case of termination of the employment of Engineer, County shall appoint an engineer to whom Contractor/Bidder makes no reasonable objection, whose status under the Contract Documents shall be that of the former Engineer. (see SC-8.02)
- 8.03 Furnish Data
 - A. County shall promptly furnish the data required of County under the Contract Documents.

8.04 Pay When Due

A. County shall make payments to Contractor/Bidder when they are due as provided in Paragraphs 14.02.C and 14.07.C.

8.05 Lands and Easements; Reports and Tests

A. County's duties with respect to providing lands and easements and providing engineering surveys to establish reference points are set forth in Paragraphs 4.01 and 4.05. Paragraph 4.02 refers to County's identifying and making available to Contractor/Bidder copies of reports of explorations and tests of subsurface conditions and drawings of physical conditions relating to existing surface or subsurface structures at the Site.

8.06 Insurance

A. County's responsibilities, if any, with respect to purchasing and maintaining liability and property insurance are set forth in Article 5.

8.07 Change Orders

- A. County is obligated to execute Change Orders as indicated in Paragraph 10.03.
- 8.08 Inspections, Tests, and Approvals
 - A. County's responsibility with respect to certain inspections, tests, and approvals is set forth in Paragraph 13.03.B.
- 8.09 Limitations on County's Responsibilities
 - A. The County shall not supervise, direct, or have control or authority over, nor be responsible for, Contractor/Bidder's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor/Bidder to comply with Laws and Regulations applicable to the performance of the Work. County will not be responsible for Contractor/Bidder's failure to perform the Work in accordance with the Contract Documents.
- 8.10 Undisclosed Hazardous Environmental Condition
 - A. County's responsibility in respect to an undisclosed Hazardous Environmental Condition is set forth in Paragraph 4.06.
- 8.11 Evidence of Financial Arrangements
 - A. Upon request of Contractor/Bidder, County shall furnish Contractor/Bidder reasonable evidence that financial arrangements have been made to satisfy County's obligations under the Contract Documents.

8.12 Compliance with Safety Program

A. While at the Site, County's employees and representatives shall comply with the specific applicable requirements of Contractor/Bidder's safety programs of which County has been informed pursuant to Paragraph 6.13.D.

ARTICLE 9 – ENGINEER'S STATUS DURING CONSTRUCTION

9.01 County's Representative

A. Engineer will be County's representative during the construction period. The duties and responsibilities and the limitations of authority of Engineer as County's representative during construction are set forth in the Contract Documents.

9.02 Visits to Site

- A. Engineer will make visits to the Site at intervals appropriate to the various stages of construction as Engineer deems necessary in order to observe as an experienced and qualified design professional the progress that has been made and the quality of the various aspects of Contractor/Bidder's executed Work. Based on information obtained during such visits and observations, Engineer, for the benefit of County, will determine, in general, if the Work is proceeding in accordance with the Contract Documents. Engineer will not be required to make exhaustive or continuous inspections on the Site to check the quality or quantity of the Work. Engineer's efforts will be directed toward providing for County a greater degree of confidence that the completed Work will conform generally to the Contract Documents. On the basis of such visits and observations, Engineer will not be required of the progress of the Work and will endeavor to guard County against defective Work.
- B. Engineer's visits and observations are subject to all the limitations on Engineer's authority and responsibility set forth in Paragraph 9.09. Particularly, but without limitation, during or as a result of Engineer's visits or observations of Contractor/Bidder's Work, Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor/Bidder's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor/Bidder to comply with Laws and Regulations applicable to the performance of the Work.

9.03 Project Representative

A. If County and Engineer agree, Engineer will furnish a Resident Project Representative to assist Engineer in providing more extensive observation of the Work. The authority and responsibilities of any such Resident Project Representative and assistants will be as provided in the Supplementary Conditions, and limitations on the responsibilities thereof will be as provided in Paragraph 9.09. If County designates another representative or agent to represent County at the Site who is not Engineer's consultant, agent or employee, the responsibilities and authority and limitations thereon of such other individual or entity will be as provided in the Supplementary Conditions.

9.04 Authorized Variations in Work

A. Engineer may authorize minor variations in the Work from the requirements of the Contract Documents which do not involve an adjustment in the Contract Price or the Contract Times and are compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents. These may be accomplished by a Field Order and will be binding on County and also on Contractor/Bidder, who shall perform the Work involved promptly. If County or Contractor/Bidder believes that a Field Order justifies an adjustment in the Contract Price or Contract Times, or both, and the parties are unable to agree on entitlement to or on the amount or extent, if any, of any such adjustment, a Claim may be made therefor as provided in Paragraph 10.05.

9.05 Rejecting Defective Work

- A. Engineer will have authority to reject Work which Engineer believes to be defective, or that Engineer believes will not produce a completed Project that conforms to the Contract Documents or that will prejudice the integrity of the design concept of the completed Project as a functioning whole as indicated by the Contract Documents. Engineer will also have authority to require special inspection or testing of the Work as provided in Paragraph 13.04, whether or not the Work is fabricated, installed, or completed.
- B. Contractor/Bidder shall reimburse the County for the charges of Engineer and Engineer's Consultants for any additional field observations, engineering analysis, correspondence, meetings, or other work due to non-complying or defective construction, materials, or equipment performed or furnished by the Contractor/Bidder, SubContractors, or Suppliers. County's reimbursement for the charges shall be a deduction from the Contractor/Bidder's Partial Payment(s). (see SC-9.05.B)
- 9.06 Shop Drawings, Change Orders and Payments
 - A. In connection with Engineer's authority, and limitations thereof, as to Shop Drawings and Samples, see Paragraph 6.17.
 - B. In connection with Engineer's authority, and limitations thereof, as to design calculations and design drawings submitted in response to a delegation of professional design services, if any, see Paragraph 6.21.
 - C. In connection with Engineer's authority as to Change Orders, see Articles 10, 11, and 12.
 - D. In connection with Engineer's authority as to Applications for Payment, see Article 14.

9.07 Determinations for Unit Price Work

A. Engineer will determine the actual quantities and classifications of Unit Price Work performed by Contractor/Bidder. Engineer will review with Contractor/Bidder the Engineer's preliminary determinations on such matters before rendering a written decision thereon (by recommendation of an Application for Payment or otherwise). Engineer's written decision thereon will be final and binding (except as modified by Engineer to reflect changed factual conditions or more accurate data) upon County and Contractor/Bidder, subject to the provisions of Paragraph 10.05.

9.08 Decisions on Requirements of Contract Documents and Acceptability of Work

- A. Engineer will be the initial interpreter of the requirements of the Contract Documents and judge of the acceptability of the Work thereunder. All matters in question and other matters between County and Contractor/Bidder arising prior to the date final payment is due relating to the acceptability of the Work, and the interpretation of the requirements of the Contract Documents pertaining to the performance of the Work, will be referred initially to Engineer in writing within 30 days of the event giving rise to the question.
- B. Engineer will, with reasonable promptness, render a written decision on the issue referred. If County or Contractor/Bidder believes that any such decision entitles them to an adjustment in the Contract Price or Contract Times or both, a Claim may be made under Paragraph 10.05. The date of Engineer's decision shall be the date of the event giving rise to the issues referenced for the purposes of Paragraph 10.05.B.
- C. Engineer's written decision on the issue referred will be final and binding on County and Contractor/Bidder, subject to the provisions of Paragraph 10.05.
- D. When functioning as interpreter and judge under this Paragraph 9.08, Engineer will not show partiality to County or Contractor/Bidder and will not be liable in connection with any interpretation or decision rendered in good faith in such capacity.

9.09 Limitations on Engineer's Authority and Responsibilities

- A. Neither Engineer's authority or responsibility under this Article 9 or under any other provision of the Contract Documents nor any decision made by Engineer in good faith either to exercise or not exercise such authority or responsibility or the undertaking, exercise, or performance of any authority or responsibility by Engineer shall create, impose, or give rise to any duty in contract, tort, or otherwise owed by Engineer to Contractor/Bidder, any SubContractor, any Supplier, any other individual or entity, or to any surety for or employee or agent of any of them.
- B. Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor/Bidder's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor/Bidder to comply with Laws and Regulations applicable to the performance of the Work. Engineer will not be responsible for Contractor/Bidder's failure to perform the Work in accordance with the Contract Documents.
- C. Engineer will not be responsible for the acts or omissions of Contractor/Bidder or of any SubContractor, any Supplier, or of any other individual or entity performing any of the Work.
- D. Engineer's review of the final Application for Payment and accompanying documentation and all maintenance and operating instructions, schedules, guarantees, bonds, certificates of inspection, tests and approvals, and other documentation required to be delivered by

Paragraph 14.07.A will only be to determine generally that their content complies with the requirements of, and in the case of certificates of inspections, tests, and approvals that the results certified indicate compliance with, the Contract Documents.

E. The limitations upon authority and responsibility set forth in this Paragraph 9.09 shall also apply to the Resident Project Representative, if any, and assistants, if any.

9.10 Compliance with Safety Program

A. While at the Site, Engineer's employees and representatives shall comply with the specific applicable requirements of Contractor/Bidder's safety programs of which Engineer has been informed pursuant to Paragraph 6.13.D.

ARTICLE 10 - CHANGES IN THE WORK; CLAIMS

- 10.01 Authorized Changes in the Work
 - A. Without invalidating the Contract and without notice to any surety, County may, at any time or from time to time, order additions, deletions, or revisions in the Work by a Change Order, or a Work Change Directive. Upon receipt of any such document, Contractor/Bidder shall promptly proceed with the Work involved which will be performed under the applicable conditions of the Contract Documents (except as otherwise specifically provided).
 - B. If County and Contractor/Bidder are unable to agree on entitlement to, or on the amount or extent, if any, of an adjustment in the Contract Price or Contract Times, or both, that should be allowed as a result of a Work Change Directive, a Claim may be made therefor as provided in Paragraph 10.05.
- 10.02 Unauthorized Changes in the Work
 - A. Contractor/Bidder shall not be entitled to an increase in the Contract Price or an extension of the Contract Times with respect to any work performed that is not required by the Contract Documents as amended, modified, or supplemented as provided in Paragraph 3.04, except in the case of an emergency as provided in Paragraph 6.16 or in the case of uncovering Work as provided in Paragraph 13.04.D.
- 10.03 Execution of Change Orders
 - A. County and Contractor/Bidder shall execute appropriate Change Orders recommended by Engineer covering:
 - changes in the Work which are: (i) ordered by County pursuant to Paragraph 10.01.A, (ii) required because of acceptance of defective Work under Paragraph 13.08.A or County's correction of defective Work under Paragraph 13.09, or (iii) agreed to by the parties;
 - 2. changes in the Contract Price or Contract Times which are agreed to by the parties, including any undisputed sum or amount of time for Work actually performed in accordance with a Work Change Directive; and

3. changes in the Contract Price or Contract Times which embody the substance of any written decision rendered by Engineer pursuant to Paragraph 10.05; provided that, in lieu of executing any such Change Order, an appeal may be taken from any such decision in accordance with the provisions of the Contract Documents and applicable Laws and Regulations, but during any such appeal, Contractor/Bidder shall carry on the Work and adhere to the Progress Schedule as provided in Paragraph 6.18.A.

10.04 Notification to Surety

A. If the provisions of any bond require notice to be given to a surety of any change affecting the general scope of the Work or the provisions of the Contract Documents (including, but not limited to, Contract Price or Contract Times), the giving of any such notice will be Contractor/Bidder's responsibility. The amount of each applicable bond will be adjusted to reflect the effect of any such change.

10.05 Claims

- A. Engineer's Decision Required: All Claims, except those waived pursuant to Paragraph 14.09, shall be referred to the Engineer for decision. A decision by Engineer shall be required as a condition precedent to any exercise by County or Contractor/Bidder of any rights or remedies either may otherwise have under the Contract Documents or by Laws and Regulations in respect of such Claims.
- B. Notice: Written notice stating the general nature of each Claim shall be delivered by the claimant to Engineer and the other party to the Contract promptly (but in no event later than 30 15 days) after the start of the event giving rise thereto. The responsibility to substantiate a Claim shall rest with the party making the Claim. Notice of the amount or extent of the Claim, with supporting data shall be delivered to the Engineer and the other party to the Contract within 60 days after the start of such event (unless Engineer allows additional time for claimant to submit additional or more accurate data in support of such Claim). A Claim for an adjustment in Contract Price shall be prepared in accordance with the provisions of Paragraph 12.01.B. A Claim for an adjustment in Contract Times shall be accompanied by claimant's written statement that the adjustment claimed is the entire adjustment to which the claimant believes it is entitled as a result of said event. The opposing party shall submit any response to Engineer and the claimant within 30 days after receipt of the claimant's last submittal (unless Engineer allows additional time). (see SC-10.05.B)
- C. *Engineer's Action*: Engineer will review each Claim and, within 30 days after receipt of the last submittal of the claimant or the last submittal of the opposing party, if any, take one of the following actions in writing:
 - 1. deny the Claim in whole or in part;
 - 2. approve the Claim; or
 - 3. notify the parties that the Engineer is unable to resolve the Claim if, in the Engineer's sole discretion, it would be inappropriate for the Engineer to do so. For purposes of further resolution of the Claim, such notice shall be deemed a denial.

- D. In the event that Engineer does not take action on a Claim within said 30 days, the Claim shall be deemed denied.
- E. Engineer's written action under Paragraph 10.05.C or denial pursuant to Paragraphs 10.05.C.3 or 10.05.D will be final and binding upon County and Contractor/Bidder, unless County or Contractor/Bidder invoke the dispute resolution procedure set forth in Article 16 within 30 days of such action or denial.
- F. No Claim for an adjustment in Contract Price or Contract Times will be valid if not submitted in accordance with this Paragraph 10.05.

ARTICLE 11 - COST OF THE WORK; ALLOWANCES; UNIT PRICE WORK

- 11.01 Cost of the Work
 - A. *Costs Included:* The term Cost of the Work means the sum of all costs, except those excluded in Paragraph 11.01.B, necessarily incurred and paid by Contractor/Bidder in the proper performance of the Work. When the value of any Work covered by a Change Order or when a Claim for an adjustment in Contract Price is determined on the basis of Cost of the Work, the costs to be reimbursed to Contractor/Bidder will be only those additional or incremental costs required because of the change in the Work or because of the event giving rise to the Claim. Except as otherwise may be agreed to in writing by County, such costs shall be in amounts no higher than those prevailing in the locality of the Project, shall not include any of the costs itemized in Paragraph 11.01.B, and shall include only the following items:
 - 1. Payroll costs for employees in the direct employ of Contractor/Bidder in the performance of the Work under schedules of job classifications agreed upon by County and Contractor/Bidder. Such employees shall include, without limitation, superintendents, foremen, and other personnel employed full time on the Work. Payroll costs for employees not employed full time on the Work shall be apportioned on the basis of their time spent on the Work. Payroll costs shall include, but not be limited to, salaries and wages plus the cost of fringe benefits, which shall include social security contributions, unemployment, excise, and payroll taxes, workers' compensation, health and retirement benefits, bonuses, sick leave, vacation and holiday pay applicable thereto. The expenses of performing Work outside of regular working hours, on Saturday, Sunday, or legal holidays, shall be included in the above to the extent authorized by County.
 - 2. Cost of all materials and equipment furnished and incorporated in the Work, including costs of transportation and storage thereof, and Suppliers' field services required in connection therewith. All cash discounts shall accrue to Contractor/Bidder unless County deposits funds with Contractor/Bidder with which to make payments, in which case the cash discounts shall accrue to County. All trade discounts, rebates and refunds and returns from sale of surplus materials and equipment shall accrue to County, and Contractor/Bidder shall make provisions so that they may be obtained.
 - 3. Payments made by Contractor/Bidder to SubContractors for Work performed by SubContractors. If required by County, Contractor/Bidder shall obtain competitive bids from SubContractors acceptable to County and Contractor/Bidder and shall deliver such

bids to County, who will then determine, with the advice of Engineer, which bids, if any, will be acceptable. If any subcontract provides that the SubContractor is to be paid on the basis of Cost of the Work plus a fee, the SubContractor's Cost of the Work and fee shall be determined in the same manner as Contractor/Bidder's Cost of the Work and fee as provided in this Paragraph 11.01.

- 4. Costs of special consultants (including but not limited to engineers, architects, testing laboratories, surveyors, attorneys, and accountants) employed for services specifically related to the Work.
- 5. Supplemental costs including the following:
 - a. The proportion of necessary transportation, travel, and subsistence expenses of Contractor/Bidder's employees incurred in discharge of duties connected with the Work.
 - b. Cost, including transportation and maintenance, of all materials, supplies, equipment, machinery, appliances, office, and temporary facilities at the Site, and hand tools not owned by the workers, which are consumed in the performance of the Work, and cost, less market value, of such items used but not consumed which remain the property of Contractor/Bidder.
 - c. Rentals of all construction equipment and machinery, and the parts thereof whether rented from Contractor/Bidder or others in accordance with rental agreements approved by County with the advice of Engineer, and the costs of transportation, loading, unloading, assembly, dismantling, and removal thereof. All such costs shall be in accordance with the terms of said rental agreements. The rental of any such equipment, machinery, or parts shall cease when the use thereof is no longer necessary for the Work. In no case shall rates exceed those published by the current edition of Data Quest Incorporated titled, Rental Rate Blue Book for Construction Equipment, and other procedures established by Florida Department of Transportation. (see SC-11.01.A.5.c)
 - d. Sales, consumer, use, and other similar taxes related to the Work, and for which Contractor/Bidder is liable, as imposed by Laws and Regulations.
 - e. Deposits lost for causes other than negligence of Contractor/Bidder, any SubContractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, and royalty payments and fees for permits and licenses.
 - f. Losses and damages (and related expenses) caused by damage to the Work, not compensated by insurance or otherwise, sustained by Contractor/Bidder in connection with the performance of the Work (except losses and damages within the deductible amounts of property insurance established in accordance with Paragraph 5.06.D), provided such losses and damages have resulted from causes other than the negligence of Contractor/Bidder, any SubContractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable. Such losses shall include settlements made with the written consent and approval of County. No

such losses, damages, and expenses shall be included in the Cost of the Work for the purpose of determining Contractor/Bidder's fee. (see SC-11.01.A.5.f)

- g. The cost of utilities, fuel, and sanitary facilities at the Site.
- h. Minor expenses such as telegrams, long distance telephone calls, telephone service at the Site, express and courier services, and similar petty cash items in connection with the Work.
- i. The costs of premiums for all bonds and insurance Contractor/Bidder is required by the Contract Documents to purchase and maintain.
- j. <u>The cost of specific consideration for the indemnifications set forth in paragraph 6.20. (see SC-11.01.A.5.j)</u>
- k. <u>The cost of compliance with current local, state and federal safety regulations. (see</u> <u>SC-11.01.A.5.k)</u>
- B. Costs Excluded: The term Cost of the Work shall not include any of the following items:
 - 1. Payroll costs and other compensation of Contractor/Bidder's officers, executives, principals (of partnerships and sole proprietorships), general managers, safety managers, engineers, architects, estimators, attorneys, auditors, accountants, purchasing and contracting agents, expediters, timekeepers, clerks, and other personnel employed by Contractor/Bidder, whether at the Site or in Contractor/Bidder's principal or branch office for general administration of the Work and not specifically included in the agreed upon schedule of job classifications referred to in Paragraph 11.01.A.1 or specifically covered by Paragraph 11.01.A.4, all of which are to be considered administrative costs covered by the Contractor/Bidder's fee.
 - 2. Expenses of Contractor/Bidder's principal and branch offices other than Contractor/Bidder's office at the Site.
 - 3. Any part of Contractor/Bidder's capital expenses, including interest on Contractor/Bidder's capital employed for the Work and charges against Contractor/Bidder for delinquent payments.
 - 4. Costs due to the negligence of Contractor/Bidder, any SubContractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, including but not limited to, the correction of defective Work, disposal of materials or equipment wrongly supplied, and making good any damage to property.
 - 5. Other overhead or general expense costs of any kind and the costs of any item not specifically and expressly included in Paragraphs 11.01.A.
- C. Contractor/Bidder's Fee: When all the Work is performed on the basis of cost-plus, Contractor/Bidder's fee shall be determined as set forth in the Agreement. When the value of any Work covered by a Change Order or when a Claim for an adjustment in Contract

Price is determined on the basis of Cost of the Work, Contractor/Bidder's fee shall be determined as set forth in Paragraph 12.01.C.

D. *Documentation:* Whenever the Cost of the Work for any purpose is to be determined pursuant to Paragraphs 11.01.A and 11.01.B, Contractor/Bidder will establish and maintain records thereof in accordance with generally accepted accounting practices and submit in a form acceptable to Engineer an itemized cost breakdown together with supporting data.

11.02 Allowances

- A. It is understood that Contractor/Bidder has included in the Contract Price all allowances so named in the Contract Documents and shall cause the Work so covered to be performed for such sums and by such persons or entities as may be acceptable to County and Engineer.
- B. Cash Allowances:
 - 1. Contractor/Bidder agrees that:
 - a. the cash allowances include the cost to Contractor/Bidder (less any applicable trade discounts) of materials and equipment required by the allowances to be delivered at the Site, and all applicable taxes; and
 - b. Contractor/Bidder's costs for unloading and handling on the Site, labor, installation, overhead, profit, and other expenses contemplated for the cash allowances have been included in the Contract Price and not in the allowances, and no demand for additional payment on account of any of the foregoing will be valid.
- C. Contingency Allowance:
 - 1. Contractor/Bidder agrees that a contingency allowance, if any, is for the sole use of County to cover unanticipated costs.
- D. Prior to final payment, an appropriate Change Order will be issued as recommended by Engineer to reflect actual amounts due Contractor/Bidder on account of Work covered by allowances, and the Contract Price shall be correspondingly adjusted.

11.03 Unit Price Work

- A. Where the Contract Documents provide that all or part of the Work is to be Unit Price Work, initially the Contract Price will be deemed to include for all Unit Price Work an amount equal to the sum of the unit price for each separately identified item of Unit Price Work times the estimated quantity of each item as indicated in the Agreement.
- B. The estimated quantities of items of Unit Price Work are not guaranteed and are solely for the purpose of comparison of Bids and determining an initial Contract Price. Determinations of the actual quantities and classifications of Unit Price Work performed by Contractor/Bidder will be made by Engineer subject to the provisions of Paragraph 9.07.

- C. Each unit price will be deemed to include an amount considered by Contractor/Bidder to be adequate to cover Contractor/Bidder's overhead and profit for each separately identified item.
- D. County or Contractor/Bidder may make a Claim for an adjustment in the Contract Price in accordance with Paragraph 10.05 if:
 - 1. the quantity of any item of Unit Price Work performed by Contractor/Bidder differs materially and significantly from the estimated quantity of such item indicated in the Agreement; and
 - 2.- there is no corresponding adjustment with respect to any other item of Work; and
 - 3. Contractor/Bidder believes that Contractor/Bidder is entitled to an increase in Contract Price as a result of having incurred additional expense or County believes that County is entitled to a decrease in Contract Price and the parties are unable to agree as to the amount of any such increase or decrease.
- E. If County objects to Contractor/Bidder's quoted adjustment in Unit Price Work set forth in paragraph 11.03.D, County may assign such work to its own forces or another Contractor/Bidder.
- F. <u>County reserves the right to delete any Unit Price Work without financial penalty incurred</u> from Contractor/Bidder.

ARTICLE 12 - CHANGE OF CONTRACT PRICE; CHANGE OF CONTRACT TIMES

- 12.01 Change of Contract Price
 - A. The Contract Price may only be changed by a Change Order. Any Claim for an adjustment in the Contract Price shall be based on written notice submitted by the party making the Claim to the Engineer and the other party to the Contract in accordance with the provisions of Paragraph 10.05.
 - B. The value of any Work covered by a Change Order or of any Claim for an adjustment in the Contract Price will be determined as follows:
 - 1. where the Work involved is covered by unit prices contained in the Contract Documents, by application of such unit prices to the quantities of the items involved (subject to the provisions of Paragraph 11.03); or
 - 2. where the Work involved is not covered by unit prices contained in the Contract Documents, by a mutually agreed lump sum (which may include an allowance for overhead and profit not necessarily in accordance with Paragraph 12.01.C.2); or
 - 3. where the Work involved is not covered by unit prices contained in the Contract Documents and agreement to a lump sum is not reached under Paragraph 12.01.B.2, on the basis of the Cost of the Work (determined as provided in Paragraph 11.01) plus a

Contractor/Bidder's fee for overhead and profit (determined as provided in Paragraph 12.01.C).

- C. *Contractor/Bidder's Fee:* The Contractor/Bidder's fee for overhead and profit shall be determined as follows:
 - 1. a mutually acceptable fixed fee; or
 - 2. if a fixed fee is not agreed upon, then a fee based on the following percentages of the various portions of the Cost of the Work:
 - a. for costs incurred under Paragraphs 11.01.A.1 and 11.01.A.2, the Contractor/Bidder's fee shall be 15 percent;
 - b. for costs incurred under Paragraph 11.01.A.3, the Contractor/Bidder's fee shall be five percent;
 - c. where one or more tiers of subcontracts are on the basis of Cost of the Work plus a fee and no fixed fee is agreed upon, the intent of Paragraphs 12.01.C.2.a and 12.01.C.2.b is that the SubContractor who actually performs the Work, at whatever tier, will be paid a fee of 15 percent of the costs incurred by such SubContractor under Paragraphs 11.01.A.1 and 11.01.A.2 and that any higher tier SubContractor and Contractor/Bidder will each be paid a fee of five percent of the amount paid to the next lower tier SubContractor;
 - d. no fee shall be payable on the basis of costs itemized under Paragraphs 11.01.A.4, 11.01.A.5, and 11.01.B;
 - e. the amount of credit to be allowed by Contractor/Bidder to County for any change which results in a net decrease in cost will be the amount of the actual net decrease in cost plus a deduction in Contractor/Bidder's fee by an amount equal to five percent of such net decrease; and
 - f. when both additions and credits are involved in any one change, the adjustment in Contractor/Bidder's fee shall be computed on the basis of the net change in accordance with Paragraphs 12.01.C.2.a through 12.01.C.2.e, inclusive.

12.02 Change of Contract Times

- A. The Contract Times may only be changed by a Change Order. Any Claim for an adjustment in the Contract Times shall be based on written notice submitted by the party making the Claim to the Engineer and the other party to the Contract in accordance with the provisions of Paragraph 10.05.
- B. Any adjustment of the Contract Times covered by a Change Order or any Claim for an adjustment in the Contract Times will be determined in accordance with the provisions of this Article 12.

- C. On the 21st of each month, or the next following business day, the Contractor/Bidder shall submit to the County and Engineer a request for weather days. Failure to submit the request forfeits the right to claim weather days for that period and any previous period. The County will grant time extensions, on a day for day basis, for delays caused by the effects of rains or other inclement weather conditions or related adverse soil conditions that prevent the Contractor/Bidder from productively performing controlling items of work resulting in:
 - (1) <u>The Contractor/Bidder being unable to work at least 50% of the normal work day on pre-</u><u>determined controlling work items due to adverse weather conditions.</u>

No additional compensation will be made for delays caused by the effects of inclement weather. (see SC-12.02.C)

- 12.03 Delays
 - A. Where Contractor/Bidder is prevented from completing any part of the Work within the Contract Times due to delay beyond the control of Contractor/Bidder, the Contract Times will be extended in an amount equal to the time lost due to such delay if a Claim is made therefor as provided in Paragraph 12.02.A. Delays beyond the control of Contractor/Bidder shall include, but not be limited to, acts or neglect by County, acts or neglect of utility Countys or other Contractor/Bidders performing other work as contemplated by Article 7, fires, floods, epidemics, abnormal weather conditions, or acts of God.
 - B. If County, Engineer, or other Contractor/Bidders or utility Countys performing other work for County as contemplated by Article 7, or anyone for whom County is responsible, delays, disrupts, or interferes with the performance or progress of the Work, then Contractor/Bidder shall be entitled to an equitable adjustment in the Contract Price or the Contract Times, or both. Contractor/Bidder's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor/Bidder's ability to complete the Work within the Contract Times.
 - C. If Contractor/Bidder is delayed in the performance or progress of the Work by fire, flood, epidemic, abnormal weather conditions, acts of God, acts or failures to act of utility Countys not under the control of County, or other causes not the fault of and beyond control of County and Contractor/Bidder, then Contractor/Bidder shall be entitled to an equitable adjustment in Contract Times, if such adjustment is essential to Contractor/Bidder's ability to complete the Work within the Contract Times. Such an adjustment shall be Contractor/Bidder's sole and exclusive remedy for the delays described in this Paragraph 12.03.C.
 - D. County, Engineer, and their officers, directors, members, partners, employees, agents, consultants, or SubContractors shall not be liable to Contractor/Bidder for any claims, costs, losses, or damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) sustained by Contractor/Bidder on or in connection with any other project or anticipated project.
 - E. Contractor/Bidder shall not be entitled to an adjustment in Contract Price or Contract Times for delays within the control of Contractor/Bidder. Delays attributable to and within the

control of a SubContractor or Supplier shall be deemed to be delays within the control of Contractor/Bidder.

ARTICLE 13 – TESTS AND INSPECTIONS; CORRECTION, REMOVAL OR ACCEPTANCE OF DEFECTIVE WORK

- 13.01 Notice of Defects
 - A. Prompt notice of all defective Work of which County or Engineer has actual knowledge will be given to Contractor/Bidder. Defective Work may be rejected, corrected, or accepted as provided in this Article 13.
- 13.02 Access to Work
 - A. County, Engineer, their consultants and other representatives and personnel of County, independent testing laboratories, and governmental agencies with jurisdictional interests will have access to the Site and the Work at reasonable times for their observation, inspection, and testing. Contractor/Bidder shall provide them proper and safe conditions for such access and advise them of Contractor/Bidder's safety procedures and programs so that they may comply therewith as applicable.
- 13.03 Tests and Inspections
 - A. Contractor/Bidder shall give Engineer timely notice of readiness of the Work for all required inspections, tests, or approvals and shall cooperate with inspection and testing personnel to facilitate required inspections or tests. <u>Contractor/Bidder shall reimburse County for the charges of Engineer and Engineer's Consultants for all costs due to work not being ready for tests and/or inspections when the Contractor/Bidder has notified Engineer that work is ready for tests and/or inspections. Contractor/Bidder shall reimburse County for all failed tests and subsequent retests. Reimbursement for the charges shall be a deduction from the Contractor/Bidder's Partial Payment(s). (see SC-13.03.A)</u>
 - B. County shall employ and pay for the services of an independent testing laboratory to perform all inspections, tests, or approvals required by the Contract Documents except:
 - 1. for inspections, tests, or approvals covered by Paragraphs 13.03.C and 13.03.D below;
 - 2. that costs incurred in connection with tests or inspections conducted pursuant to Paragraph 13.04.B shall be paid as provided in Paragraph 13.04.C; and
 - 3. as otherwise specifically provided in the Contract Documents.
 - B. The Contractor/Bidder shall obtain and employ an independent testing laboratory to provide the services specified herein and shall include all costs for these services in the contract price. The Contractor/Bidder shall submit for approval by the County and Engineer, the independent testing laboratory, including qualifications.

Copies of all testing agency invoices submitted to the Contractor/Bidder for payment shall be forwarded with the Contractor/Bidder's request for partial payment. Invoices shall be

submitted routinely throughout the project and shall be pertinent to the partial payment period under consideration. Testing agency invoices in excess of sixty (60) days old shall not be considered for payment. Invoices shall clearly indicate type and amount of test performed, unit and total cost, and shall indicate if the invoiced testing cost is a result of retests required due to the Contractor/Bidder's failure to achieve specified requirements. The cost of retesting due to test failure will be borne by the Contractor/Bidder. Payment to Contractor/Bidder for testing shall not be made without the required itemized invoicing. (see SC-13.03.B)

- C. If Laws or Regulations of any public body having jurisdiction require any Work (or part thereof) specifically to be inspected, tested, or approved by an employee or other representative of such public body, Contractor/Bidder shall assume full responsibility for arranging and obtaining such inspections, tests, or approvals, pay all costs in connection therewith, and furnish Engineer the required certificates of inspection or approval.
- D. Contractor/Bidder shall be responsible for arranging and obtaining and shall pay all costs in connection with any inspections, tests, or approvals required for County's and Engineer's acceptance of materials or equipment to be incorporated in the Work; or acceptance of materials, mix designs, or equipment submitted for approval prior to Contractor/Bidder's purchase thereof for incorporation in the Work. Such inspections, tests, or approvals shall be performed by organizations acceptable to County and Engineer.
- E. If any Work (or the work of others) that is to be inspected, tested, or approved is covered by Contractor/Bidder without written concurrence of Engineer, Contractor/Bidder shall, if requested by Engineer, uncover such Work for observation.
- F. Uncovering Work as provided in Paragraph 13.03.E shall be at Contractor/Bidder's expense unless Contractor/Bidder has given Engineer timely notice of Contractor/Bidder's intention to cover the same and Engineer has not acted with reasonable promptness in response to such notice.

13.04 Uncovering Work

- A. If any Work is covered contrary to the written request of Engineer, it must, if requested by Engineer, be uncovered for Engineer's observation and replaced at Contractor/Bidder's expense.
- B. If Engineer considers it necessary or advisable that covered Work be observed by Engineer or inspected or tested by others, Contractor/Bidder, at Engineer's request, shall uncover, expose, or otherwise make available for observation, inspection, or testing as Engineer may require, that portion of the Work in question, furnishing all necessary labor, material, and equipment.
- C. If it is found that the uncovered Work is defective, Contractor/Bidder shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such uncovering, exposure, observation, inspection, and testing, and of satisfactory replacement or reconstruction (including but not limited to all costs of repair or replacement of work of others); and County shall be entitled

to an appropriate decrease in the Contract Price. If the parties are unable to agree as to the amount thereof, County may make a Claim therefor as provided in Paragraph 10.05.

- D. If the uncovered Work is not found to be defective, Contractor/Bidder shall be allowed an increase in the Contract Price or an extension of the Contract Times, or both, directly attributable to such uncovering, exposure, observation, inspection, testing, replacement, and reconstruction. If the parties are unable to agree as to the amount or extent thereof, Contractor/Bidder may make a Claim therefor as provided in Paragraph 10.05.
- 13.05 County May Stop the Work
 - A. If the Work is defective, or Contractor/Bidder fails to supply sufficient skilled workers or suitable materials or equipment, or fails to perform the Work in such a way that the completed Work will conform to the Contract Documents, County may order Contractor/Bidder to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, this right of County to stop the Work shall not give rise to any duty on the part of County to exercise this right for the benefit of Contractor/Bidder, any SubContractor, any Supplier, any other individual or entity, or any surety for, or employee or agent of any of them.
- 13.06 Correction or Removal of Defective Work
 - A. Promptly after receipt of written notice, Contractor/Bidder shall correct all defective Work, whether or not fabricated, installed, or completed, or, if the Work has been rejected by Engineer, remove it from the Project and replace it with Work that is not defective. Contractor/Bidder shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such correction or removal (including but not limited to all costs of repair or replacement of work of others).
 - B. When correcting defective Work under the terms of this Paragraph 13.06 or Paragraph 13.07, Contractor/Bidder shall take no action that would void or otherwise impair County's special warranty and guarantee, if any, on said Work.
- 13.07 Correction Period
 - A. If within one year after the date of Substantial Completion (or such longer period of time as may be prescribed by the terms of any applicable special guarantee required by the Contract Documents) or by any specific provision of the Contract Documents, any Work is found to be defective, or if the repair of any damages to the land or areas made available for Contractor/Bidder's use by County or permitted by Laws and Regulations as contemplated in Paragraph 6.11.A is found to be defective, Contractor/Bidder shall promptly, without cost to County and in accordance with County's written instructions:
 - 1. repair such defective land or areas; or
 - 2. correct such defective Work; or

- 3. if the defective Work has been rejected by County, remove it from the Project and replace it with Work that is not defective, and
- 4. satisfactorily correct or repair or remove and replace any damage to other Work, to the work of others or other land or areas resulting therefrom.
- B. If Contractor/Bidder does not promptly comply with the terms of County's written instructions, or in an emergency where delay would cause serious risk of loss or damage, County may have the defective Work corrected or repaired or may have the rejected Work removed and replaced. All claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such correction or repair or such removal and replacement (including but not limited to all costs of repair or replacement of work of others) will be paid by Contractor/Bidder.
- C. In special circumstances where a particular item of equipment is placed in continuous service before Substantial Completion of all the Work, the correction period for that item may start to run from an earlier date if so provided in the Specifications.
- D. Where defective Work (and damage to other Work resulting therefrom) has been corrected or removed and replaced under this Paragraph 13.07, the correction period hereunder with respect to such Work will be extended for an additional period of one year after such correction or removal and replacement has been satisfactorily completed.
- E. Contractor/Bidder's obligations under this Paragraph 13.07 are in addition to any other obligation or warranty. The provisions of this Paragraph 13.07 shall not be construed as a substitute for, or a waiver of, the provisions of any applicable statute of limitation or repose.

13.08 Acceptance of Defective Work

A. If, instead of requiring correction or removal and replacement of defective Work, County (and, prior to Engineer's recommendation of final payment, Engineer) prefers to accept it, County may do so. Contractor/Bidder shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) attributable to County's evaluation of and determination to accept such defective Work (such costs to be approved by Engineer as to reasonableness) and for the diminished value of the Work to the extent not otherwise paid by Contractor/Bidder pursuant to this sentence. If any such acceptance occurs prior to Engineer's recommendation of final payment, a Change Order will be issued incorporating the necessary revisions in the Contract Documents with respect to the Work, and County shall be entitled to an appropriate decrease in the Contract Price, reflecting the diminished value of Work so accepted. If the parties are unable to agree as to the amount thereof, County may make a Claim therefor as provided in Paragraph 10.05. If the acceptance occurs after such recommendation, an appropriate amount will be paid by Contractor/Bidder to County. (see SC-13.08.A)

13.09 County May Correct Defective Work

- A. If Contractor/Bidder fails within a reasonable time after written notice from Engineer to correct defective Work, or to remove and replace rejected Work as required by Engineer in accordance with Paragraph 13.06.A, or if Contractor/Bidder fails to perform the Work in accordance with the Contract Documents, or if Contractor/Bidder fails to comply with any other provision of the Contract Documents, County may, after seven days written notice to Contractor/Bidder, correct, or remedy any such deficiency.
- B. In exercising the rights and remedies under this Paragraph 13.09, County shall proceed expeditiously. In connection with such corrective or remedial action, County may exclude Contractor/Bidder from all or part of the Site, take possession of all or part of the Work and suspend Contractor/Bidder's services related thereto, take possession of Contractor/Bidder's tools, appliances, construction equipment and machinery at the Site, and incorporate in the Work all materials and equipment stored at the Site or for which County has paid Contractor/Bidder but which are stored elsewhere. Contractor/Bidder shall allow County, County's representatives, agents and employees, County's other Contractor/Bidders, and Engineer and Engineer's consultants access to the Site to enable County to exercise the rights and remedies under this Paragraph.
- C. All claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) incurred or sustained by County in exercising the rights and remedies under this Paragraph 13.09 will be charged against Contractor/Bidder, and a Change Order will be issued incorporating the necessary revisions in the Contract Documents with respect to the Work; and County shall be entitled to an appropriate decrease in the Contract Price. If the parties are unable to agree as to the amount of the adjustment, County may make a Claim therefor as provided in Paragraph 10.05. Such claims, costs, losses and damages will include but not be limited to all costs of repair, or replacement of work of others destroyed or damaged by correction, removal, or replacement of Contractor/Bidder's defective Work. (see SC-13.09.C)
- D. Contractor/Bidder shall not be allowed an extension of the Contract Times because of any delay in the performance of the Work attributable to the exercise by County of County's rights and remedies under this Paragraph 13.09.

ARTICLE 14 – PAYMENTS TO CONTRACTOR/BIDDER AND COMPLETION

14.01 Schedule of Values

A. The Schedule of Values established as provided in Paragraph 2.07.A will serve as the basis for progress payments and will be incorporated into a form of Application for Payment acceptable to Engineer. Progress payments on account of Unit Price Work will be based on the number of units completed.

14.02 Progress Payments

A. Applications for Payments:

- 1. At least 20 days before the date established in the Agreement for each progress payment (but not more often than once a month), Contractor/Bidder shall submit to Engineer for review an Application for Payment filled out and signed by Contractor/Bidder covering the Work completed as of the date of the Application and accompanied by such supporting documentation as is required by the Contract Documents. If payment is requested on the basis of materials and equipment not incorporated in the Work but delivered and suitably stored at the Site or at another location agreed to in writing, the Application for Payment shall also be accompanied by a bill of sale, invoice, or other documentation warranting that County has received the materials and equipment free and clear of all Liens and evidence that the materials and equipment are covered by appropriate property insurance or other arrangements to protect County's interest therein, all of which must be satisfactory to County.
- 2. Beginning with the second Application for Payment, each Application shall include an affidavit of Contractor/Bidder stating that all previous progress payments received on account of the Work have been applied on account to discharge Contractor/Bidder's legitimate obligations associated with prior Applications for Payment. Beginning with the second Application for Payment, each Application shall include an affidavit of Contractor/Bidder certifying that Contractor/Bidder has disbursed to all SubContractors and suppliers having an interest in the contract their pro rata share of the payment out of previous progress payments received by Contractor/Bidder for all work completed and materials furnished in the previous work period, less a retainage withheld by Contractor/Bidder pursuant to an agreement with a SubContractor. Within 30 days of receipt for the final progress payment or any other payments received thereafter except the final payment, Contractor/Bidder shall pay all SubContractors and suppliers having an interest of the payment for all work completed and materials furnished. (see SC-14.02.A.2)
- 3. The amount of retainage with respect to progress payments will be as stipulated in the Agreement.
- B. Review of Applications:
 - Engineer will, within 10 days after receipt of each Application for Payment, either indicate in writing a recommendation of payment and present the Application to County or return the Application to Contractor/Bidder indicating in writing Engineer's reasons for refusing to recommend payment. In the latter case, Contractor/Bidder may make the necessary corrections and resubmit the Application or direct Engineer to present the Application to County with Engineer's recommendation of partial payment. (see SC-14.02.B.1)
 - 2. Engineer's recommendation of any payment requested in an Application for Payment will constitute a representation by Engineer to County, based on Engineer's observations of the executed Work as an experienced and qualified design professional, and on Engineer's review of the Application for Payment and the accompanying data and

schedules <u>and the Contract Documents (see SC-14.02.B2)</u>, that to the best of Engineer's knowledge, information and belief:

- a. the Work has progressed to the point indicated;
- b. the quality of the Work is generally in accordance with the Contract Documents (subject to an evaluation of the Work as a functioning whole prior to or upon Substantial Completion, the results of any subsequent tests called for in the Contract Documents, a final determination of quantities and classifications for Unit Price Work under Paragraph 9.07, and any other qualifications stated in the recommendation); and
- c. the conditions precedent to Contractor/Bidder's being entitled to such payment appear to have been fulfilled in so far as it is Engineer's responsibility to observe the Work.
- d. <u>Contractor/Bidder's other obligations under the Contract Documents have been</u> <u>fulfilled. (see SC-14.02.B.2.d)</u>
- 3. By recommending any such payment Engineer will not thereby be deemed to have represented that:
 - a. inspections made to check the quality or the quantity of the Work as it has been performed have been exhaustive, extended to every aspect of the Work in progress, or involved detailed inspections of the Work beyond the responsibilities specifically assigned to Engineer in the Contract Documents; or
 - b. there may not be other matters or issues between the parties that might entitle Contractor/Bidder to be paid additionally by County or entitle County to withhold payment to Contractor/Bidder.
- 4. Neither Engineer's review of Contractor/Bidder's Work for the purposes of recommending payments nor Engineer's recommendation of any payment, including final payment, will impose responsibility on Engineer:
 - a. to supervise, direct, or control the Work, or
 - b. for the means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or
 - c. for Contractor/Bidder's failure to comply with Laws and Regulations applicable to Contractor/Bidder's performance of the Work, or
 - d. to make any examination to ascertain how or for what purposes Contractor/Bidder has used the moneys paid on account of the Contract Price, or
 - e. to determine that title to any of the Work, materials, or equipment has passed to County free and clear of any Liens.

- 5. Engineer may refuse to recommend the whole or any part of any payment if, in Engineer's opinion, it would be incorrect to make the representations to County stated in Paragraph 14.02.B.2. Engineer may also refuse to recommend any such payment or, because of subsequently discovered evidence or the results of subsequent inspections or tests, revise or revoke any such payment recommendation previously made, to such extent as may be necessary in Engineer's opinion to protect County from loss because:
 - a. the Work is defective, or completed Work has been damaged, requiring correction or replacement;
 - b. the Contract Price has been reduced by Change Orders;
 - c. County has been required to correct defective Work or complete Work in accordance with Paragraph 13.09; or
 - d. Engineer has actual knowledge of the occurrence of any of the events enumerated in Paragraph 15.02.A.
- C. Payment Becomes Due:
 - 1. Ten days after presentation of the Application for Payment to County with Engineer's recommendation, the amount recommended will (subject to the provisions of Paragraph 14.02.D) become due, and when due will be paid by County to Contractor/Bidder.
- D. Reduction in Payment:
 - 1. County may refuse to make payment of the full amount recommended by Engineer because:
 - a. claims have been made against County on account of Contractor/Bidder's performance or furnishing of the Work;
 - Liens have been filed in connection with the Work, except where Contractor/Bidder has delivered a specific bond satisfactory to County to secure the satisfaction and discharge of such Liens;
 - c. there are other items entitling County to a set-off against the amount recommended; or
 - d. County has actual knowledge of the occurrence of any of the events enumerated in Paragraphs 14.02.B.5.a through 14.02.B.5.c or Paragraph 15.02.A.
 - 2. If County refuses to make payment of the full amount recommended by Engineer, County will give Contractor/Bidder immediate written notice (with a copy to Engineer) stating the reasons for such action and promptly pay Contractor/Bidder any amount remaining after deduction of the amount so withheld. County shall promptly pay Contractor/Bidder the amount so withheld, or any adjustment thereto agreed to by County and Contractor/Bidder, when Contractor/Bidder remedies the reasons for such action.

- 3. Upon a subsequent determination that County's refusal of payment was not justified, the amount wrongfully withheld shall be treated as an amount due as determined by Paragraph 14.02.C.1 and subject to interest as provided in the Agreement.
- 14.03 Contractor/Bidder's Warranty of Title
 - A. Contractor/Bidder warrants and guarantees that title to all Work, materials, and equipment covered by any Application for Payment, whether incorporated in the Project or not, will pass to County no later than the time of payment free and clear of all Liens.

14.04 Substantial Completion

- A. When Contractor/Bidder considers the entire Work ready for its intended use Contractor/Bidder shall notify County and Engineer in writing that the entire Work is substantially complete (except for items specifically listed by Contractor/Bidder as incomplete) and request that Engineer issue a certificate of Substantial Completion.
- B. Promptly after Contractor/Bidder's notification, County, Contractor/Bidder, and Engineer shall make an inspection of the Work to determine the status of completion. If Engineer does not consider the Work substantially complete, Engineer will notify Contractor/Bidder in writing giving the reasons therefor.
- C. If Engineer considers the Work substantially complete, Engineer will deliver to County a tentative certificate of Substantial Completion which shall fix the date of Substantial Completion. There shall be attached to the certificate a tentative list of items to be completed or corrected before final payment. County shall have seven days after receipt of the tentative certificate during which to make written objection to Engineer as to any provisions of the certificate or attached list. If, after considering such objections, Engineer concludes that the Work is not substantially complete, Engineer will, within 14 days after submission of the tentative certificate to County, notify Contractor/Bidder in writing, stating the reasons therefor. If, after consideration of County's objections, Engineer considers the Work substantially complete, Engineer will, within said 14 days, execute and deliver to County and Contractor/Bidder a definitive certificate of Substantial Completion (with a revised tentative list of items to be completed or corrected) reflecting such changes from the tentative certificate as Engineer believes justified after consideration of any objections from County.
- D. At the time of delivery of the tentative certificate of Substantial Completion, Engineer will deliver to County and Contractor/Bidder a written recommendation as to division of responsibilities pending final payment between County and Contractor/Bidder with respect to security, operation, safety, and protection of the Work, maintenance, heat, utilities, insurance, and warranties and guarantees. Unless County and Contractor/Bidder agree otherwise in writing and so inform Engineer in writing prior to Engineer's issuing the definitive certificate of Substantial Completion, Engineer's aforesaid recommendation will be binding on County and Contractor/Bidder until final payment.
- E. County shall have the right to exclude Contractor/Bidder from the Site after the date of Substantial Completion subject to allowing Contractor/Bidder reasonable access to remove its property and complete or correct items on the tentative list.

14.05 Partial Utilization

- A. Prior to Substantial Completion of all the Work, County may use or occupy any substantially completed part of the Work which has specifically been identified in the Contract Documents, or which County, Engineer, and Contractor/Bidder agree constitutes a separately functioning and usable part of the Work that can be used by County for its intended purpose without significant interference with Contractor/Bidder's performance of the remainder of the Work, subject to the following conditions:
 - 1. County at any time may request Contractor/Bidder in writing to permit County to use or occupy any such part of the Work which County believes to be ready for its intended use and substantially complete. If and when Contractor/Bidder agrees that such part of the Work is substantially complete, Contractor/Bidder, County, and Engineer will follow the procedures of Paragraph 14.04.A through D for that part of the Work.
 - 2. Contractor/Bidder at any time may notify County and Engineer in writing that Contractor/Bidder considers any such part of the Work ready for its intended use and substantially complete and request Engineer to issue a certificate of Substantial Completion for that part of the Work.
 - 3. Within a reasonable time after either such request, County, Contractor/Bidder, and Engineer shall make an inspection of that part of the Work to determine its status of completion. If Engineer does not consider that part of the Work to be substantially complete, Engineer will notify County and Contractor/Bidder in writing giving the reasons therefor. If Engineer considers that part of the Work to be substantially complete, the provisions of Paragraph 14.04 will apply with respect to certification of Substantial Completion of that part of the Work and the division of responsibility in respect thereof and access thereto.
 - 4. No use or occupancy or separate operation of part of the Work may occur prior to compliance with the requirements of Paragraph 5.10 regarding property insurance.

14.06 Final Inspection

A. Upon written notice from Contractor/Bidder that the entire Work or an agreed portion thereof is complete, Engineer will promptly make a final inspection with County and Contractor/Bidder and will notify Contractor/Bidder in writing of all particulars in which this inspection reveals that the Work is incomplete or defective. Contractor/Bidder shall immediately take such measures as are necessary to complete such Work or remedy such deficiencies.

14.07 Final Payment

A. Application for Payment:

- 1. After Contractor/Bidder has, in the opinion of Engineer, satisfactorily completed all corrections identified during the final inspection and has delivered, in accordance with the Contract Documents, all maintenance and operating instructions, schedules, guarantees, bonds, certificates or other evidence of insurance, certificates of inspection, marked-up record documents (as provided in Paragraph 6.12), and other documents, Contractor/Bidder may make application for final payment following the procedure for progress payments.
- 2. The final Application for Payment shall be accompanied (except as previously delivered) by:
 - a. all documentation called for in the Contract Documents, including but not limited to the evidence of insurance required by Paragraph 5.04.B.6;
 - b. consent of the surety, if any, to final payment;
 - c. a list of all Claims against County that Contractor/Bidder believes are unsettled; and
 - d. complete and legally effective releases or waivers (satisfactory to County) of all Lien rights arising out of or Liens filed in connection with the Work.
- 3. In lieu of the releases or waivers of Liens specified in Paragraph 14.07.A.2 and as approved by County, Contractor/Bidder may furnish receipts or releases in full and an affidavit of Contractor/Bidder that: (i) the releases and receipts include all labor, services, material, and equipment for which a Lien could be filed; and (ii) all payrolls, material and equipment bills, and other indebtedness connected with the Work for which County might in any way be responsible, or which might in any way result in liens or other burdens on County's property, have been paid or otherwise satisfied. If any SubContractor or Supplier fails to furnish such a release or receipt in full, Contractor/Bidder may furnish a bond or other collateral satisfactory to County to indemnify County against any Lien.
- B. Engineer's Review of Application and Acceptance:
 - 1. If, on the basis of Engineer's observation of the Work during construction and final inspection, and Engineer's review of the final Application for Payment and accompanying documentation as required by the Contract Documents, Engineer is satisfied that the Work has been completed and Contractor/Bidder's other obligations under the Contract Documents have been fulfilled, Engineer will, within ten days after receipt of the final Application for Payment, indicate in writing Engineer's recommendation of payment and present the Application for Payment to County for payment. At the same time Engineer will also give written notice to County and Contractor/Bidder that the Work is acceptable subject to the provisions of Paragraph 14.09. Otherwise, Engineer will return the Application for Payment to Contractor/Bidder, indicating in writing the reasons for refusing to recommend final

payment, in which case Contractor/Bidder shall make the necessary corrections and resubmit the Application for Payment.

- C. Payment Becomes Due:
 - 1. Thirty days after the presentation to County of the Application for Payment and accompanying documentation, the amount recommended by Engineer, less any sum County is entitled to set off against Engineer's recommendation, including but not limited to liquidated damages, will become due and will be paid by County to Contractor/Bidder.

14.08 Final Completion Delayed

A. If, through no fault of Contractor/Bidder, final completion of the Work is significantly delayed, and if Engineer so confirms, County shall, upon receipt of Contractor/Bidder's final Application for Payment (for Work fully completed and accepted) and recommendation of Engineer, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed and accepted. If the remaining balance to be held by County for Work not fully completed or corrected is less than the retainage stipulated in the Agreement, and if bonds have been furnished as required in Paragraph 5.01, the written consent of the surety to the payment of the balance due for that portion of the Work fully completed shall be submitted by Contractor/Bidder to Engineer with the Application for such payment. Such payment shall be made under the terms and conditions governing final payment, except that it shall not constitute a waiver of Claims.

14.09 Waiver of Claims

- A. The making and acceptance of final payment will constitute:
 - a waiver of all Claims by County against Contractor/Bidder, except Claims arising from unsettled Liens, from defective Work appearing after final inspection pursuant to Paragraph 14.06, from failure to comply with the Contract Documents or the terms of any special guarantees specified therein, or <u>whenever said failure occurs</u> from Contractor/Bidder's continuing obligations under the Contract Documents; and <u>(see SC-14.09.A.1)</u>
 - 2. a waiver of all Claims by Contractor/Bidder against County other than those previously made in accordance with the requirements herein and expressly acknowledged by County in writing as still unsettled.
 - 3. The acceptance of final payment by Contractor/Bidder designated and identified by Engineer as final payment shall be and shall operate as a release to County of all claims and all liability to Contractor/Bidder other than claims in stated amounts as may be specifically excepted by Contractor/Bidder for all things done or finished in connection with the Work and for every act of County and others relating to or arising out of the Work. Any payment, however, final or otherwise, shall not release Contractor/Bidder or Contractor/Bidder's Surety(ies) from any obligations under the Contract Documents or Bonds. (see SC-14.09.A.3)

ARTICLE 15 – SUSPENSION OF WORK AND TERMINATION

- 15.01 County May Suspend Work
 - A. At any time and without cause, County may suspend the Work or any portion thereof for a period of not more than 90 consecutive days by notice in writing to Contractor/Bidder and Engineer which will fix the date on which Work will be resumed. Contractor/Bidder shall resume the Work on the date so fixed. Contractor/Bidder shall be granted an adjustment in the Contract Price or an extension of the Contract Times, or both, directly attributable to any such suspension if Contractor/Bidder makes a Claim therefor as provided in Paragraph 10.05.
- 15.02 County May Terminate for Cause
 - A. The occurrence of any one or more of the following events will justify termination for cause:
 - Contractor/Bidder's <u>start the work in accordance with the Notice to Proceed or Contractor/Bidder's</u> persistent failure to perform the Work in accordance with the Contract Documents (including, but not limited to, failure to supply sufficient skilled workers or suitable materials or equipment or failure to adhere to the Progress Schedule established under Paragraph 2.07 as adjusted from time to time pursuant to Paragraph 6.04) (see SC-15.02.A.1);
 - 2. Contractor/Bidder's disregard of Laws or Regulations of any public body having jurisdiction;
 - 3. Contractor/Bidder's repeated disregard of the authority of Engineer; or
 - 4. Contractor/Bidder's violation in any substantial way of any provisions of the Contract Documents.
 - B. If one or more of the events identified in Paragraph 15.02.A occur, County may, after giving Contractor/Bidder (and surety) seven days written notice of its intent to terminate the services of Contractor/Bidder:
 - 1. exclude Contractor/Bidder from the Site, and take possession of the Work and of all Contractor/Bidder's tools, appliances, construction equipment, and machinery at the Site, and use the same to the full extent they could be used by Contractor/Bidder (without liability to Contractor/Bidder for trespass or conversion);
 - 2. incorporate in the Work all materials and equipment stored at the Site or for which County has paid Contractor/Bidder but which are stored elsewhere; and
 - 3. complete the Work as County may deem expedient.
 - C. If County proceeds as provided in Paragraph 15.02.B, Contractor/Bidder shall not be entitled to receive any further payment until the Work is completed. If the unpaid balance of the Contract Price exceeds all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court

or arbitration or other dispute resolution costs) sustained by County arising out of or relating to completing the Work, such excess will be paid to Contractor/Bidder. If such claims, costs, losses, and damages exceed such unpaid balance, Contractor/Bidder shall pay the difference to County. Such claims, costs, losses, and damages incurred by County will be reviewed by Engineer as to their reasonableness and, when so approved by Engineer, incorporated in a Change Order. When exercising any rights or remedies under this Paragraph, County shall not be required to obtain the lowest price for the Work performed.

- D. Notwithstanding Paragraphs 15.02.B and 15.02.C, Contractor/Bidder's services will not be terminated if Contractor/Bidder begins within seven days of receipt of notice of intent to terminate to correct its failure to perform and proceeds diligently to cure such failure within no more than 30 days of receipt of said notice.
- E. Where Contractor/Bidder's services have been so terminated by County, the termination will not affect any rights or remedies of County against Contractor/Bidder then existing or which may thereafter accrue. Any retention or payment of moneys due Contractor/Bidder by County will not release Contractor/Bidder from liability.
- F. If and to the extent that Contractor/Bidder has provided a performance bond under the provisions of Paragraph 5.01.A, the termination procedures of that bond shall supersede the provisions of Paragraphs 15.02.B and 15.02.C.
- 15.03 County May Terminate For Convenience
 - A. Upon seven days written notice to Contractor/Bidder and Engineer, County may, without cause and without prejudice to any other right or remedy of County, terminate the Contract. In such case, Contractor/Bidder shall be paid for (without duplication of any items):
 - 1. completed and acceptable Work executed in accordance with the Contract Documents prior to the effective date of termination, including fair and reasonable sums for overhead and profit on such Work;
 - 2. expenses sustained prior to the effective date of termination in performing services and furnishing labor, materials, or equipment as required by the Contract Documents in connection with uncompleted Work, plus fair and reasonable sums for overhead and profit on such expenses;
 - 3. all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) incurred in settlement of terminated contracts with SubContractors, Suppliers, and others; and
 - 4. reasonable expenses directly attributable to termination.
 - B. Contractor/Bidder shall not be paid on account of loss of anticipated profits or revenue or other economic loss arising out of or resulting from such termination.

15.04 Contractor/Bidder May Stop Work or Terminate

- A. If, through no act or fault of Contractor/Bidder, (i) the Work is suspended for more than 90 consecutive days by County or under an order of court or other public authority, or (ii) Engineer fails to act on any Application for Payment within 30 days after it is submitted, or (iii) County fails for 30 days to pay Contractor/Bidder any sum finally determined to be due, then Contractor/Bidder may, upon seven days written notice to County and Engineer, and provided County or Engineer do not remedy such suspension or failure within that time, terminate the Contract and recover from County payment on the same terms as provided in Paragraph 15.03.
- B. In lieu of terminating the Contract and without prejudice to any other right or remedy, if Engineer has failed to act on an Application for Payment within 30 days after it is submitted, or County has failed for 30 days to pay Contractor/Bidder any sum finally determined to be due, Contractor/Bidder may, seven days after written notice to County and Engineer, stop the Work until payment is made of all such amounts due Contractor/Bidder, including interest thereon. The provisions of this Paragraph 15.04 are not intended to preclude Contractor/Bidder from making a Claim under Paragraph 10.05 for an adjustment in Contract Price or Contract Times or otherwise for expenses or damage directly attributable to Contractor/Bidder's stopping the Work as permitted by this Paragraph.

ARTICLE 16 – DISPUTE RESOLUTION

- 16.01 Methods and Procedures
 - A. Either County or Contractor/Bidder may request mediation of any Claim submitted to Engineer for a decision under Paragraph 10.05 before such decision becomes final and binding. The mediation will be governed by the Construction Industry Mediation Rules of the American Arbitration Association in effect as of the Effective Date of the Agreement. The request for mediation shall be submitted in writing to the American Arbitration Association and the other party to the Contract. Timely submission of the request shall stay the effect of Paragraph 10.05.E.
 - B. County and Contractor/Bidder shall participate in the mediation process in good faith. The process shall be concluded within 60 days of filing of the request. The date of termination of the mediation shall be determined by application of the mediation rules referenced above.
 - C. If the Claim is not resolved by mediation, Engineer's action under Paragraph 10.05.C or a denial pursuant to Paragraphs 10.05.C.3 or 10.05.D shall become final and binding 30 days after termination of the mediation unless, within that time period, County or Contractor/Bidder:
 - 1. elects in writing to invoke any dispute resolution process provided for in the Supplementary Conditions; or
 - 2. agrees with the other party to submit the Claim to another dispute resolution process; or
 - 3. gives written notice to the other party of the intent to submit the Claim to a court of competent jurisdiction.

ARTICLE 17 – MISCELLANEOUS

17.01 Giving Notice

- A. Whenever any provision of the Contract Documents requires the giving of written notice, it will be deemed to have been validly given if:
 - 1. delivered in person to the individual or to a member of the firm or to an officer of the corporation for whom it is intended; or
 - 2. delivered at or sent by registered or certified mail, postage prepaid, to the last business address known to the giver of the notice.

17.02 Computation of Times

A. When any period of time is referred to in the Contract Documents by days, it will be computed to exclude the first and include the last day of such period. If the last day of any such period falls on a Saturday or Sunday or on a day made a legal holiday by the law of the applicable jurisdiction, such day will be omitted from the computation.

17.03 Cumulative Remedies

A. The duties and obligations imposed by these General Conditions and the rights and remedies available hereunder to the parties hereto are in addition to, and are not to be construed in any way as a limitation of, any rights and remedies available to any or all of them which are otherwise imposed or available by Laws or Regulations, by special warranty or guarantee, or by other provisions of the Contract Documents. The provisions of this Paragraph will be as effective as if repeated specifically in the Contract Documents in connection with each particular duty, obligation, right, and remedy to which they apply.

17.04 Survival of Obligations

A. All representations, indemnifications, warranties, and guarantees made in, required by, or given in accordance with the Contract Documents, as well as all continuing obligations indicated in the Contract Documents, will survive final payment, completion, and acceptance of the Work or termination or completion of the Contract or termination of the services of Contractor/Bidder.

17.05 Controlling Law

A. This Contract is to be governed by the law of the state in which the Project is located.

17.06 Headings

A. Article and paragraph headings are inserted for convenience only and do not constitute parts of these General Conditions.

SUPPLEMENTARY CONDITIONS

These Supplementary Conditions amend or supplement the Standard General Conditions of the Construction Contract (EJCDC C-700, 2007 Edition). All provisions which are not so amended or supplemented remain in full force and effect.

The terms used in these Supplementary Conditions which are defined in the Standard General Conditions of the Construction Contract have the meanings assigned to them in the General Conditions.

ARTICLE 1 DEFINITIONS AND TERMINOLOGY

Add the following new paragraph immediately after paragraph 1.01.51:

SC-1.01.52 SURETY – The person, firm, or corporation which is bound by the contract bonds with and for Contractor/Bidder (Principal); and which is held and firmly bound unto County for the conditions of obligations set forth in said bonds.

ARTICLE 2 PRELIMINARY MATTERS

- SC-2.02.A Amend the first sentence of paragraph 2.02.A of the General Conditions by changing "up to ten" to "five".
- SC-2.05.A Amend the first sentence of paragraph 2.05.A of the General Conditions by changing "Within 10 days after the Effective Date of the Agreement" to "At the Preconstruction Conference".

Add the following new paragraph immediately after paragraph 2.05.A.3:

SC-2.05.B Before any Work at the Site is started, Contractor/Bidder shall deliver to the County, certificates of insurance that Contractor/Bidder is required to purchase and maintain in accordance with Article 5.

Add the following new paragraph immediately after paragraph 2.06.B:

SC-2.06.C County may issue Notice to Proceed at the Preconstruction Conference. Contractor/Bidder shall begin the Work within twenty-four (24) hours of the date given in the Notice to Proceed. If the Contractor/Bidder does not start the Work within fourteen (14) calendar days after this date, County may, at his discretion, terminate Contractor/Bidder in accordance with paragraph 15.02.

Delete paragraph 2.07.A in its entirety and insert the following in its place:

SC-2.07.A All schedules as set forth in Article 2 shall be submitted and accepted by the County and Engineer within 30 days of NTP. Should any schedule not be accepted within 30 days of the NTP, it will be considered a breach of contract and reason for termination of the contract for cause in accordance with the General Conditions, Section 15.02.

ARTICLE 4 AVAILABILITY OF LANDS; SUBSURFACE AND PHYSICAL CONDITIONS; HAZARDOUS ENVIRIONMENTAL CONDITIONS; REFERENCE POINTS

Add the following to the end of paragraph 4.01.C:

SC-4.01.C Contractor/Bidder shall obtain said land rights at his own expense and without liability to the County. Contractor/Bidder shall not enter upon private property without first obtaining written permission from the rightful property County.

Add the following new paragraph immediately after paragraph 4.02.B:

- SC-4.02.CIn the preparation of Drawings and Specifications, Engineer or Engineer's Consultants relied
upon the following report(s) of explorations and tests of subsurface conditions at the Site:
See Appendix A
- Amend the last sentence in paragraph 4.03.C.3 to read:
- SC-4.03.C.3 However, County, Engineer and Engineer's Consultants shall not be liable to Contractor/Bidder for any claims, costs, losses, or damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or other dispute resolution costs) sustained by Contractor/Bidder on or in connection with any other project or anticipated project.

ARTICLE 5 BONDS AND INSURANCE

Delete paragraph 5.01.B in its entirety and insert the following in its place:

SC-5.01.B All Bonds shall be in the form prescribed by the Contract Documents or other form approved by County. All else notwithstanding, the terms of all Bonds shall be substantially in the form prescribed by Chapter 255, Florida Statutes. All Bonds shall be executed by Contractor/Bidder and a corporate bonding company licensed to transact such business in the State of Florida and named on the current list of "Surety Companies Acceptable on Federal Bonds" as published in the Treasury Department Circular Number 570. Contractor/Bidder will cause the Bonds to be recorded with the Clerk of the Circuit Court in the county in which the Work is to be performed. Failure to execute bonds in the form prescribed may constitute non-responsiveness on the part of the Contractor/Bidder. The expense for all Bonds shall be the Contractor/Bidder's responsibility.

Add the following to the end of paragraph 5.02.A:

SC-5.02.A Certificates of insurance shall be issued by a company with a Best's rating of at least B+ authorized to do business in the State of Florida. County must approve non-rated insurers. If used, County shall be shown as Certificate Holder, Engineer as Additional Insured and provide a 30-day cancellation notice.

Delete paragraph 5.03.B in its entirety and insert the following in its place:

SC-5.03.B Insurance policies written on a "Claims Made" form is not acceptable without County's approval.

Add the following new paragraphs immediately after paragraph 5.03.B:

- SC-5.03.C Umbrella Liability insurance is preferred, but an Excess Liability equivalent is acceptable. Whichever type of coverage is provided, it shall not be more restrictive than the underlying insurance policy coverages, including, but not limited to the coverage Trigger, defense, notice of occurrence/accident/circumstances, notice of claim and extended reporting period.
- SC-5.03.D No work shall commence under this contract until the required Certificate(s) have been provided. Work shall not continue after expiration (or cancellation) until new Certificate(s) have been provided. Non-continuance of work after expiration (or cancellation) of Certificate(s) will not constitute a delay beyond Contractor/Bidder's control as defined in paragraph 12.03.
- SC-5.03.E Contractor/Bidder shall arrange for its insurers' policies to include, or be endorsed to include, a severability or interest/cross liability provision, so that County will be treated as if a separate policy were in existence, but without increasing the policy limits.
- SC-5.03.F Contractor/Bidder's deductibles/self-insured retentions shall be disclosed to County and may be disapproved by the latter. They shall be reduced or eliminated at the option of County. Contractor/Bidder is responsible for the amount of any deductible or self-insured retention.
- SC-5.03.G These insurance requirements shall not relieve or limit the liability of Contractor/Bidder. County does not in any way represent that these types or amounts of insurance are sufficient or adequate to protect Contractor/Bidder's interests or liabilities, but are merely minimums.
- SC-5.03.H Insurance required of Contractor/Bidder or any other insurance of Contractor/Bidder shall be considered primary, and insurance or self-insurance of County shall be considered excess, as may be applicable to claims that arise out of this contract.
- SC-5.03.1 Receipt of Certificates or other documentation of insurance or policies or copies of policies by County, or by any of its representatives, which indicate less coverage than required does

not constitute a waiver of the Contractor/Bidder's obligation to fulfill the insurance requirements herein.

- SC-5.03. J The Contractor/Bidder shall either (a) require each subContractor/Bidder to produce and maintain the same coverage as required of the Contractor/Bidder, or (b) insure the activities of subContractor/Bidders in his own policy.
- SC-5.03.K These insurance requirements are minimums and may not be adequate to cover Contractor/Bidder exposures.

Add the following new paragraphs immediately after paragraph 5.04.B:

SC-5.04.C Contractor/Bidder shall purchase and maintain coverages listed on Appendix D of Contract Documents.

Delete paragraphs 5.06 through 5.10 in their entirety except for paragraph 5.06.D and insert the following in place of 5.09.A:

SC-5.09.A If County has any objection to the coverage afforded by or other provisions of Bonds or insurance required to be purchased and maintained by Contractor/Bidder in accordance with Article 5 on the basis of non-conformance with the Contract Documents, County shall so notify Contractor/Bidder in writing within ten days after receipt of the certificates (or other evidence requested) required by paragraph 2.05.C. Contractor/Bidder shall provide to County such additional information in respect of insurance provided as County may reasonably request.

ARTICLE 6 CONTRACTOR/BIDDER'S RESPONSIBILITIES

Add the following to the end of paragraph 6.01.A:

- SC-6.01.A County reserves the right to reject any means, methods, techniques, sequences or procedures proposed by Contractor/Bidder which:
 - 1. will constitute or create a hazard to the Work or to the persons or damage to property or existing utilities; or
 - 2. will not produce finished work in accordance with the terms of the contract Documents.

County's failure to exercise his right to reject such means, methods, techniques, sequences or procedures shall not relieve the Contractor/Bidder of his obligation to accomplish the result intended in the Contract Documents nor shall the exercise of such right create a cause of action for damages.

Add the following new paragraph immediately after paragraph 6.02.B:

SC-6.02.C Engineer shall record time and costs required by Engineer and Engineer's Consultants to provide inspection services due to Contractor/Bidder's working beyond regular working hours as defined in the General Requirements. County's reimbursement for the charges shall be a deduction from Contractor/Bidder's Partial Payment(s) in accordance with Section 01 11 00 (Summary of Work) Part 2.04.

Add the following new paragraphs immediately after paragraph 6.05.A.2.d:

- SC-6.05.A.2.e Each action mentioned above required for review of proposed substitute items of material or equipment shall be followed in the order given. Failure to do so shall be cause for rejection of the proposed substitution.
- SC-6.05.A.2.f Contractor/Bidder shall reimburse County for the charges of Engineer or Engineer's Consultants for evaluation of substitutions. County's reimbursement for the charges shall be a deduction from the Contractor/Bidder's Partial Payment(s).

Add the following to the end of paragraph 6.06.A:

SC -6.06.A Contractor/Bidder shall not subcontract part(s) or the work, the aggregate cost of which is greater than 50 percent of the contract price, without prior written approval by County. Contractor/Bidder shall cause appropriate provisions to be inserted in all subcontracts relative to the Work that bind SubContractor/Bidders to Contractor/Bidder by the terms of the Contract Documents insofar as applicable to the work of SubContractor/Bidders and to give Contractor/Bidder the same power as regards terminating any subcontract that County may exercise over Contractor/Bidder under any provision of the Contract Documents. Nothing contained in the subcontract shall create any contractor/Bidder shall discharge all duties and responsibilities of Contractor/Bidder to County covered by his subcontract.

Add the following to the end of paragraph 6.06.B:

SC-6.06.B SubContractor/Bidders and Suppliers shall be identified on the form provided in the Bidding Requirements.

Add the following to the end of paragraph 6.08.A:

SC-6.08.A Permits, licenses, and easements for permanent structures or permanent changes in existing facilities shall be secured and paid for by County, unless otherwise specified.

Add the following to the end of paragraph 6.09.A:

SC-6.09.A Contractor/Bidder shall also cause all SubContractor/Bidders to comply with all federal, state, county, and municipal laws, ordinances, rules, and regulations bearing on the conduct of the Work.

Add the following to the end of paragraph 6.09.B:

SC-6.09.B If Contractor/Bidder observes that the Contract Documents are at variance with said laws, ordinances, rates, or regulations, Contractor/Bidder shall promptly notify Engineer of Record and the County in writing, and any necessary changes shall be adjusted as provided in the Contract Documents. Contractor/Bidder shall not proceed with the Work until so instructed by County.

Add the following to the end of paragraph 6.12.A:

SC-6.12.A Annotations of record documents shall be legible, precise, and complete as determined by Engineer of Record and the County.

Add the following new paragraph after paragraph 6.13.D:

SC-6.13.E Contractor/Bidder shall be responsible at all times for precautions to achieve the protection of all persons, including employees and property. Contractor/Bidder shall make special effort to detect hazardous conditions and shall take prompt action where necessary to avoid accident, injury, or property damage. OSHA and all other applicable safety laws and ordinances shall be followed as well as American National Standards Institute Safety Standards. All accidents, injuries, claims, or potential claims shall be reported promptly to County.

Add the following new paragraph immediately after paragraph 6.17.E.1:

- SC-6.17.E.2 Contractor/Bidder shall reimburse County for the charges of the County and the County's Consultants for costs generated as a result of more than two submittals of any one Shop Drawing or Sample being required for evaluation due to rejection for noncompliance of the original submittal or lack of information required by the Contract Documents. County's reimbursement for the charges shall be a deduction from Contractor/Bidder's Partial Payment(s).
- SC-6.20.A Amend the first paragraph of 6.20.A of the General Conditions by changing "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court: or arbitration or other dispute resolution costs)" to "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or other dispute resolution costs)".

Add the following new paragraph immediately after paragraph 6.20.A.1:

SC-6.20.A.1 Five percent of the Contract Price is given as consideration for this indemnification.

Add the following new paragraph immediately after paragraph 6.20.C:

SC-6.20.D Neither Contractor/Bidder nor County shall sell, transfer, assign, or otherwise dispose of the contract or any portion thereof, or any right, title, or interest therein, or any obligations thereunder, without written consent of the other party.

ARTICLE 8 COUNTY'S RESPONSIBILITIES

SC-8.02 Amend paragraph 8.02 of the General Conditions by striking out the following words: "to whom Contractor/Bidder makes no reasonable objection."

ARTICLE 9 ENGINEER'S STATUS DURING CONSTRUCTION

Add the following new paragraph immediately after paragraph 9.05.A:

SC-9.05.B Contractor/Bidder shall reimburse the County for the charges of Engineer and Engineer's Consultants for any additional field observations, engineering analysis, correspondence, meetings, or other work due to non-complying or defective construction, materials, or equipment performed or furnished by the Contractor/Bidder, SubContractor/Bidders, or Suppliers. County's reimbursement for the charges shall be a deduction from the Contractor/Bidder's Partial Payment(s).

ARTICLE 10 CHANGES IN THE WORK; CLAIMS

SC-10.05.B Amend the first sentence of paragraph 10.05.B of the General Conditions by changing "(but in no event later than 30 days)" to "(but in no event later than 15 days)".

ARTICLE 11 COST OF THE WORK; CASH ALLOWANCES; UNIT PRICE WORK

Add the following to the end of paragraph 11.01.A.5.c:

- SC-11.01.A.5.c In no case shall rates exceed those published by the current edition of Data Quest Incorporated titled, Rental Rate Blue Book for Construction Equipment, and other procedures established by Florida Department of Transportation.
- SC-11.01.A.5.f Amend the first sentence of paragraph 11.01.A.5.f by striking out the following words: "(except losses and damages within the deductible amounts of property insurance established in accordance with paragraph 5.06.D)".

Add the following new paragraphs immediately after paragraph 11.01.A.5.i:

SC-11.01.A.5.j The cost of specific consideration for the indemnifications set forth in paragraph 6.20.

SC-11.01.A.5.k The cost of compliance with current local, state and federal safety regulations.

Delete paragraph 11.03.D in its entirety

ARTICLE 12 CHANGE OF CONTRACT PRICE; CHANGE OF CONTRACT TIMES

Add the following new paragraph immediately after paragraph 12.02.B:

SC-12.02.C On the 21st of each month, or the next following business day, the Contractor/Bidder shall submit to the County and Engineer a request for weather days. Failure to submit the request forfeits the right to claim weather days for that period and any previous period. The County will grant time extensions, on a day for day basis, for delays caused by the effects of rains or other inclement weather conditions or related adverse soil conditions that prevent the Contractor/Bidder from productively performing controlling items of work resulting in:

(1) The Contractor/Bidder being unable to work at least 50% of the normal work day on pre-determined controlling work items due to adverse weather conditions.

No additional compensation will be made for delays caused by the effects of inclement weather.

ARTICLE 13 TESTS AND INSPECTIONS; CORRECTION, REMOVAL OR ACCEPTANCE OF DEFECTIVE WORK

Add the following to the end of paragraph 13.03.A:

SC-13.03.A Contractor/Bidder shall reimburse County for the charges of Engineer and Engineer's Consultants for all costs due to work not being ready for tests and/or inspections when the Contractor/Bidder has notified Engineer that work is ready for tests and/or inspections. Contractor/Bidder shall reimburse County for all failed tests and subsequent retests. Reimbursement for the charges shall be a deduction from the Contractor/Bidder's Partial Payment(s).

Delete paragraph 13.03.B of the General Conditions and add the following in its place:

SC-13.03.B The Contractor/Bidder shall obtain and employ an independent testing laboratory to provide the services specified herein and shall include all costs for these services in the contract price. The Contractor/Bidder shall submit for approval by the County and Engineer, the independent testing laboratory, including qualifications.

Copies of all testing agency invoices submitted to the Contractor/Bidder for payment shall be forwarded with the Contractor/Bidder's request for partial payment. Invoices shall be submitted routinely throughout the project and shall be pertinent to the partial payment period under consideration. Testing agency invoices in excess of sixty (60) days old shall not be considered for payment, Invoices shall clearly indicate type and amount of test performed, unit and total cost, and shall indicate if the invoiced testing cost is a result of retests required due to the Contractor/Bidder's failure to achieve specified requirements. The cost of retesting due to test failure will be borne by the Contractor/Bidder. Payment to the Contractor/Bidder for testing shall not be made without the required itemized invoicing.

- SC-13.08.A Amend the first sentence of 13.08.A by changing "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs)" to "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or other dispute resolution costs)".
- SC-13.09.C Amend the first sentence of 13.09.C by changing "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs)" to "(including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or other dispute resolution costs)".

ARTICLE 14 PAYMENTS TO CONTRACTOR/BIDDER AND COMPLETION

Delete paragraph 14.02.A.2 in its entirety and insert the following in its place:

SC-14.02.A.2 Beginning with the second Application for Payment, each Application shall include an affidavit of Contractor/Bidder certifying that Contractor/Bidder has disbursed to all subContractor/Bidders and suppliers having an interest in the contract their pro rata shares of the payment out of previous progress payments received by Contractor/Bidder for all work completed and materials furnished in the previous work period, less a retainage withheld by Contractor/Bidder pursuant to an agreement with a subContractor/Bidder. Within 30 days of receipt for the final progress payment or any other payments received thereafter except the final payment, Contractor/Bidder shall pay all subContractor/Bidders and suppliers having an interest in the contract their pro rata shares of the payment for all work completed and materials furnished.

Add the following words to the end of paragraph 14.02.B.1:

"or direct Engineer to present the Application to County with Engineer's recommendation of partial payment."

SC-14.02.B.2 After the word "schedules", add the words "and the Contract Documents".

Add the following new paragraph immediately after paragraph 14.02.B.2.c:

SC-14.02.B.2.d Contractor/Bidder's other obligations under the Contract Documents have been fulfilled.

Amend paragraph 14.09.A.1 to read:

SC-14.09.A.1 A waiver of all Claims by County against Contractor/Bidder, except Claims arising from unsettled Liens, from defective Work appearing after final inspection pursuant to paragraph 14.06, from failure to comply with the Contract Documents or the terms of any special guarantees specified therein whenever said failure occurs or from Contractor/Bidder's continuing obligations under the Contractor/Bidder Documents; and

Add the following new paragraph immediately after paragraph 14.09.A.2:

SC-14.09.A.3 The acceptance of final payment by Contractor/Bidder designated and identified by Engineer as final payment shall be and shall operate as a release to County of all claims and all liability to Contractor/Bidder other than claims in stated amounts as may be specifically excepted by Contractor/Bidder for all things done or finished in connection with the Work and for every act of County and others relating to or arising out of the Work. Any payment, however, final or otherwise, shall not release Contractor/Bidder or Contractor/Bidder's Surety(ies) from any obligations under the Contract Documents or Bonds.

ARTICLE 15 SUSPENSION OF WORK AND TERMINATION

SC-15.02.A. 1 After the word "Contractor/Bidder's", add the words "start the work in accordance with the Notice to Proceed or Contractor/Bidder's".

ARTICLE 16 DISPUTE RESOLUTION

Add the following new paragraph immediately after paragraph 16.01.C.3

SC-16.01.D Venue for any mediation shall be in Nassau County, Florida. Venue for any litigation shall be in state court in Nassau County, Florida.

TECHNICAL SPECIFICATIONS

SECTION 01 11 00

SUMMARY OF WORK

PART 1 THE WORK AND ITS PERFORMANCE

1.1 CHARACTER OF THE WORK

Unless otherwise expressly provided in the Contract Documents, the Work must be performed in accordance with best modern practice, with materials and workmanship of the highest quality to the satisfaction of the County.

1.2 DESCRIPTION OF THE PROJECT

A. The project title is: Stokes Road Bridge Repair over St. Mary's River Bid Number NC19-027 Nassau County, Florida

- B. This project consists of repairing the Stratton Road Bridge over St. Mary's River (Bridge No. 744001) in Nassau County, Florida. Bridge repairs consist of:
 - Repair of spalls and delamination in the slab units.
 - Installation of pile jackets to protect piles at Bents 4 thru 7 from abrasion damage.

All work shall be in accordance with the construction drawings, specifications, and contract documents.

C. The specification divisions and drawings are an integrated part of the contract documents and, as such, will not stand alone if used independently as individual sections, divisions, or drawings sheets. The drawings and specifications establish minimum standards of quality for this project. They do not purport to cover all details entering the design and construction of materials and equipment.

PART 2 WORKING HOURS

2.1 GENERAL

Work under this contract shall not be performed on County, State and/or national holidays or during such events as the Fernandina Beach Shrimp Festival, Nassau County School System FCAT or other events identified at the pre-bid conference, except in time of emergency, and then only under written permission from the County who shall be the sole judge as to the urgency of that situation. It is the responsibility of the contractor to ascertain the exact dates of each of the preceding events. Available workdays to perform work will not include night time work, weekend work, or work before 8:00 am or after 5:00 pm (40 hours per work week).

Should the Contractor deem it necessary to work on Sundays, holidays, or beyond daylight hours in order to comply with his construction schedule or because of an emergency, the Contractor shall request permission of the County. If, in the opinion of the County, the need is bona fide, the contractor will authorize the Contractor to work such hours as may be necessary.

2.2 LANE CLOSURES

Lane closures will be allowed subject to the Nassau County Road Closure Policy in Appendix A.

2.3 ROAD CLOSURES

Bridge may be closed for a total duration of 30 Days and the contractor must follow Road Closure Policy in Appendix A

2.4 REIMBURSEMENT FEES

Should the County approve work time beyond regular hours, the following hourly rates shall be applied as the County's reimbursement of Engineer of Record's fee to be paid by Contractor for expenses defined in Supplemental Conditions SC-6.02.C, SC-6.05.A.2.f, SC-6.17.E., SC-9.05.B and SC-13.03.A.

A. Engineer	\$190.00
B. Project Manager	\$175.00
C. Construction Administrator	\$110.00
D. Inspector	\$95.00
E. Administrative Assistant	\$65.00
F. Consultant Construction Engineering Inspection (CEI)	\$140.00*

*Note the above is estimated rates, the hourly rates will be the actual costs under the CEI contract work authorization executed for this project

PART 3 ABBREVIATIONS

3.1 ORDINANCES, REGULATIONS, STANDARDS, AND CODES

Reference in the specifications to known standards, codes, specifications, etc., promulgated by professional or technical associations, institutions, and societies, is intended to mean the latest edition of each such standard adopted and published as of the date of the Invitation to Bid on this project except where otherwise specifically indicated. Each such standard referred to shall be considered a part of the specifications to the same extent as if reproduced herein in full. The following is a list of applicable documents that apply to this contract.

American Association of State Highway and Transportation Officials (AASHTO) formerly (AASHO)

American Concrete Institute (ACI)

American Institute of Steel Construction (AISC)

American Iron and Steel Institute (AISI)

American National Standards Institute (ANSI)

American Standards Association (ASA)

American Society of Mechanical Engineers (ASME)

American Society of Testing and Materials (ASTM)

American Water Works Association (AWWA)

American Welding Society (AWS)

Anti-Friction Bearing Manufacturer's Association (AFBMA)

Building Officials and Code Administrators International, Inc. (BOCA)

Construction Specifications Institute (CSI)

Federal Specifications (FS)

Florida Department of Transportation (FDOT) Standard Specifications for Road and Bridge Construction, 2019 Edition (Standard Specifications)

Florida Department of Traffic Design Standards 2019 Edition (FDOT Index)

National Bureau of Standards (NBS)

National Electrical Manufacturer's Association (NEMA)

National Fire Protection Association (NFPA)

Portland Cement Association (PCA)

Occupational Safety and Health Act (Public Law 91-596), U.S. Department of Labor (OSHA)

Steel Structures Painting Council (SSPC)

Southern Standards Building Code (SSBC)

Underwriters' Laboratories, Inc. (UL)

United States of America Standards Institute (USASI)

Regulations of Florida Industrial Commission Regarding Safety

All local, state, county, or municipal building codes requirements of the Owner's Insurance

SECTION 01 22 50

MEASUREMENT AND PAYMENT

PART 1 GENERAL

Work under this Contract shall be paid as designated below under the appropriate items associated with the Bid Schedule. Payment shall be in accordance with Lump Sum or Unit Price bid by the Contractor in his proposal.

When Lump Sum prices are contained in the Bid Schedule, the Contractor shall provide a detailed schedule of values for Lump Sum cost acceptable to the Engineer of Record and the County, which will be used for estimating partial payment requests.

Contractual costs for work not specifically mentioned under a payment item and which are incidental to the overall conduct of the work shall be included in the individual items at the Contractor's option. No additional charges shall be made to the County for items not specifically mentioned under individual payment items. Examples of these types of costs include, but are not limited to, the following: bonds, insurance, permits, licenses, traffic control, dust control, clean-up, temporary access, temporary facilities, soil erosion control, temporary drainage, temporary offices, restoration of disturbed areas, temporary utilities, test pits locating existing utilities, temporary water and sewer, surveying, layout, and other items similar to above.

Measurement and payment for all items shall be in accordance with the FDOT Standard Specifications for Road & Bridge Construction 2019 Edition with the exception that reduction in the FDOT acceptance criteria based on payment factors will not be allowed.

PART 2 BID SCHEDULE ITEMS

Item 1. Mobilization

- A. Measurement and Payment for Mobilization shall be in accordance with Section 101 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition.
- B. Payment will be made under Item No. 101-1 Mobilization, on a lump sum basis.

Item 2. Maintenance of Traffic

- A. Measurement and Payment for Maintenance of Traffic shall be in accordance with Section 102 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition.
- B. Payment will be made under Item No. 102-1 Maintenance of Traffic, on a lump sum basis and includes and not limited to Item No. 102-60 for Work Zone Signs, Item No. 102-74-1 and Item

No. 102-74-2 for Channelization Devices, Item No. 102-77 for High Intensity Flashing Lights and Item No. 102-99 for Portable Changeable Message Signs.

Item 3. Erosion and Sediment Control

- A. Measurement and Payment for Turbidity Barrier shall be in accordance with Section 104 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition. (As modified in Section 32 12 04 of these documents.)
- B. Payment will be made under Item No. 104-11 Turbidity Barriers, on a per foot basis.

Item 4. Restore Spalled Area, Portland Cement Grout

- A. Measurement and Payment for the Restore Spalled Area, Portland Cement Grout shall be in accordance with Technical Special Provision T401-1.
- B. Payment will be made under Item No. 401-70-4 Restore Spalled Area, Portland Cement Grout, on a Cubic Feet (CF) basis.

Item 5. Standard Integral Pile Jacket, Non-Structural, Up to 16"

- A. Measurement and Payment for the Standard Integral Pile Jacket shall be in accordance with Section 457 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition - Special Provisions for Integral Pile and Column Jackets.
- B. Payment will be made under Item No. 457-1-11 Removal of Existing Structures, on a Linear Foot (LF) basis.

SECTION 01 31 19

PROJECT MEETINGS

1.1 PRECONSTRUCTION CONFERENCE

- A. A preconstruction conference will be scheduled after award of contract and prior to beginning work. This meeting shall be attended by Engineer of Record, the County, and an authorized representative of Contractor.
- B. Meeting will consider matters of contract administration and initial construction operations.
- C. Contractor shall submit proposed construction schedule prior to or at preconstruction conference; see Section 01 33 00.

1.2 PROGRESS MEETINGS

- A. Periodic progress meetings will be held at a time and place mutually agreed upon at preconstruction conference. A responsible representative of Contractor who can bind Contractor/subcontractor to decisions shall attend. A responsible representative of other subcontractors working on site shall also attend.
- B. Meetings will be held to coordinate and expedite progress of work and shall be conducted by Contractor. Contractor and each subcontractor on site shall submit a written report at each meeting indicating:
 - 1. Work progress since last meeting.
 - 2. Upcoming work sequences and schedules.
 - 3. Requests for information.
- C. Contractor shall record meeting minutes and shall distribute a written summary of items discussed to all parties involved in the project within 48 hours of each meeting. The written summary shall document all issues discussed and decisions reached at progress meeting.

SECTION 01 33 00

SUBMITTAL PROCEDURES

1.1 SUMMARY

A. Submit items to Engineer of Record for review as listed below and as required by the other Contract Documents. Refer to individual specification sections, General Conditions, Supplementary Conditions, and sections of Division 01 - General Requirements for submittal requirements.

1.2 CONSTRUCTION SCHEDULE

- A. Prior to or at preconstruction conference, submit two copies of a proposed schedule of operations. Coordinate activities of the various trades for orderly completion of the work. Coordinate activities with those of the County to schedule a minimum of temporary disruptions to continuing operations. Allow ample time for the County to alter operations as required.
- B. After acceptance of construction schedule, distribute copies to subcontractors and other parties required to comply with scheduled dates.
- C. When revisions to schedule are made, notify all parties of changes in writing.

1.3 SCHEDULE OF SUBMITTALS

- A. Within 10 days of acceptance of construction schedule, submit two copies of a schedule of submittals. Schedule shall list anticipated date for each required submittal and shall allow A/E reasonable time for reviews. Submit all submittals requiring Engineer of Record review within 30 days of acceptance of construction schedule.
- B. After acceptance of schedule of submittals, distribute copies to subcontractors and other parties required to comply with submittal dates.

1.4 SHOP DRAWINGS

A. Required shop drawings are designated under the various specification sections. Submit shop drawings for review prior to fabrication, delivery, or installation. Submit a minimum of five copies; two copies will be retained, and the remainder returned to Contractor who shall keep one copy at project site.

- B. Fabrication and erection drawings may consist of a reproducible and two sets of prints; the reproducible copy will be returned to Contractor.
- C. Each brochure of shop drawings shall contain an index of contents and shall consist of layout details, schedules, setting instructions, manufacturer's literature, and other data specifically prepared for the work. Shop drawings shall be identified with project name, numbered consecutively, and bear the stamp of approval of Contractor as evidence of accuracy, compatibility, and conformance with contract requirements. Drawings not so stamped will be returned without being examined.
- D. Specific written notice shall be given of each variation that shop drawings may have from requirements of the Contract Documents.
- E. Partial submittals will not be considered; each portion of work shall be complete in one submittal.
- F. Shop drawings shall not be used in the work unless they have been reviewed and bear the stamp and signature of Engineer of Record. Shop drawings will only be reviewed for general conformance with the design concept of the project and general compliance with the information given in the Contract Documents. Contractor shall be responsible for confirming and correlating all quantities and dimensions, selecting fabrication processes and techniques of construction, coordinating his or her work with that of all other trades, and performing all work in a safe and satisfactory manner. Corrections or comments made on shop drawings shall not relieve Contractor from compliance with requirements of Drawings and Specifications and shall not be considered an order for extra work.
- G. If information on previously reviewed shop drawings is altered, submit changes for review.

1.5 PRODUCT DATA

- A. Required product data submittals are designated under the various specification sections. Submit product data for review in accordance with procedures for shop drawings.
- B. Product data shall consist of manufacturer's literature, illustrations, and brochures of catalog cuts; instructions for handling, storage, and installation; and specifications and design data. Where multiple options are indicated, identify specific options as required for this project.

C. Products subject to product data review shall not be used in the work until they have been reviewed and bear the stamp and signature of Engineer of Record.

1.6 SAMPLES

- A. Prior to fabrication, delivery, or installation, submit samples as designated in the various specification sections; allow reasonable time for review and testing.
- B. Submit samples in sufficient quantity and of adequate size to show quality, type, and extremes of color range, finish, and texture. Submit a minimum of two sets of appearance and color samples. Label each sample stating material, description, project name, and Contractor's name. Expedite submittal of appearance and color samples following Notice to Proceed.
- C. Submit samples with transmittal letter requesting review; prepay transportation charges Samples shall become the County's property, unless otherwise designated.
- D. Samples will be reviewed for acceptability or selection of color, pattern, and texture only Compliance with specifications is the responsibility of Contractor.
- E. Order no materials subject to sample review until receipt of written notice of completion of review. Installed materials shall match reviewed samples. No review of samples shall be taken to change contract requirements.

1.7 CERTIFICATES OF COMPLIANCE

- A. Submit two copies of certificates of compliance as designated in the various specification sections.
- B. Certificates shall be furnished by manufacturer, producer, or supplier of material or product and shall indicate that material or product conforms to or exceeds specified requirements. Include supporting reference data as appropriate. Certificates may be recent or previous test results on material or product but must be acceptable to Engineer of Record.

1.8 PERMITS AND APPROVALS

A. Submit one copy of permits, code inspections, and agency approval documents, as designated in the various specification sections.

1.9 TEST REPORTS

A. Submit two copies of test reports as designated in the various technical specifications.

1.10 PROJECT RECORD DOCUMENTS

A. Keep a current set of documents at job site that are marked to show all changes made during construction. Dimension underground and concealed work and utilities from permanent reference points; record vertical distances. Submit project record documents upon completion of Work.

Contract CM2831

SECTION 01 41 23

PERMITS AND FEES

PART 1 - GENERAL

1.1 DESCRIPTION

- A. Contractor responsibilities: Obtain and pay for all other permits and licenses required by authorities having jurisdiction, including but not limited to: land clearing permit, NPDES Notice of Intent and dewatering permit if required.
- B. Contractor shall be responsible to adhere to all provisions, requirements, and cost contained in all permits applicable to this project.

PART 2 - PRODUCTS (NOT USED)

PART 3 - EXECUTION (NOT USED)

SECTION 01 45 00

QUALITY CONTROL

PART 1 GENERAL

1.1 CONTRACTOR QUALITY CONTROL PLAN

The Contractor is responsible for his own quality control and must comply with FDOT Specifications Section 105 Contractor Quality Control General Requirements. Nassau County will act as the Department in all issues relating to Quality Control.

1.2 SECTION INCLUDES

Certification and testing, examination by the County, quality assurance testing, and final approval or work.

1.3 CERTIFICATION AND TESTING

The materials and equipment used in the construction of the project shall be subject to adequate certification and testing in accordance with generally accepted standards, as required and defined in the Contract Documents.

1.4 CONTRACTOR TO PROVIDE

The Contractor shall provide all tools, testing apparatus, materials to be tested, and labor as necessary to provide certification required by the Contract Documents.

1.5 OUTSIDE AGENCY

If the Contract Documents, laws, ordinances, rules, regulation or orders of any pubic authority having jurisdiction require any work to be certified, tested, or approved by someone other than the County, the Contractor will give the Engineer of Record timely notice of readiness. The Contractor will then furnish the County the required certification and/or testing certificates for approval.

1.6 LIMIT OF APPROVALS

Certifications, tests, or approvals by the County, Engineer of Record, or others shall not relieve the Contractor from his obligations to perform the work in accordance with the requirements of the Contract Documents.

Contract CM2831

1.7 ACCESS TO WORK SITE

The County and his representative will at all times have access to the work. In addition, authorized representatives and agents of any participating federal or state agency shall be permitted access to all work, materials, payrolls, records of personnel, invoices of materials, and other relevant data and records. The Contractor will provide proper facilities for such access and observation of the work.

PART 2 EXAMINATION BY THE COUNTY

2.1 ACCESS

The County contemplates, and the Contractor agrees to thorough examination of the work at all times by the County and the Engineer of Record, including all labor performed and materials furnished, delivered, or intended to be used in the work, including manufacture, preparation, and testing. The Contractor shall not use any material which has not been tested and accepted. The Contractor shall keep the Engineer of Record advised of the progress of the work away from the site requiring certification of witnessing of tests to ensure that scheduling conflicts or delays do no develop.

2.2 ACCEPTANCE TESTS

Tests, or acceptance of any materials prior to shipment, shall not be deemed as a final acceptance of the materials. The County may require tests or analysis of any portion of the materials at any time. Any material which is found to be defective or which does not otherwise conform to the requirements of the specifications shall be rejected and removed forthwith from the site, as provided in the contract.

2.3 RIGHT TO EXAMINE WORK

The County and the Engineer of Record shall have the right to examine all materials and work done during any phase of construction, fabrication, or manufacture. The Contractor shall furnish all reasonable facilities and aid to the Engineer of Record and safe and convenient means for the examination of any part of the work. No work shall be closed or covered until it has been duly examined and approved.

PART 3 QUALITY ASSURANCE TESTING

3.1 DESCRIPTION

The Contractor is required to provide all testing as described in these specifications. Testing shall be completed by an independent testing laboratory retained by the Contractor and approved by the Engineer of Record. The Contractor is required to submit independent testing laboratory qualifications. Certifications, tests, or approvals by the County, Engineer of Record, or others shall not relieve the

Contractor from his obligations to perform the Work in accordance with the requirements of the Contract Documents.

3.2 CODES AND REGULATIONS TESTING

Testing will be in accordance with all pertinent codes and regulations and with selected standards of the American Society of Testing and Materials. The Engineer of Record shall process and distribute all required copies of test reports and related instruction to ensure all necessary retesting and/or replacement of materials with the least possible delay in progress of work.

3.3 RETESTING

When initial quality assurance tests indicate noncompliance with the Contract Documents, all subsequent retesting occasioned by the noncompliance shall be performed by the same testing laboratory and the costs thereof shall be borne by the Contractor.

3.4 COOPERATION WITH THE COUNTY'S TESTING LABORATORY

The County may perform any additional tests that he may deem necessary at his own expense. Representatives of the County's testing laboratory shall have access to the work at all times. The Contractor shall provide facilities for such access in order that the laboratory may properly perform its functions.

3.5 ADDITIONAL TESTING

If the County orders sampling, analysis, or tests of materials which are specified to be accepted on certification by the manufacturer, but which appear defective or not conforming to the requirements of the specifications, the Contractor shall bear all the costs of sampling, transportation, tests, and analyses if the material is in fact found defective or does not conform to the specifications. If the material is found to be sound and conforming to the specifications, the County will pay for the testing.

PART 4 FINAL APPROVAL

4.01 FINAL APPROVAL

Final approval of the Work shall be made by the County and the Engineer of Record shall be contingent upon the findings of a thorough examination of the Work. Such examination shall be made within ten (10) working days after receipt of the Contractor's written request. The Work will be accepted and deemed completed as of the date of such examination if, upon such examination, the Engineer of Record and the County find that no further Work remains to be done at the site. If the examination reveals items of Work still to be performed, the Contractor shall promptly perform them and request a re-examination. If upon any reinspection the Engineer of Record and the County determine that the Work is complete, the date of completion shall be deemed to be the actual date of such reexamination.

SECTION 01 50 00

TEMPORARY FACILITIES AND CONTROLS

1.1 TEMPORARY ELECTRICITY

A. Contractor shall provide temporary electric service and distribution facilities as required for its own construction purposes. Provide portable power supply or make arrangements with local utility company for temporary service including service poles, driven ground, main service switch, transformer, and metering facilities. Pay for electrical energy consumed.

1.2 TEMPORARY LIGHTING

A. Contractor shall provide temporary lighting sufficient to enable its workers to complete work and to enable inspectors to check work, as required.

1.3 TEMPORARY WATER

A. Contractor shall be responsible for obtaining water for its needs. Pay cost of water used and meter rental, if applicable.

1.4 TEMPORARY SANITARY FACILITIES

A. Contractor shall provide temporary outside toilets sufficient for its own workers.

1.5 TEMPORARY FIRE PROTECTION

A. Contractor shall provide fire extinguishers and other fire protection equipment for all possible classes and types of fire.

1.6 PROTECTION OF WORK AND PROPERTY

- A. Observe safety provisions of applicable laws and regulations.
- B. Erect and maintain all required planking, barricades, guardrails, fences, safety lanterns, and temporary walkways of sufficient size, strength, and type necessary for protection of material storage, adjacent property, and new construction, as well as to prevent accidents to public and workers at job site.
- C. Notify the County if existing property interferes with work so that arrangements for proper protection can be made.

- D. Protect all work, materials, apparatus, and fixtures incorporated in work or stored on site against damage. At end of day, cover all new work likely to be damaged.
- E. Protect all finished construction until acceptance by the County. Repair damage to finished work to satisfaction of the County.

1.7 ENVIRONMENTAL CONTROLS

- A. Maintain erosion control measures to protect the project site and prevent sediment pollution of adjacent water courses and properties.
 - 1. Install erosion control measures prior to start of construction and maintain them until final completion of work. Unless otherwise instructed, remove temporary erosion control measures prior to final application for payment.
 - 2. Strive to limit stripping of sod and vegetation to a period that will expose bare soil to the least possibility of erosion that construction requirements allow.
 - 3. Construct and maintain silt fence barriers, erosion bale barriers, or temporary diversions to receive runoff leaving site.
 - 4. Protect storm drain inlets by using silt fence barriers, erosion bale barriers, or equivalent.
 - 5. Remove at the end of each work day soils and sediment reaching public or private streets not part of the construction site.
 - 6. Unless otherwise shown or specified, erosion control measures shall comply with the planning, design, and maintenance provisions of Section 104 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition and Index Nos. 102 and 103 in the 2019 Roadway and Traffic Design Standards Manual.
- B. Provide controls to confine dust and dirt within project area. Thoroughly soak masonry and debris during demolition and loading operations. Water exposed soils or aggregates as required to prevent windblown dust.
- Provide noise control measures to limit the amount of noise and prevent nuisance.
 Properly equip all equipment with mufflers. Limit construction activities generating significant noise to normal working hours.

1.8 TRAFFIC CONTROL

A. Conduct operations to ensure minimum interference with streets, driveways, walks, and adjacent facilities not part of construction project.

B. Do not close or obstruct streets, walks, or other occupied or used facilities without permission from authorities having jurisdiction. Provide alternate routes around closed or obstructed traffic ways if required by governing regulations.

1.9 CONSTRUCTION CLEANING

- A. Remove rubbish and debris from work area promptly upon its accumulation. Perform a broom cleaning of all appropriate surfaces weekly.
- B. Immediately clean-up spillages of oil, grease, or other liquids which could cause a slippery or otherwise hazardous situation or stain a finished surface.
- C. Form or scrap lumber shall have all nails withdrawn or bent over and shall be stacked, placed in trash bins, or removed from site.
- D. At completion of project, thoroughly clean, sweep, and wash work to remove foreign matter, spots, and soil from work and equipment under this contract. Remove temporary guards and protective coatings.

1.10 DISPOSAL

- A. Provide industrial type waste containers in number and size required or provide other acceptable methods of disposing of debris. Place containers at adequate locations to handle debris and have them emptied as required.
- B. No burning of rubbish or debris will be allowed at site.
- C. Store combustible waste in fire-resistive containers. Store hazardous wastes, such as caustics, acids, and harmful dusts, in appropriate covered containers. Dispose of wastes regularly.
- D. If a contractor does not remove rubbish or clean work as specified above, the County reserves right to have work done by others at Contractor's expense.

SECTION 01 55 26

TRAFFIC CONTROL

PART 1 - GENERAL

1.1 DESCRIPTION

A. This Section covers procedures for developing and implementing traffic control and regulation measures and maintenance of traffic in and around the construction area to provide for safe and efficient protection and movement of vehicular and pedestrian traffic/through and adjacent to the construction site areas.

1.2 REFERENCE STANDARDS

- A. General
 - Codes, specifications, and standards referred to by number or title shall form a part of this Specification to the extent required by the reference thereto. Latest revisions shall apply, unless otherwise shown or specified.
- B. Florida Department of Transportation (FDOT) Standards:
 - 1. USDOT Manual on Uniform Traffic Control Devices.
 - 2. FDOT Manual of Traffic Control and Safe Practices for Street and Highway Construction, Maintenance and Utility Operations.
 - 3. FDOT Standard Specifications for Road and Bridge Construction, 2019 Edition.
- C. Nassau County Standards:
 - 1. Nassau County Road Closure Policy

1.3 SUBMITTALS

A. Before closing or restricting traffic flow through any thoroughfare, the Contractor shall give written notice to and, if necessary, obtain a permit or permits from the duly constituted public authority having jurisdiction over the thoroughfare. Contractor shall also notify the applicable law enforcement, fire, and emergency services having jurisdiction in the area. Notice shall be given no less than seventy-two (72) hours in advance of the time when it may be necessary in the process of construction to close or restrict traffic to such thoroughfare, or as may be otherwise required by the governing authority.

Contract CM2831

- B. For any road or lane closures on this project, Contractor shall refer to the Nassau County Road Closure Policy and contact Nassau County Engineering Services Department at (904) 530-6225.
- C. A Lane closure notice will be placed in the newspaper one month prior and one week prior to the closure to give residents notice that the bridge will be closed. VMB's will be up two weeks prior to the closure. Two weeks prior notice will be given to the Nassau County residents that reside on Stokes Road with a return receipt certified mail letter that the road will be closed at various times throughout the next month, in addition to any other notifications required in the Nassau County Road Closure Policy. Each notice shall include, at a minimum, the dates of the bridge closure, the detour, and the name and contact phone number for the contractor's representative, should the residents have any questions or concerns. Each time the road is fully closed, and the detour will need to be utilized, a notice will be placed in the newspaper. The notice shall also be given to the necessary departments, as per the Nassau County Road Closure Policy.

1.4 SITE CONDITIONS

- A. The Contractor shall plan construction operations such that existing local traffic access can be maintained and shall be maintained during the construction using such barricades, lights, flagmen, and other protective devices as appropriate, whether specified for the project or required by the local governing authority. Traffic control devices and implementation used for maintenance of traffic shall comply with the FDOT Manuals and the Nassau County Road Closure Policy.
- Β. The Contractor shall conduct his work in such manner as not to unduly or unnecessarily restrict or impede normal traffic through the streets of the community. Insofar as it is practicable, excavated material and spoil banks shall not be located in such manner as to obstruct traffic. The traveled way of all roads shall be kept clear and unobstructed insofar as is possible and shall not be used for the storage of construction materials, equipment, supplies, or excavated earth, except when and where necessary. If required by duly constituted public authority, the Contractor shall, at his own expense, construct bridges or other temporary crossing structures over trenches so as not to unduly restrict traffic. Such structures shall be of adequate strength and proper construction and shall be maintained by the Contractor in such manner as not to constitute an undue traffic hazard. Private driveways shall not be closed except when and where necessary, and then only upon due advance notice to the County, property owner and applicable jurisdictional authority, and shall be for the shortest practicable period of time consistent with efficient and expeditious construction. The Contractor shall be liable for any damages to persons or property resulting from his work.
- C. The Contractor shall make provisions at cross streets for the free passage of vehicles and foot passengers, either by bridging or otherwise, and shall not obstruct the swales nor prevent in any manner the flow of water in the swales but shall use all proper and necessary means to permit the free passage of surface water in the swales. The Contractor shall immediately cart away all offensive matter, exercising such

precaution as may be directed by the County or applicable jurisdictional authority. All material excavated shall be so disposed of as to inconvenience the public and adjacent tenants as little as possible and to prevent injury to trees, sidewalks, fences, and adjacent property of all kinds. The Contractor may be required to erect suitable barriers to prevent such inconvenience or injury.

D. Unless otherwise required by the governing authority, maintenance of traffic in and around the construction zone shall conform to Section 102 of the FDOT Specification,600 Series Roadway Design Standards drawings of the FDOT Standards, and Manual on Uniform Traffic Control Devices (MUTCD) latest edition, as applicable.

PART 2 - PRODUCTS (NOT USED)

PART 3 - EXECUTION (NOT USED)

SECTION 01 60 00

PRODUCT REQUIREMENTS

1.1 PRODUCTS

A. Provide new, high quality products manufactured and conditioned for the particular application as recommended by manufacturer, unless otherwise noted. Transport, handle, store, and protect products as specified and in accordance with manufacturer's recommendations.

1.2 MANUFACTURER'S DIRECTIONS

A. Wherever work is to be performed or products are to be installed in accordance with manufacturer's instructions, furnish copies of printed instructions before installation.

1.3 SOURCE OF PRODUCTS

A. In order that ready availability of materials, parts, or components for repair, replacement, or expansion can be assured, original equipment and components shall be obtained where feasible from domestic sources which maintain a regular stock.

1.4 ACCEPTABLE MANUFACTURERS

A. Products, materials, and equipment identified by reference to a manufacturer's name, catalog number, or model are identified for the purpose of establishing a standard of quality, type, and function. Products first named in specifications are depicted for general descriptive purposes only. Any other product, material, or equipment which will perform adequately the duties imposed by the general design will be considered for substitution in accordance with the provisions below.

1.5 OPTIONS AND CHANGES

- A. Wherever options consisting of two or more choices are permitted for any product, procedure, or method, Contractor may select any of the named alternatives.
- B. Changes and revisions to Contract Documents may be made by Change Order, Field Order, or other procedure authorized under the Contract Documents.
- C. All other revisions not defined as options or changes shall be treated as Substitutions. (Options and changes will not be treated as Substitutions.)

1.6 BID PHASE SUBSTITUTIONS

A. Substitutions and alternatives proposed prior to the Bid Deadline shall be submitted in accordance with the Instructions to Bidders.

1.7 CONSTRUCTION PHASE SUBSTITUTIONS

- A. Substitutions proposed after Contract has been awarded shall be submitted for approval prior to their use. Consideration will be given only to proposed substitutions for those products named in the Contract Documents which are no longer available or cannot be provided within the Contract Time, or where standard products are no longer in conformance, or where the County's interests may be adversely affected.
- B. If substitutions are approved, Contractor assumes responsibility for any other changes in systems or for modifications required in other work to accommodate the substitution, regardless of approval of the substitution.
- C. Requests for substitution of alternate products shall be submitted with complete references to manufacturer's product identification and product data indicating composition, guarantee, availability, applicable standards or agency approvals met or exceeded, restrictions imposed on product, and manufacturer's recommended method of application or installation. Substitutions will be considered acceptable if the product will perform adequately the duties imposed by the general design and, in opinion of Engineer of Record, is of equal substance, quality, appearance, and function, unless the named item is necessary for interchangeability or if the named product has been demonstrated to be most cost-effective.

1.8 DEFECTIVE PRODUCTS

A. All products which do not conform to specified requirements shall be considered defective and shall be removed from the Work. If in place, faulty materials shall be corrected or replaced to meet specified requirements.

1.9 TRANSPORTATION AND HANDLING

- A. Products shall be transported and handled in accordance with the Contract Documents and as defined below. Deliver in original packaging with manufacturer's brand, seals, and labels intact. Refer to individual sections of specifications for specific requirements.
- B. Arrange for product transportation as required for construction. Select means of transportation which will reasonably assure timely and safe arrival. Products shall be suitable for intended use upon arrival at the project and shall be undamaged and free from defects.
- C. Select appropriate methods for handling products to preserve their integrity, quality,

and function.

1.10 MATERIAL PROTECTION

- A. Protect materials in accordance with Section 01 50 00, specific requirements of individual sections of specifications, and according to manufacturer's recommendations.
- B. Provide and maintain watertight storage sheds with raised floors for storage of products that might be damaged by weather. Cement, lime, and other materials affected by moisture shall be stored on platforms.

1.11 STORAGE

- A. Confine storage of products to limits designated by the County. Do not bring products to site until needed for progress of work. Storage of products within buildings shall not exceed design capacity of structural system.
- B. The County assumes no responsibility for products stored on site. Contractor shall assume full responsibility for damage to stored products, except as covered by property insurance for the work under construction (see General and Supplementary Conditions).
- C. Contractor shall allot space to subcontractors for storage of products and erection of offices and tool sheds. Locate storage buildings, temporary sheds, and stockpiles to avoid interference with new and existing facilities; move sheds, storage platforms, and materials as necessary.
- D. Upon completion, restore areas disturbed by construction.

SECTION 01 71 23

FIELD ENGINEERING

PART 1 - GENERAL

1.1 SECTION INCLUDES

A. Provide field engineering service for project as indicated on Drawings and specified in this Section.

1.2 QUALIFICATIONS OF SURVEYOR OR ENGINEER

A. Florida Registered Engineer or Land Surveyor.

1.3 SURVEY REFERENCE POINTS

- A. Existing basic horizontal and vertical control points are designated on Drawings. All elevations are based on the benchmarks shown on the plans. Establish all vertical and horizontal controls required for construction.
- B. Locate and protect control points prior to starting site work and preserve permanent reference points during construction.
 - 1. Make no changes or relocations of such points without prior written notice to Engineer of Record and the County.
 - 2. Report to Engineer of Record and the County when any reference point is lost or destroyed or requires relocation because of necessary changes in grades or locations.
 - 3. Require surveyor to replace control points which may be lost or destroyed Establish replacements based on original survey control.
 - 4. Engineer of Record will identify existing control points and properly line corner stakes indicated on Drawings, as required.
 - 5. Elevations are based on the National Geodetic Vertical Datum of 1988.

1.4 PROJECT SURVEY REQUIREMENTS

- A. Establish a minimum of two (2) permanent bench marks on the project site, all referenced to data established by survey control points. Record locations, with horizontal and vertical data, on Project Record Documents.
- B. Establish lines and levels, locate and lay out, by instrument and similar appropriate

means.

- 1. Site improvements.
- 2. Controlling lines and levels required for mechanical and electrical trades.
- C. Verify layouts by same methods from time to time.

1.5 RECORDS

- A. Maintain a complete, accurate log of control and survey work as it progresses.
- B. On completion of foundations and major site improvements, prepare a certified asbuilt survey showing finished dimensions, locations, angles and elevations of construction.
- C. Refer to Nassau County's As-Built Checklist.

1.6 SUBMITTALS

- A. Submit name and address of surveyor or professional engineer to Engineer of Record and the County.
- B. On request of Engineer of Record and the County, submit documentation to verify accuracy of field survey work.
- C. Submit certificate signed and sealed by a State of Florida Registered Engineer or Land Surveyor certifying that elevations and locations of improvements are in conformance with Contract Documents.

PART 2 - PRODUCTS (NOT USED)

PART 3 - EXECUTION (NOT USED)

SECTION 01 77 00

CLOSEOUT PROCEDURES

1.1 SUMMARY

A. Complete closeout procedures and final submissions as listed below and as required by the other Contract Documents. Refer to General Conditions regarding Substantial Completion, final completion, and final payment.

1.2 FACILITY START-UP

A. Submit test reports before requesting certification of Substantial Completion.

1.3 SUBSTANTIAL COMPLETION

- A. Contractor shall notify Engineer of Record when it considers the Work (or a portion of the Work which the County agrees to accept separately) to be substantially complete. Contractor's notice shall include a comprehensive list of items to be completed or corrected prior to final payment. Additionally, the Contractor shall submit preliminary as-builts conforming to the as-built check list and signed and sealed by a registered surveyor.
- B. Upon receipt of Contractor's list, Engineer of Record, the County, and Contractor shall make an inspection to verify that the Work is substantially complete.
 - 1. If the County considers the Work to be substantially complete, the County will issue a Certificate of Substantial Completion along with a "Construction Acceptance Checklist" of items to be completed or corrected prior to final payment. Items on punch list shall be completed within 30 days. Required submittals (see below) shall be completed prior to or when requesting final payment.
 - 2. If the County does not consider the work to be substantially complete, the County will inform Contractor of items that need to be completed or corrected before substantial completion. Contractor shall promptly complete these items and request a reinspection by the County.

1.4 FURNISHED PRODUCTS AND LOANED TOOLS

A. Prior to final payment, return all extra materials, unused parts, and equipment furnished by the County; return loaned tools and equipment.

1.5 FINAL COMPLETION

- A. Contractor shall notify Engineer of Record and the County when it considers all Work to be complete. Engineer of Record, the County, and Contractor shall make an inspection to verify that the Work is complete.
 - 1. If the County considers the Work to be complete, Contractor shall submit final Application for Payment.
 - 2. If the County does not consider the Work to be complete, the County will inform Contractor of items that need to be completed or corrected before completion. Contractor shall promptly complete these items and request a reinspection by the County.
- B. Prime Contractor is responsible for reviewing all Construction Acceptance Checklist items and verifying that each item is complete before requesting final inspection.

1.6 CHARGES FOR REINSPECTIONS

A. The County will inspect the Work (or a portion of the Work which the County agrees to accept separately) at substantial completion and at final completion. If the Work is not complete to the required level at either substantial completion or final completion, and a re-inspection is required, Contractor shall reimburse the County for charges of the County and the County's consultants for performing the re-inspection.

1.7 SUBMITTALS

- A. Submittals required before Contract Closeout are listed below:
 - 1. Contractor Lien Waiver
 - 2. Subcontractor Lien Waiver
 - 3. Consent of Surety to Final Payment
 - 4. Compliance with all permits and other governmental agencies
 - 5. Certification of Inspections "Certification Package"
 - 6. Warranties and Bonds
 - 7. As-Built Drawings (Final)
 - 8. Operation and Maintenance Manuals
 - 9. All other documents as required in the Contract Documents.

Contract CM2831

DIVISION 32

EXTERIOR IMPROVEMENTS

Mobilization

PART 1 GENERAL

1.01 SUMMARY

A. Mobilization shall be in accordance with Section 101 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition, including Supplemental Specifications.

Maintenance of Traffic

PART 1 GENERAL

1.01 SUMMARY

A. Maintenance of Traffic shall be in accordance with Section 102 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition, including Supplemental Specifications and includes Work Zone Signs, Channelization Devices, High Intensity Flashing Lights, and Portable Changeable Message Signs.

SITE PREPARATION

PART 1 GENERAL

1.01 SUMMARY

- A. Provide site preparation as shown and as specified. Comply with applicable provisions of Div. 00 and 01.
- B. Work includes, but is not limited to:
 - 1. Protection of improvements, plants, and utilities.
 - 2. Removal and replacement of improvements.
 - 3. Location of utilities and coordination with utility companies.
 - 4. All clearing and grubbing of trees and vegetation.
 - 5. Topsoil salvage.

1.02 MEASUREMENT AND PAYMENT

- A. Site preparation will be considered incidental to the work except where separate pay items are included in Bid Schedule.
- B. Drawing notes related to removals and replacements shall be interpreted as directives to Contractor for such work at no extra cost except where separate pay items are provided in Bid Schedule.

PART 2 (NOT USED)

PART 3 EXECUTION

3.01 PROTECTION

- A. Protect improvements on site and on adjoining properties. Provide barricades, coverings, or other types of protection as necessary to prevent damage and to safeguard against injury. Restore to original condition improvements damaged by the work or improvements which required temporary removal during construction.
- B. Protect existing vegetation indicated to remain against unnecessary cutting, breaking, bruising, or smothering by stockpiling excavated materials or parking of vehicles within drip line. Provide temporary fences, tree wells, barricades, or guards; repair or replace trees and vegetation damaged by construction operations.
- C. Protect survey monuments, reference points, and benchmarks from movement. Should removal be necessary, notify Engineer of Record and the County who will give notice for removal at Contractor's expense. Contractor shall pay cost for re-establishing monuments lost due to its negligence or failure to notify Engineer of Record and the

County.

D. No extra payment or time will be allowed for protection work that could have been suspected or anticipated by site inspection and interpretation of bidding documents prior to execution of contract.

3.02 UTILITIES

- A. Location and description of underground utilities and structures shown on drawings are approximate and are based on records available to the County or surface features indicating their existence. There may be other utilities within project area that are not shown.
- B. Notify all affected utility companies of construction operations at least three working days before beginning work near their facilities. Do not begin excavation work until underground utility locations have been marked.
- C. Use caution when excavating so that exact location of underground utilities, both known and unknown, may be determined. Provide adequate protection and support for utilities during construction operations.
- D. If uncharted or incorrectly charted utilities are encountered during excavation work, or if proposed construction conflicts with existing utilities, give prompt notice and submit proposed solution to Engineer of Record and the County for approval. If required, make arrangements with utility companies for relocation of interfering utilities. No extra cost or time will be allowed for unexpected delays or coordination work, except for authorized alterations as follows. When a change is permitted to avoid a utility relocation, Engineer of Record and the County will determine whether such change constitutes extra work. Underground utilities and structures located outside of construction limits which Contractor wishes to have moved to facilitate construction shall be arranged with each owner of such facilities; Contractor shall pay all costs of such relocations for convenience.
- E. During construction of pipe lines, it may be necessary to cross under certain underground utilities and structures. Prevent damage to such facilities. Where necessary, divert flow in drains or culverts so that trenches are kept dry during work. Deposit and compact sand or gravel bedding and backfill around exposed facilities by mechanical means in layers not to exceed 6 in. Wherever such facilities are disturbed or broken, restore them to good condition at no additional cost to the County.

3.03 SITE CLEARING

- A. Remove trees, stumps, snags, shrubs, brush, heavy growths of grass, weeds and other vegetation, improvements, rubbish and debris, and obstructions that interfere with proposed construction; remove items only as necessary for completion of work.
- B. Cut brush and vegetation flush with ground. Grub out stumps, roots having a diameter of 2 in. or larger, and root clusters to a depth of at least 2 ft below subgrade elevation for pavements, structures, and embankments and 6 in. below ground surface in other

areas.

C. Carefully and cleanly cut roots and branches of trees indicated to be left standing, where such roots and branches obstruct new construction. Cut back roots a minimum of 1 ft from concrete work, paving, and structures and to a depth of not less than 2 ft below structures, foundations, and embankments.

3.04 TOPSOIL STRIPPING

- A. Topsoil shall include all friable, fertile, loam soil suitable for grass and plants, found at surface to a depth of approximately 4 in., reasonably free of subsoil, clay lumps, stones, objects over 2-in. diameter, weeds, large roots, root clusters, and other objectionable material.
- B. Strip topsoil from project area to whatever depths encountered; prevent intermingling with underlying subsoil or other objectionable material. Remove heavy growths of grass from areas before stripping topsoil.
- C. Where trees are indicated to remain, terminate stripping a sufficient distance from such trees to prevent damage to root system.
- D. Stockpile topsoil in storage piles in areas where designated. Construct storage piles to freely drain surface water. Cover or sprinkle water on storage piles to prevent windblown dust.

3.05 DEMOLITION

- A. Remove structures, pavements, and improvements within construction limits as shown and as required for construction. Saw cut asphaltic and concrete pavement to provide a smooth straight joint. Remove below-grade items encountered, such as slabs and foundations, that interfere with construction.
- B. The County shall have first right to retain all useful salvage. All items not retained by the County and construction debris shall become property of Contractor.

3.06 DEBRIS DISPOSAL

A. Remove debris and excess materials from site and legally dispose of it. Burning shall not be permitted on project site. Comply with federal, state, and local laws and regulations.

EROSION AND SEDIMENTATION CONTROL

PART 1 - GENERAL

1.01 DESCRIPTION

- A. In addition to the requirements of the applicable sections in Divisions 00 and 01:
 - 1. The provisions for prevention, control and abatement of erosion, sedimentation and water pollution shall be as stated in the FDOT Standard Specifications for Road and Bridge Construction, Section 104, 2019 Edition (as modified in this document below), and as required by the St. John's River Water Management District.

1.02 CHANGES TO FDOT STANDARD SPECIFICATION 104

SECTION 104 (Pages 124 - 131) is deleted and the following substituted:

SECTION 104

PREVENTION, CONTROL, AND ABATEMENT OF EROSION AND WATER POLLUTION

104-1 Description

Provide an erosion and sediment control plan signed and sealed by a Specialty Engineer. Select and install temporary erosion and sediment control features in accordance with the plan for the project and for areas outside the right-of-way where work is accomplished in conjunction with the project and the project permits to prevent pollution of water and wetlands, detrimental effects to public or private property adjacent to the project right-of-way and damage to work on the project. Adjust, maintain, replace, or supplement selected devices as needed to ensure continuous control of erosion, sediment, turbid discharge, water pollution, and compliance with permit conditions until Final Acceptance in accordance with 5-11.

104-2 Features.

Use features identified as Best Management Practices (BMPs) in the State of Florida Erosion and Sediment Control Designer and Reviewer Manual and accepted by the Engineer. The Engineer will base acceptance on visual inspection, review of pertinent toxicity data and BMPs. Products containing geotextile fabric must meet the testing requirements in 985-4. The Engineer may also approve reuse of erosion and sediment control features, provided those features will not be incorporated into the completed project.

104-3 Preconstruction.

Provide an erosion and sediment control plan prepared by a Specialty Engineer in accordance with BMPs identified in the State of Florida Erosion and Sediment Control Designer and Reviewer Manual. At the

preconstruction conference, submit the plan to the Engineer for review, discuss the plan, and review the requirements and special conditions of all permits. As a minimum, include the following items or activities in the plan:

(1) For each phase of construction operations or activities provide:

- (a) Locations of features
- (b) Types of features
- (c) Estimated time features will be in operation
- (d) Monitoring schedules for maintenance of features
- (e) Methods of maintaining features
- (f) Methods of containing or removing pollutants or hazardous wastes
- (g) Limitations of exposed erodible earth as defined in 104-4.1
- (h) Existing and proposed drainage and flow patterns

(i) Positive drainage measures to be employed, installing as soon as practical permanent drainage features

(2) A procedure to control off-site tracking of soil by vehicles and construction equipment.

(3) A procedure for cleanup and reporting of non-stormwater discharges such as contaminated groundwater or accidental spills.

(4) The name and telephone number and copy of inspection qualifications for the person responsible for monitoring and maintaining the features.

Submit the project specific erosion and sediment control plan to the appropriate Water Management District for review and approval. Do not begin any construction activities until all approvals are received.

Prior to submitting a Notice of Intent (NOI) to the Florida Department of Environmental Protection (FDEP) to be covered under the FDEP Generic Permit for Stormwater Discharge from Large and Small Construction Activities (CGP), the Contractor's erosion and sediment control plan shall be incorporated into the Department's Stormwater Pollution Prevention Plan (SWPPP). Do not begin any soil disturbing activities until notification of permit coverage is received.

104-4 Construction.

104-4.1 General: Select and install temporary erosion and sediment control features in accordance with the sediment and erosion control plan. Adjust, maintain, replace, or supplement selected features as needed to ensure continuous control of erosion, sediment or turbid discharge and water pollution.

104-4.2 Erodible Earth Limits: Do not expose more than 750,000 ft2 of erodible earth, unless otherwise approved by the Engineer. This limitation applies separately to clearing and grubbing operations and excavation and filling operations.

104-4.3 Field Reviews: The Specialty Engineer shall perform field reviews in conjunction with successive operations to verify implementation of the erosion and sediment control plan. Based on the field review, the Specialty Engineer shall provide additions or corrections to the copy of the sediment and erosion control plan kept at the project site and provide the Engineer with 2 copies of the changes.

104-4.4 Control of Operations: Install erosion and sediment control features prior to any soil disturbing operations commencing unless otherwise noted in the permits.

Prevent pollution of surface waters and wetlands including streams, canals, lakes, reservoirs, and other water impoundments with fuels, oils, bitumens, calcium chloride, sediment, turbidity, or other harmful materials. Also, conduct and schedule operations to avoid pollution or siltation of such water impoundments, and to avoid interference with movement of migratory fish. Do not dump any residue from dust collectors or washers into any surface waters.

Onsite fuel storage tanks and any equipment and material storage or maintenance areas within Department right of way must be maintained and stored in compliance with regulatory agency standards.

Locate temporary sanitary provisions away from inlets, streams, canals, lakes, reservoirs, and other water impoundments.

Restrict construction operations to those conditions allowed by permit in surface waters and wetlands such as rivers, streams, lakes, tidal waters, reservoirs, canals, and other water impoundments to those areas where it is necessary to perform filling or excavation to accomplish the work shown in the plans and permits and to those areas which must be entered to construct temporary or permanent structures using contained or stable materials. As soon as conditions permit, promptly clear rivers, streams, and impoundments of all obstructions placed therein or caused by construction operations back to preconstruction condition. Stabilize exposed areas as required by permit or within seven days, whichever is earlier.

Do not ford any surface waters with construction equipment. Wherever crossings are necessary, use a temporary bridge or other structure.

Except as necessary for construction and unless permitted by regulatory agencies, do not deposit excavated material or other erodible material in areas subject to concentrated flow of stormwater or in surface waters or wetlands such as rivers, streams, canals, or impoundments, or in a position close enough thereto, to be washed away by high water or runoff.

Where pumps are used to remove highly turbid waters from enclosed construction areas such as cofferdams or forms or from trench excavations, treat the water with methods outlined in the Manual to bring it into compliance with water quality standards acceptable to regulatory agencies prior to discharge into State waters. Do not allow discharged water to flow across unstabilized areas prior to entering surface waters or wetlands, and do not allow discharged waters to scour sediments and create turbidity in surface waters or wetlands.

Do not disturb lands or waters outside the limits of construction as staked, except as authorized by the Engineer.

Obtain the Engineer's approval for the location of, and method of operation in, borrow pits, material pits, and disposal areas furnished for waste material from the project (other than commercially operated sources) such that erosion during and after completion of the work will not result in detrimental siltation or water pollution in accordance with 7-1.

104-4.5 Erosion and Sediment Control Methods: Each of the erosion and sediment control methods has intended functions. Utilize the method that best controls erosion, sediment, turbidity, or pollution discharges from the project. Select protection methods from those detailed in the State of Florida Erosion and Sediment Control Designer and Reviewer Manual appropriate to the type of work.

104-4.6 Erosion and Sediment Control Device Inspection and Maintenance: Using a FDEP certified inspector, inspect all erosion and sediment control devices in accordance with the Construction Generic Permit. Immediately correct any deficiencies. In addition, make a daily review of the location of erosion and sediment control devices in areas where construction activities have changed the natural contour and drainage runoff to ensure that the erosion and sediment control devices are properly located for effectiveness. Where deficiencies exist, install additional erosion and sediment control devices to conform to permit requirements.

Maintain permanent and temporary erosion and sediment control features, at no expense to the Department, until the project is complete and accepted. If reconstruction of such erosion and sediment control features is necessary due to the Contractor's negligence or carelessness or, in the case of temporary erosion and sediment control features, failure by the Contractor to install permanent erosion or sediment control features as scheduled, the Contractor shall replace such erosion or sediment control features is necessary, as determined by the Engineer, due to factors beyond the control of the Contractor, the Department will consider payment for replacement pursuant to 4-4, Unforeseeable Work.

Maintain all erosion and sediment control features as required in the Stormwater Pollution Prevention Plan, Contractor's project specific erosion and sediment control plan and as specified in the State of Florida Department of Environmental Protection Generic Permit for Stormwater Discharge from Large and

Small Construction Activities.

Address any sediment deposits remaining in place after the temporary erosion and sediment control devices are no longer required to conform to the finished grade and prepare them in accordance with Section 570.

104-4.7 Performance Standards for Sediment and Erosion Control Plan and Water Quality Monitoring Requirements: Completely retain eroded soils and turbid water on the project site and do not discharge into wetlands or surface waters on any portion of the job site for the duration of the project.

Prior to starting construction, conduct water quality sampling in the receiving waters at points above, within and below the project site to establish a baseline assessment of turbidity for the waterbody. Inspect the project site per the requirements of the NPDES CGP.

When a visible stormwater discharge is detected during a rain event, sample all stormwater discharge points that leave the project site for turbidity. Provide the turbidity monitoring results to the engineer with the weekly inspection reports required by the CGP. Discharged stormwater turbidity must be ≤ 29 Nephelometric Turbidity Units (NTU) above background for surface waters and must be 0 NTUs above background for any waterbody designated as an Outstanding Florida Water. Sediment migration off site and discharge of turbid water above state standards is a violation of the permit and corrective measures must be performed immediately.

104-4.8 Removal of Temporary Erosion Control Features: Remove temporary erosion and sediment control devices only after the protected areas are permanently stabilized or as directed by the Engineer. Final Acceptance in accordance with 5-11 will not be issued until all required temporary erosion and sediment control devices have been satisfactorily removed and disposed.

104-4.9 Protection During Suspension of Contract Time: If the Engineer determines it is necessary to suspend the construction operations for any appreciable length of time, inspect installed erosion and sediment control devices and install, as needed, additional measures to prevent erosion and sediment transport from the site. During such suspensions of operations, perform additional erosion and sediment control work as required by the Engineer. Payment for additional work during periods of Department directed suspensions will be in accordance with 4-4 as unforeseeable work.

In the event of a suspension of work due to a named storm event, remove existing temporary erosion or sediment control devices as directed by the Engineer. Payment for removal and subsequent replacement, if necessary, will be in accordance with 4-4 as unforeseeable work.

104-5 Method of Measurement.

The quantity paid will be the lump sum quantity for all work specified in this Section, completed and accepted.

104-6 Basis of Payment.

Price and payment will be full compensation for all work specified in this Section. Separate payment will not be made for the cost of constructing temporary earth berms along the edges of roadways to prevent erosion or sediment transport during grading and subsequent operations. Include these costs in the unit prices for grading.

If the requirements of this Section are not satisfied, the Engineer may employ outside assistance or use Department employees to perform corrective measures as needed. The monthly progress estimate will be reduced by any such costs incurred, including engineering costs.

Payment will be made under: Item No. 104-1 - Erosion and Sediment Control - LS

Standard Integral Pile Jacket, Non-Structural Up To 16"

PART 1 GENERAL

1.01 SUMMARY

,

A. Standard Integral Pile Jacket, Non-Standard Up To 16" shall be constructed in accordance with Section 457 of the Florida Department of Transportation Standard Specifications for Road and Bridge Construction, 2019 Edition, Special Provisions for Integral Pile and Column Jackets.

APPENDICES

Contract CM2831

APPENDIX A ROAD CLOSURE POLICY



Nassau County Engineering Services Department 96161 Nassau Place Yulee, Florida 32097

Road Closure Policy

- 1. Submit a written request to the Public Works Director for the road closure. In the request you must explain the following:
 - a) Why the road needs to be closed and the duration of the closure?
 - b) What are the benefits to public for closing the road?
 - c) Include a draft detour plan.

After the road closure request and draft detour plan have been approved, the following information shall be submitted to the Nassau County Engineering Services Department for review and approval.

2. Submit to Nassau County Engineering Services Department: A Maintenance of Traffic (MOT) Plan that was prepared by or approved by Florida Advanced Maintenance of Traffic (AMOT) certified personnel referencing the latest editions of the Florida Department of Transportation (FDOT) Design Standards Section 600 and the Manual on Uniform Traffic Control Devices (MUTCD). These plans shall include the Worksite Traffic Supervisor as per the latest edition of the FDOT Standard Specifications for Road & Bridge Construction Section 105-8.3. Valiable Message Boards (VMB) will be required and shall be installed 7 days prior to the detour taking place and remain throughout. Any signed detour that will be within FDOT Right-of-Way (or on portions thereof) shall have prior FDOT approval.

A Maintenance of Traffic Plan proposing a change to any approved documents, including contract documents and approved construction plans must be signed and sealed.

3. Provide a public notification advertisement to an approved local newspaper. To appear no less than fourteen (14) days prior to the scheduled closure. Submit the draft notification to Nassau County Engineering Services for review and approval prior to advertising. This notification will clearly describe the name of the project and contractor, scope of the detour, scope of construction, the name of all roads that will be affected, official detour routes, duration of closure and the Worksite Traffic Supervisor's telephone number. Attach a diagram showing the surrounding area and detour routes. Diagram must be clear and depict road names and route direction. The size of advertisement in newspaper shall be a minimum of 2 columns wide by 12 inches long (tall) or one fifth (1/5) of a page with a minimum of 24 point font for the heading and 10 point font for the body and detour plan. Flyers with the same information may be required. With the Engineering Services Department's written approval, local roads may not require publishing of the advertisement in the paper; however, all other criteria must be adhered to.

Phone (904) 530-6225

Fax (904) 491-3611

Road Closure Policy Page 2 of 3



- 4. Submit notification to the following departments and agencies prior to the road closure. A confirmation of notification to the Engineering Services Department must be provided prior to road closure.
- Nassau County Sheriff's Office:
 - o Ricky A Rowell, TAC Phone - (904) 548-4000 Fax- (904) 225-5737 Email -rickyr@nassauso.com
 - o L. Rene Graham, Lt. Phone - (904) 548-4000 Fax - (904) 548-4128 Email - Irgraham @nassauso.com
- Nassau County Emergency Management:
 - o Martha Oberdorfer Phone - (904) 548-4094 Fax - (904) 548-4194 Email- mlwagaman@nassauso.com
- Nassau County School Bus Transportation: o AmyBell Phone - (904) 225-0127 Fax - (904) 255-9404 Email - amy.bell@nassau.k12.fl.us
- Nassau County Road & Bridge Department:
 Jennifer Kirkland Phone - (904) 530-6175 Fax - (904) 530-6901 Email - jbeayer @nassaucountyfl.com

- Nassau County Manager 's Office

 Sabrina Robertson
 Phone- (904) 530-6010
 Fax -(904) 321-5784
 Email SRobertson@nassaucou ntyfl.com
- United Postal Service (Yulee)
 o Beverly Dye
 Phone (904) 225-5331
 Fax (904) 225-9733
 Email- beverly .a.dye@usps .goy
- United Postal Service (Fernandina)
 o EdwinLang
 Phone (904) 491-8102
 Fax (904) 277-7947
 Email -edwin.p.lang@usps .gov
- United Postal Service (Callahan)

 Kim Vojtech
 Phone- (904) 879-2131
 Fax (904) 879-6737
 Email -kim.k.vojtech@usps.gov
- United Postal Service (Hilliard)

 Heather Ackerman
 Phone (904) 845-2151
 Fax (904) 845-7738
 Email -heather.r.ackeonan@usps.gov

Depending on the location of the project/detour, notification to other agencies may be required.

Fax (904) 491-3611

Road Closure Policy Page 3 of3



- 5. Signage will be in place prior to road closure. They will be bagged/covered until needed. VMBs, will be installed and operating a minimum of seven (7) calendar days prior to any closure/detour.
- 6. Visual inspection of the VMB by the Engineering Services Department is required at installation or relocation. Visual inspection of all road/detour signage shall be accomplished prior to road closure. Contact Engineering Services 48 hours prior to installation for inspection.

APPENDIX B AS-BUILTS REQUIREMENT CHECKLIST



Nassau County Engineering Services Department 96161 Nassau Place Yulee, Florida 32097

AS-BUILT REQUIREMENT CHECKLIST:

The following list is intended to highlight the majority of the as-built requirements for Construction projects in Nassau County. This list should not be considered to be all-inclusive as each project is unique in nature and may require additional information that can only be determined during the course of the project's completion. Generally, however,theAS-BUILT information shall contain the following:

- 1. AS-BUILTS should be based on the design plans as approved through the DRC process. The submitted as-builts should be at the same scale and have the same orientation as the design files.
- AS-BUILTS should have the same page numbering as the design plans, and the cover of the AS-BUILT plans should have all sheets from the design plans listed with sheets not "AS-BUILTED" stricken through.
- 3. AS-BUILTS should display the original design information as displayed on the plan sheets with the design information stricken through and the as-built information displayed in bold adjacent to the design information.
- 4. AS-BUILTS shall be accompanied by an "Engineer's Certification" form from the Engineer of Record. (Exhibits 3 & 4)
- 5. Three {3} sets of fully signed and sealed AS-BUILTS should be submitted along with CD containing the PDF file(s) and CADD file(s) of the AS-BUILT information. CADD files should be in State Plane coordinates (NAD 83) with a vertical datum of NAVD88 or NGVD 1929 (with the datum shift noted). Furthermore, CADD files should only be submitted in ACAD version 2013 or later.
- 6. Northing and Easting of all drainage structures should be included.
- 7. The plans should be clearly legible, and all structure notes, distances, angles and elevations should be clearly readable.
- 8. If the plan represents a phase of a development, then that phase should be clearly identified for clarity and avoid confusion with future phases.
- 9. There should be a north arrow and scale on each sheet.
- 10. A legend should be included explaining the symbols used in the plans.
- 11. ALL sheets must be signed and sealed by a surveyor licensed in the State of Florida.




- 12. There should be sufficient "plan" and "as-built" elevations shown to verify that the streets were constructed substantially in accordance with the approved construction plans. Generally, the County will review all low points and high points in the street and verify that the minimum grade exists for each street. On straight sections between high and low points elevations should be taken every 200 feet.
- 13. All street curve radii should be shown on the plans or in a table.
- 14. Street widths and curb type should be identified for each street on each sheet.
- 15. Whenever there are islands within the streets the as-builts should include dimensions for these islands.
- 16. The paved radii of all Cui-de-Sacs should be listed and Cul-De-Sac center and edge of pavement or gutter elevations at quarter points shall be shown.
- 17. All underdrains should be shown with size, lengths, inverts and cleanouts all shown.
- 18. Where swales are utilized there should be sufficient flow line elevations and ditch cross sections to verify capacity of the channel.
- 19. There should be a comparison table of design and as-built pipe sizes, lengths, invert elevations, and pipe slopes.
- 20. The as-built surface area of the pond(s) at Normal Water Level (design) and Top of Bank (as-built) should be included.
- 21. The bottom elevation and area should be shown (2 locations min. per pond).
- 22. The surveyor shall certify by note (for each pond) that no slope is greater than 1:4 above the design NWL, unless the pond is fenced.
- 23. All structures in the pond (overflow weirs, etc.) should be included.
- 24. All water main and sewer main locations, size, lengths, inverts, etc.
- 25. All easements required (or on a plat) should be shown on the "As- Builts" and improvement located so as to verify improvements are within the easement. Easement not recorded as part of the recorded plat including drainage and right-of-way easements shall also be identified as "as-built". For these easements the book and page of their record, property to whom easement is dedicated and date of filing should be shown on as the "as-built". All improvements intended to be within these easements shall be shown as the "as-built" to verify the improvements are within the easement. Wetlands are not reviewed by Nassau County and need not be shown.
- 26. Depict all storm drain and utility repair locations and methods.

Phone (904) 530-6225

Contract CM2831

APPENDIX C PLANS/DRAWINGS

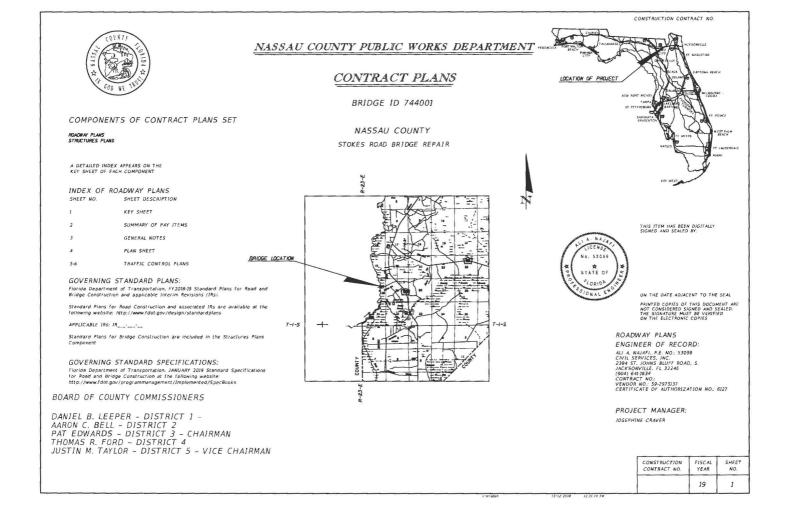

ITEM NUMBER DI01-1 0102-1 0104-11 SUMMARY OF ROADWAY UNIT OUANTITY QUANTITY TOTAL 15 1.00 1.00 15 1.00 1.00 IT MOBILIZATION MAINTENANCE OF TRAFFIC TURBIDITY BARRIER 17 000 SUMMARY OF STRUCTURES THE DESCRIPTION RESTORE SPALLED AREA. PORTLAND CEMENT GROUT STANDARD INTEGRAL FILE JACKET, NON-STRUCTURAL UP TO 18* ITEM NUMBER 0401-70-4 0457-1-11 UNIT QUANTITY QUANTITY TOTAL CF 10.00 10.00 UF 236.00 236.00 REVISIONS DESCRIPTION DATE BY CIVIL SERVICES, INC. CONSULTING ENGINEERS 2394 ST. JOHNS BLUFF ROAD, S. JACKSONVILE, FL 32246 C.A. NUMBER: 6127 ALI A. NAJAFI, PE NO. 53099 NABAU COUNTY ENGINEERING NASEAU COUNTY PLOREDA CONSTRUCTION PLANS FOR: DATE DESCRIPTION SHEET NO. SUMMARY OF PAY ITEMS 2 STOKES RD 1708 ProjecteV81-2403 Reseau County Stokes Road Bridg

GENERAL NOTES

1. EXISTING DRAINAGE STRUCTURES WITHIN CONSTRUCTION LINITS SHALL REMAIN UNLESS OTHERWISE NOTED.

2. THE CONTRACTOR SHALL NOTIFY UTILITY OWNERS LISTED BELOW THROUGH SUNSHINE ONE CALL OF FLORIDA, INC. (1-800-432-4770) IN ADVANCE OF BEDINNING CONSTRUCTION ON THE PROJECT SITE.

AT NO ADDITIONAL COST TO THE COUNTY, THE CONTRACTOR WAY BE REQUIRED TO PHYSICALLY EXPOSE AND SUPPORT UNDERFROND FACILITIES AND PROVIDE REASONABLE TIME TO ALLOW FOR MINOR UNFORESSEN UTLITY RELOCATIONS BY UTLITY COMPANY AND/ON PROVIDE ANY RECESSANT SUPPORT TO ARTIAL FACILITIES AS DEEMED NECESSANT TO PERFORM CONSTRUCTION. CONTRACTOR MUST NOTIFY UTLITY COMPANY E4 HOURS PRIOR TO ANY SUCH WORK.

UTILITY	AGENCY OWNER	CONTACT	TELEPHONE NUMBER
TELEPHONE	AT& T DISTRIBUTION	DINO FARRIGGIO	(561) 997-0240
ELECTRIC	OKEFENOKE RURAL ELECTRIC MEMBERSHIP CORP	ELVIN CUSHMAN	(904)-845-7477 EXT. 314

- 3. ANY PUBLIC LAND CORMER WITHIN THE LIWITS OF CONSTRUCTION TO BE PROTECTED. IF A CORMER WONUMENT OR BERCHMARK IS IN DANGER OF BEING DESTROYED AND MAS WOT BEEN PROPERTY REFERENCED, THE CONTRACTOR SHOULD BOTIFY THE COURT WITHOUT BELAY, BY TELEPONGE. THE CONTRACTOR IS REPORTIBLE FOR ANY EPPENDENTS. ENCUMERTED FOR PROTECTING, REFERENCING AND/OR REPLACING ANY CORMER WONUMENTS OR BERCHMARKS.
- 4. FILTER FABRIC USED TO WRAP PIPE JOINTS IN ACCORDANCE WITH SPECIFICATION 430 SMALL MEET THE REQUIREMENTS OF FOOT DESIGN STANDARDS INDEX 199, TYPE D-3 WITH AN A.O.S. (SIEVE NUMBER) OF 70 TO 100.
- 5. ALL WORK PERFORMED WITHIN THE COUNTY RIGHT-OF-WAY, MATERIALS AND TESTING SHALL BE IN COMPLETE ACCORDANCE WITH ALL RELATIVE SECTIONS OF MASSAN COUNTY STADAMOS, ILATEST REVISION AND ALL CUMPENT MASSAN COUNTY STADAMOD DETAILS FORD DESIGN STADAMOS AND FODD STADAMOS SHEEVISION AND ALL CUMPENT BHIDDE ROIGN'S, WILL BE USED IF NOT ADDRESSED BY MASSAN COUNTY DOCUMENTS. CONTRACTOR SHALL COMPLY WITH CUMPENT FLORIDA ACCESSION IT COOR FOR ALL WORK ON THIS PROJECT.
- 6. ALL WORK SHALL BE PERFORMED IN A SAFE MANNER. ALL SAFETY RULES AND GUIDELINES OF 0.S.H.A. SHALL BE FOLLOWED. THE CONTRACTOR SHALL BE WROLLY RESPONSIBLE FOR ANY INJURIES TO HIS EMPLOYEES AND ANY DAMAGE TO PRIVATE PROPERTY ON PERSONS DURING THE CONCERNE OF THIS PROJECT. ALL COSTS ASSOCIATED WITH COMPLYING WITH 0.S.H.A. REGULATIONS AND THE FLORIDA TREMCH SAFETY ACT MUST BE INSLUDED IN THE CONTRACTORS BID.
- 7. THE CONTRACTOR SHALL BE RESPONSIBLE FOR VISITING THE JOB SITE PRIOR TO PREPARING THE BID FOR THE PURPOSE OF FAMILIARIZING HIMSELF WITH THE NATURE AND THE EXTENT OF THE WORK AND LOCAL CONDITIONS. EITHER SURFACE OR SUB-SURFACE, WHICH MAN AFFECT THE WORK TO BE PERFORMED, AND THE EQUIPMENT, LABOR AND ANTERLAS REQUIRED. FAILURE TO DO SU WILL NOT RELIVET HE CONTRACTOR OF COMPLETE PERFORMANCE UNDER THE CONTRACT. THE CONTRACTOR IS ALSO URBED TO TAKE COLOR PHOTOGRAPHS THROUGHOUT THE PROJECT AREA TO RECORD EXISTING CONDITIONS PHILOR TO CONSTRUCTION OF THE THOLETOR. THE POSSIBLE PUTURE COMPLAINTS THAT WAY OCCUR DUE TO CONSTRUCTION OF THE PROJECT.
- 8. IT SHALL BE THE CONTRACTORS RESPONSIBILITY TO EITHER CONDUCT ANY FIELD EXPLORATION OR ACQUIRE ANY GEOTECHNICAL ASSISTANCE REQUIRED TO ESTIMATE THE AMOUNT OF UNSUITABLE WATERIAL REQUIRED TO BE REMOVED MODOR TO ESTIMATE THE AMOUNT OF OFS THE BORROW THAT WILL BE REQUIRED. CONTRACTOR TO USE AN APPROVED FOOT PIT. THE REMOVAL OF UNSUITABLE MATERIAL WITHIN THE PROJECT LINITS SHALL BE IN ACCORDANCE WITH FOOT STANDARD INDER NO. 550.
- 9. BENCHMARK DATUM: VERTICAL DATUM COMVERSION, ELEVATION OF 10.00' MAVD 88 = 11.01' MGVD' 29 (PER CORPSCOM V 6.01) ELEVATION OF 10.00' MAVD 88 = 11.05' MGVD' 29 (PER FLOOD INSURANCE RATE MAP)
- 10. THE CONTRACTOR WILL CONTRACT WITH AN INDEPENDENT TESTING LABORATORY TO PERFORM WATERIAL TESTING AND SOLITESTING IN ACCORDANCE WITH MASSAN COUNTY AND/OR FOOT REQUIREMENTS WITH PHOLO ADVANCE MOTICE TO WASSAN COUNTY AND/OR OWNER C.E.I.'S THIS SHALL INCLUDE DEWSITY TEST IN ALL PAYEMENT AREAS AND IN ALL UTILITY TRENDES LOCATED IN PAYEMENT AREAS, COMPARE TESTING AND ALL OTHER MATERIAL TESTING.
- 11. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND INSURANCE FOR THE PROJECT INCLUDING WPDES PERMITS, AND ETC.


12. THE CONTRACTOR SHALL COORDINATE THE WORK WITHIN MASSAU COUNTY RIGHT-OF-WAY WITH THE PROPER AGENCIES FOR MAINTENANCE OF TRAFFIC AND METHOD OF CONSTRUCTION AND REPAIR.

- 13. AS-BUILT DRAWINGS (E PAPERS & I CADD) AS-BUILTS TO BASSAU COUNTY ARE REQUIRED TO BE SIGNED AND SEALED BY A FLORIDA REDISTERED LAND SUMPTOR THEREFORE, IT SHALL BE THE CONTACTOR'S RESPONSIBILITY TO CONTACT WITH A LAND SUMPTOR A CONTRERED IN THE STATE OF FLORIDA FOR THE PREPARATION, FIELD LOCATIONS, CERTIFICATION AND SUMMITTAL OF "AS-BUILT" DRAWINGS IN ACCORDANCE WITH CUMBENT ASSAU COUNTY STANDARDS AND SPECIFICATIONS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO PROPESTA THE AS-BUILT DRAWINGS FOR APPROVA BY MASSAU COUNTY. CONTRACTOR SHALL REFER TO BASSAU COUNTY AS-BUILT CHECKLIST.
- 14. THE CONTRACTOR SMALL COORDINATE HIS CONSTRUCTION WITH ALL OTHER CONTRACTORS IN THE AREA. IN THE EVENT OF ANT CONFLICT WANTSOLVER. THE CONTRACTOR SMALL WOTHEY THE ENGINEER AND OWNER PRIOR TO PRECEDING WITH CONSTRUCTION.
- 15. CLEARING AND GRUBBING REQUIRED FOR ALL ROADWAY, UTILITIES, DITCHES AND BERNS INCLUDED IN THIS PROJECT, AND THE CLEARING AND GRUBBING OF ALL RIGHT-OF-WAY OR EXSEMENTS SHALL BE CONSIDERED AS PART OF THIS PROJECT. CONTINCTOR WILL SOO ALL DISTURBED AREAS.
- 15. ALL AREAS SHOWN TO BE FILLED SHALL BE CLEARED AND GRUBBED IN ACCORDANCE WITH FDOT STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION 2016, SECTION 110.
- IT. ALL DEBRIS RESULTING FROM ALL ACTIVITIES SHALL BE DISPOSED OF BY THE CONTRACTOR.
- 18. ALL EXCESS SUITABLE AND UNSUITABLE WATERIAL SHALL BE REMOVED FROM THE SITE BY THE CONTRACTOR UNLESS DIRECTED GTHERWISE BY ENGINEER OR OWNER.
- 19. ALL EXISTING TREES TO REMAIN SHALL BE PRESERVED AND PROTECTED.
- 20. CONTRACTOR SHALL CERTIFY THAT ALL SOD WITHIN THE COUNTY RIGHT-OF-WAY SHALL BE PERFORMANCE TURF AND SHALL BE PREE OF WOIYOUS WEEDS & GRASSES, INCLUDING TROPICAL SODA APPLE. CERTIFICATION SHALL BE PROVIDED PRIOR TO INSTALLATION.
- 21. A PRE- CONSTRUCTION WEETING IS REQUIRED TO BE ATTENDED BY WASSAU COUNTY REPRESENTATIVES, THE CONTRACTOR, AC (CONTRACTOR'S TESTING FIRM), SUB -CONTRACTORS, UTILITY COMPANIES, AND THE ENGINEER OF RECOMD.
- 22. ALL LANES MUST BE REOPENED TO NORMAL TRAFFIC WITHIN 8 HOURS AFTER RECEIVING WOTIFICATION OF A MURRICAME EVACUATION OR ANY OTHER CATASTADEMIC EVENT AND SHALL REMAIN OPEN FOR THE DURATION OF THE EVACUATION OR EVENT AS DIRECTED BY MASSAN COMMY. A DISASTER PREPAREDNESS PLAN SHALL BE SUBMITTED AT THE MRE- CONSTANCTION CONFERENCE.
- 23. THE CONTRACTOR WILL BOT BE ALLOWED TO PERFORM HIGHT TIME WORK, OR WEEKEND WORK. ANY CHANGES TO THESE LANE CLOSURE RESTRICTIONS WIST BE APPROVED BE MASSAU COUNTY ENGINEERING SERVICES DEPARTMENT. REFER TO MASSAU COUNT HOAD CLOSURE POLICY.
- 24. THE REMOVAL OF MUCK AND PLASTIC MATERIAL WITHIN THE PROJECT LINITS SHALL BE IN ACCORDANCE WITH THE FOOT STANDARD INDEX NO. 505.
- 25. ALL WORK PERFORMED WITHIN COUNTY'S RIGHT-OF-WAY SMALL CONFORM TO NASSAU COUNTY'S ORDINANCE 99-17 AND TO THE MOST CURRENT EDITION OF THE FOLLOWING PUBLICATIONS:

STANDARD SPECIFICATIONS FOR ROAD AND BRIDDE CONSTRUCTION (ERGLISH) FOOT DESIGN STANDARDS (EBOLISH) FOOT FLANS PREP MANUAL FOOT FLANS INLE PAYEMENT DESIGN WANUAL FOR NEW CONSTRUCTION AND PAYEMENT REMABILITATION


- FOOT FLEXIBLE PAVEMENT DESIGN MANUAL FOR NEW CONSTRUCTION AND PAVEMENT REMABILITATION 25. BURNING OF ANY MATERIAL OR DEBRIS IS PROHIBITED.
- 27. ACCESS TO DRIVENAYS AND SIDE STREETS SHALL BE MAINTAINED AT ALL TIMES.
- 28. CONTRACTOR SHALL SUBNIT AN MOT PLAN AT THE PRE- CONSTRUCTION MEETING. MAINTENANCE OF PEDESTRIAN TRAFFIC SHALL BE INCLUDED IN THE PLAN. CONTRACTOR'S PLAN SHALL CONFORM TO FOOT STANDARD INDEX 600 LAYEST EDITION, AND MASSAN CONTY'S ROAD CLOSURE POLICY.


REVISIONS			CIVIL SERVICES, INC.	10(17)	NASAU COUNTY ENGINEERING			
DATE B'	DESCRIPTION	DATE	DESCRIPTION	CONSULTING ENGINEERS 2384 ST. JOHNS BLUFF ROAD, S. JACKSONVILLE, FL 32246 C.A. NUMBER: 6127 ALI A. NAJAFI, PE NO, 53099		CONSTRUCTION FLANS FOR:	GENERAL NOTES	SHE MC

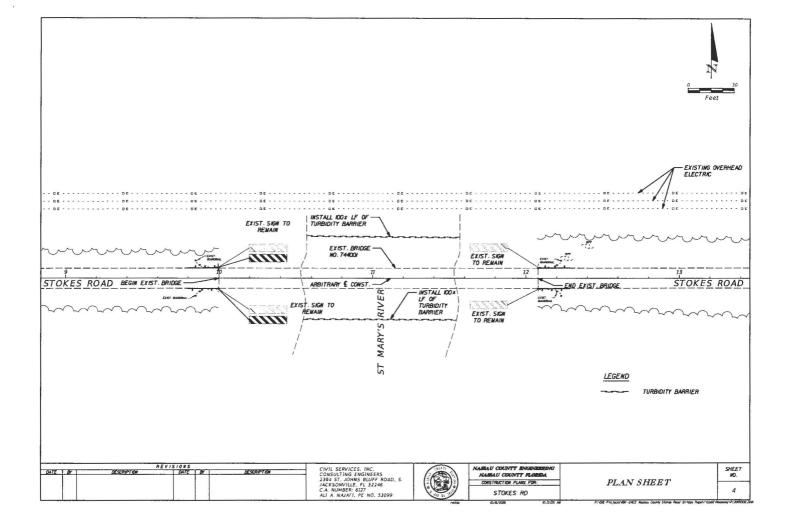

Contract CM2831


GENERAL NOTES:	
I. AT ALL TIMES, ADMERE TO THE REQUIREMENTS SET FORTH IN THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES WUTCD ILATEST EDITIONI, AND THE STANDARD PLANS ILATEST EDITION. ATTERTION IS DIRECTED OD SENIES INDICES.	
2. PLACE PORTABLE CHANGEABLE WESSAGE SLOWS LPCWSJ (7) DAYS IN ADVANCE OF THE PROPOSED CONSTRUCTION START DATE ON BOTH ENDS OF THE BRIDDE:	
MESSAGE SERVING AS PUBLIC NOTIFICATION SHALL READ:	
DI SPLAY I: DI SPLAY 2: STORES (BEGII DATE) • BRIDGE (WANTH)	
CORST (DAY)	
NESSAGE I NESSAGE 2 STORES IX/II + ROAD THEN	
CLOSED XX/XX = • TO BE DETERMINED BY THE ENGINEER.	
2. PLACE PCMS ON STOKES BOAD AT SR 23 AND CR 121 FOR DURATION OF CONSTRUCTION.	
DI SPLAY I: MESSAGE 2: STORES XL/XL = ROAD THRU	
REVISIONS DATE B' DESCRIPTON CIVIL SERVICES JIC. NAMBAU COUNTY ENGRADED NO	SHEET
CONSULTING ENGINEERS 2944 51, JACKSONVILLE, FL 32246 JACKSONVILLE, FL 32246	ORARY NO.
ALI A. NAJAFI, PE NO. 53099 STOKES RD	CO Numici County States And Britose Media/CoestVisionery/TCD/NEDF.Dow

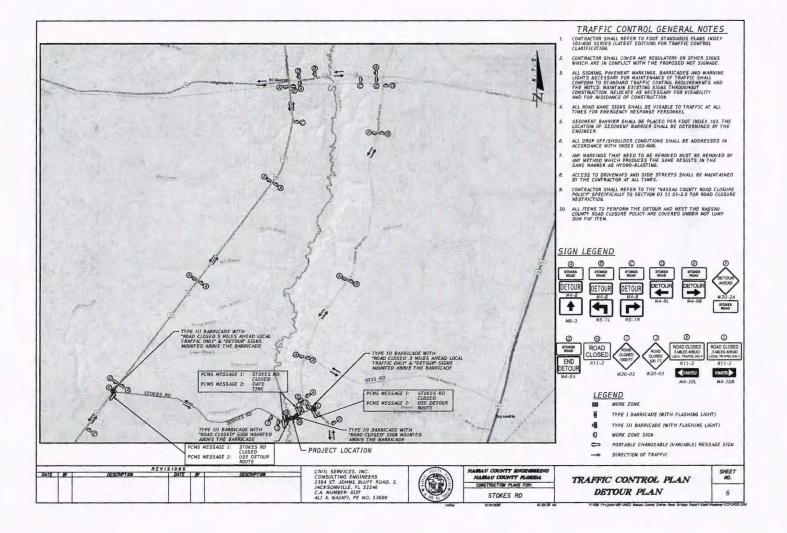


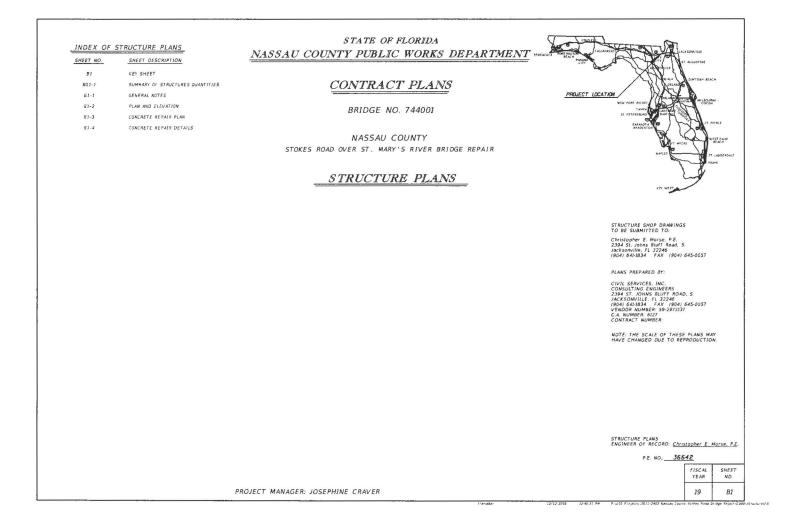


	CITIZEA	RY OF STRUCTURE O			CE 744001		
PAY ITEM			1 1	QUANTITY		DESIGN	CONSTRUCTION
PAY ITEM NO.	PAY ITEM DESCRIPTION	LOCATION	UNIT			DESIGN NOTES	CONSTRUCTION REMARKS
			-				
401-70-4	RESTORE SPALLED AREA, PORTLAND CEMENT GROUT				10.0		-F
						ACTUAL QUANTITY IS 4.7 CF	
					230		
	00 10 18						
	457 - 1 - 11		457-1-11 STANDARD INTEGRAL PILE JACKET, NON-STRUCTURAL, BENT 4	457-1-11 STANDARD INTEGRAL PILE JACKET. NON-STRUCTURAL, BENT 4 LF UP TO 16" BENT 5 LF BENT 6 LF	#INGWALLS CF 0.6 457-1-11 STANDARD INTEGRAL FILE JACKET. NON-STRUCTURAL. BENT 4 LF 56 UP TO 16" BENT 5 LF 64 BENT 6 LF 72	WINGWALLS CF 0.6 457-1-11 STANDARD INTEGRAL PILE JACKET. NON-STRUCTURAL. BENT 4 LF 56 236 UP TO 16* BENT 5 LF 64 64 64	WINGWALLS CF 0.6 ACTUAL QUANTITY IS 4.7 CF 457-1-11 STANDARD INTEGRAL PILE JACKET. NON-STRUCTURAL. BENT 4 LF 56 236 UP TO 16* BENT 5 LF 64 64 64

				1. 100 C. 100 C.	
	ERAL NOTES:				
DES	IGN SPECIFICATIONS				
1.	FDOT Structures Manual dated January 2018	and subsequent Struc	tures Design		
.2	Bulletin (17-10). American Association of State Highway and T	ransportation Official	IS (AASHTO)		
2.	Load and Resistance Factor (LRFD) Bridge De				
	and all subsequent interims.				
3.	FDOT Design Manual dated January, 2018 and Bulletin [17-13].	subsequent Roadway	Design		
	FRAL SPECIFICATIONS				
1.	Florida Department of Transportation, FY 201 Drawings as appended herein, and January 20				
	Road and Bridge Construction as amended by				
2.	Bridge Maintenance and Repair Handbook rev	sea 08/13/2011.			
PLA	DIMENSIONS				
	dimensions in these plans are measured in tee	t either horizontally	or vertically		
ותט 	iss otherwise noted.				
PRO	FECTION OF EXISTING STRUCTURE				
	ractor will perform work on and around the e				
	age the structure. Any damage incurred by the aired at no additional cost to the County and to				
		The surgedense of	in anymer.		
	ENSION VERIFICATION				
	dimensions, elevations and intersection angles the Contractor's responsibility to verify this				
		uala del ure deginning	ispairs.		
	JACKETS				
1.	Should high water affect pile jacket installal approval, a dewatering plan or alternative in:				
	Cost of dewatering is incidental to the cost of		able for blue water usage.		
2.	See the FDOT Standard Specifications Specia for pile jacket filler concrete class and furt		457 "Integral Pile Jackets"		
	for pre jacket tiner concrete crass and funt	der derairs.			
REL	EORCING STEEL				
A11	einforcing steel will be ASTM A615, Graae 60	Uncoated).			
	ITEM NOTES:				
	of preparation, labor, material and all other i				
incl	ided in the bid cost of Restore Spalled Area, f	ortiand Lement Grout		Bridge N	lo. 744001
REVISIONS DATE BY DESCRIPTION DATE BY DESCRIPTION	CIVIL SERVICES, INC. CONSULTING ENGINEERS	(STUT)	NASSAU COUNTY SNGINESRING	GENERAL NOTES	SHEET
	2394 ST. JOHNS BLUFF ROAD, S. JACKSONVILLE, FL 32246		NASSAU COUNTY FLORIDA CONSTRUCTION PLANS FOR:		NO.
	C.A. NUMBER: 6127 CHRISTOPHER E. MORSE, PE NO. 36642		STOKES RD	STOKES ROAD OVER ST. MARY'S RIVER	B1-1
and the second		SL'SEPS	SDATES STIMES	351152	

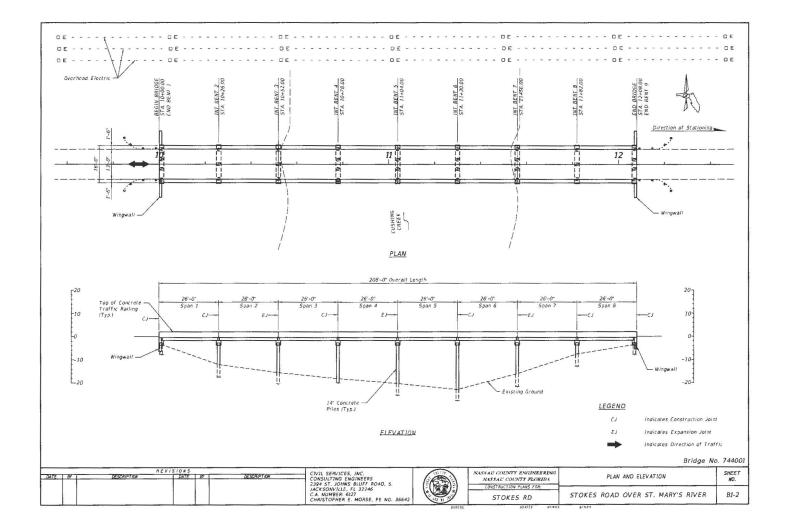

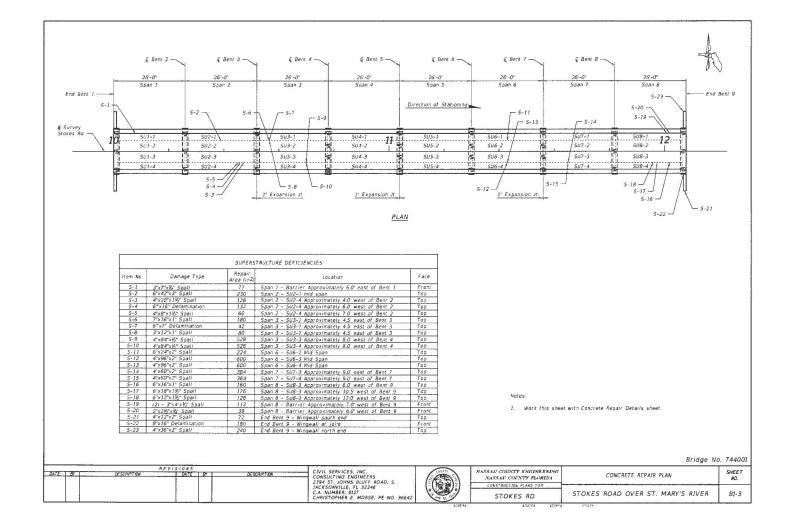

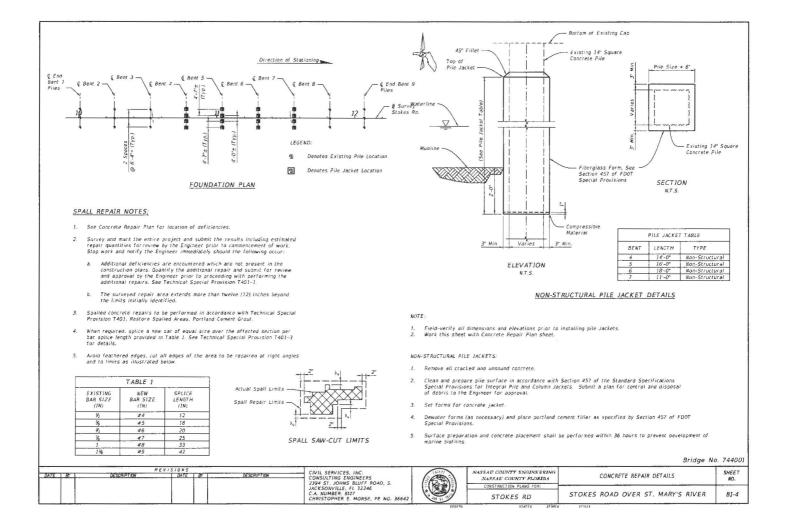

ADDENDA



NASSAU COUNTY BOARD OF COUNTY COMMISSIONERS Contract Management Department 96135 Nassau Place, Suite 2 Yulee, Florida 32097 904-530-6040 Grayson Hagins ghagins@nassaucountyfl.com

TO:	All Proposers
FROM:	Grayson Hagins, Contract/Purchasing Manager
SUBJECT:	Addendum #1
	Invitation to Bid, Bid Number NC19-027
	Stokes Rd. Bridge Repair
	January 21, 2020

REMINDER: This addendum must be acknowledged, on the Bid Form Section 00-41-15, Article 3.01.A. Failure to comply may result in disqualification of your submittal.

This addendum is hereby incorporated into the bid documents of the project referenced above. The following items are clarifications, corrections, additions, deletions and/or revisions to, and shall take precedence over, the original documents.

Part 1 – Questions & Answers

Can you tell me if the Board of Commissioners has a budgeted amount established for the above referenced project? I was not able to locate this budgetary number on bid docs or public record.

Answer: The engineer's construction estimate for this project is \$474,505.40

Part 2 – Clarifications

THERE WILL BE NO PRE-BID MEETING FOR THIS PROJECT

ATTACHMENTS:

N/A

NOTE: You are required to acknowledge receipt of this addendum on the Bid Form, Section 00-41-15, Article 3.01.A.

End of Addendum #1

Contract CM2831

EXHIBIT 1 GENERAL INFORMATION AND MINIMUM INSURANCE INFORMATION

.

GENERAL INFORMATION AND MINIMUM INSURANCE REQUIREMENTS

COMMERCIAL GENERAL LIABILITY INSURANCE

The Contractor shall purchase and maintain at the Contractor's expense Commercial General Liability insurance coverage (ISO or comparable Occurrence Form) for the life of this Contract. Modified Occurrence or Claims Made forms are not acceptable.

The Limits of this insurance shall not be less than the following limits:	
Each Occurrence Limit	\$1,000,000
Personal & Advertising Injury Limit	\$1,000,000
Fire Damage Limit (any one fire)	\$ 50,000
Medical Expense Limit (any one person)	\$ 5,000
Products & Completed Operations Aggregate Limit	\$2,000,000
General Aggregate Limit (other than Products &	
Completed Operations) Applies Per Project	\$2,000,000

General liability coverage shall continue to apply to "bodily injury" and to "property damage" occurring after all work on the Site of the covered operations to be performed by or on behalf of the additional insureds has been completed and shall continue after that portion of "your work" out of which the injury or damage arises has been put to its intended use.

WORKERS' COMPENSATION AND EMPLOYER'S LIABILITY INSURANCE

The Contractor shall purchase and maintain at the Contractor's expense Workers' Compensation and Employer's Liability insurance coverage for the life of this Contract.

The Limits of this insurance shall not be less than the following limits:

<u>Part One</u> – Workers' Compensation Insurance – Unlimited Statutory Benefits as provided in the Florida Statutes and <u>Part Two</u> – Employer's Liability Insurance Bodily Injury By Accident Bodily Injury By Disease Bodily Injury By Disease

\$1,000,000 Each Accident \$1,000,000 Policy Limit \$1,000,000 Each Employee

*If leased employees are used, policy must include an Alternate Employer's Endorsement

U.S. LONGSHORE & HARBOR COVERAGE (Federal Act)

The Contractor shall purchase and maintain at the Contractor's expense U. S. Longshore & Harbor Workers Coverage for the life of this Contract.

This can be a stand-alone policy or added by endorsement to the State Act Workers' Compensation and Employers Liability policy noted above.

Limits as noted under Workers' Compensation and Employers Liability Insurance.

AUTOMOBILE LIABILITY INSURANCE

The Contractor shall purchase and maintain at the Contractor's expense Automobile Liability insurance coverage for the life of this Contract.

The Limits of this insurance shall not be less than the following limits: Combined Single Limit – Each Accident

\$1,000,000

Covered Automobiles shall include any auto owned or operated by the insured Contractor, insured Subsubcontractor including autos which are leased, hired, rented or borrowed, including autos owned by their employees which are used in connection with the business of the respective Contractor or Sub-subcontractor.

UMBRELLA INSURANCE

The Contractor shall purchase and maintain at the Contractor's expense Umbrella Liability (Umbrella Form) insurance coverage for the life of this Contract.

The Limits of this insurance shall not be less than the following limits:

Each Occurrence Limit Aggregate Limit \$1,000,000 \$1,000,000

Contractor shall require each of his Subcontractors to likewise purchase and maintain at their expense Commercial General Liability insurance, Workers' Compensation and Employer's Liability coverage, Automobile Liability insurance, Umbrella Liability Professional Liability, Environmental Liability, Builders Risk or Installation Floater (as applicable) insurance coverage meeting the same limit and requirements as the Contractors insurance.

Certificates of Insurance acceptable to Nassau County Board of County Commissioners for the Contractor's insurance must be received within five (5) days of Notification of Selection and at time of signing Agreement.

Certificates of Insurance and the insurance policies required for this Agreement shall contain an endorsement that coverage afforded under the policies will not be cancelled or allowed to expire until at least thirty (30) days prior written notice has been given to Nassau County Board of County Commissioners.

Certificates of Insurance and the insurance policies required for this Agreement will include a provision that policies, except Workers' Compensation and Professional Liability, are primary and noncontributory to any insurance maintained by the Contractor.

Nassau County Board of County Commissioners must be named as an Additional Insured and endorsed onto the Commercial General Liability (CGL), Auto Liability and Umbrella Liability policy (ies). A copy of the endorsement(s) must be supplied to Nassau County Board of County Commissioners ten (10) days following the execution of the agreement or prior to the first date of services, whichever comes first.

CGL policy Additional Insured Endorsement must include Ongoing and Completed Operations (Form CG2010 11 84 **OR** Form CG2010 04 13 and GC2037 04 13 edition or equivalent). Other Additional Insured forms might be acceptable but only if modified to delete the word "ongoing" and insert the sentence "Operations include ongoing and completed operations".

CGL policy shall not be endorsed with Exclusion - Damage to Work performed by Subcontractors on Your Behalf (CG2294 or CG2295)

CGL policy shall not be endorsed with Contractual Liability Limitation Endorsement (CG2139) or Amendment of Insured Contract Definition (CG 2426)

CGL policy shall not be endorsed with Exclusion - Damage to Premises Rented to you (CG 2145) CGL policy shall include broad form contractual liability coverage for the Contractors covenants to and indemnification of the Authority under this Contract

Certificates of Insurance and the insurance policies required for this Agreement shall contain a provision under General Liability, Auto Liability and Workers' Compensation to include a Waiver of Subrogation clause in favor of Nassau County Board of County Commissioners.

All Certificates of Insurance shall be dated and shall show the name of the insured Contractor, the specific job by name and job number, the name of the insurer, the policy number assigned its effective date and its termination date and a list of any exclusionary endorsements.

All Insurers must be authorized to transact insurance business in the State of Florida as provided by Florida Statute 624.09(1) and the most recent Rating Classification/Financial Category of the insurer as published in the latest edition of "Best's Key Rating Guide' (Property-Casualty) must be at least A- or above.

All of the above referenced Insurance coverage is required to remain in force for the duration of this Agreement and for the duration of the warranty period. Accordingly, at the time of submission of final application for payment, Contractor shall submit an additional Certificate of Insurance evidencing continuation of such coverage.

If the Contractor fails to procure, maintain or pay for the required insurance, Nassau County Board of County Commissioners shall have the right (but not the obligation) to secure same in the name of and for the account of Contractor, in which event, Contractor shall pay the cost thereof and shall furnish upon demand, all information that may be required to procure such insurance. Nassau County Board of County Commissioners shall have the right to back-charge contractor for the cost of procuring such insurance. The failure of Nassau County Board of County Commissioners to demand certificates of insurance and endorsements evidencing the required insurance or to identify any deficiency in contractors coverage based on the evidence of insurance provided by the contractor shall not be construed as a waiver by Nassau County Board of County Commissioners of contractor's obligation to procure, maintain and pay for required insurance.

The insurance requirements set forth herein shall in no way limit Contractors liability arising out of the work performed under the Agreement or related activities. The inclusions, coverage and limits set forth herein are minimum inclusion, coverage and limits. The required minimum policy limits set forth shall not be construed as a limitation of Contractor's right under any policy with higher limits, and no policy maintained by the Contractor shall be construed as limiting the type, quality or quantity of insurance coverage that Contractor should maintain. Contractor shall be responsible for determining appropriate inclusions, coverage and limits, which may be in excess of the minimum requirements set forth herein.

If the insurance of any Contractor or any subcontractor contains deductible(s), penalty(ies) or self-insured retention(s), the Contractor or Subcontractor whose insurance contains such provision(s) shall be solely responsible for payment of such deductible(s), penalty(ies) or self-insured retention(s).

The failure of Contractor to fully and strictly comply at all times with the insurance requirements set forth herein shall be deemed a material breach of the Agreement.

EXHIBIT 2 CONTRACTOR'S BID

SECTION 00 41 15

BID FORM

PROJECT IDENTIFICATION:	Stokes Road Bridge Repair over St. Mary's River Bid Number NC19-027 Nassau County, Florida
BID DEADLINE:	Tuesday, February 04, 2020
THIS BID IS SUBMITTED TO:	Board of County Commissioners, Nassau County Judicial Annex Office of the Ex-Officio Clerk 76347 Veterans Way, Suite 456 Yulee, Florida 32097

1.01 The undersigned Bidder proposes and agrees, if this Bid is accepted, to enter into an agreement with the County in the form included in the Bidding Documents to perform all Work as specified or indicated in the Bidding Documents for the prices and within the times indicated in this Bid and in accordance with the other terms and conditions of the Bidding Documents.

Company Name (typed or printed): CPR Contracting LLC Business address: 11468 New Berlin Rd Jacksenulle FL 32226
Business address: 11468 New Berlin Rd Jacksonulle FL 32226
Phone No.: 904 - 723 - 3500 Fax No.: 904 - 723 - 3505
Contact Name: Max Ajelm
Contact Title: <u>Roject Manager</u> Contact email address: <u>Max & Cipt Contracting</u> . Cam
Contact email address: Max @ COTCONTRACTING. COM

- 2.01 Bidder accepts all of the terms and conditions of the Advertisement or Invitation to Bid and Instructions to Bidders, including without limitation those dealing with the disposition of Bid security. The Bid will remain subject to acceptance for 90 days after the Bid opening, or for such longer period of time that Bidder may agree to in writing upon request of the County.
- 3.01 In submitting this Bid, Bidder represents, as set forth in the Agreement, that:
 - A. Bidder has examined and carefully studied the Bidding Documents, the other related data identified in the Bidding Documents, and the following Addenda, receipt of all which is hereby acknowledged:

Invitation	to	Bid
mvilation	ιu	DIG

Addendum No.	Addendum Date
Addendum No. Haderdum # 1	January 21,2020
	1 -

- B. Bidder has visited the Site and become familiar with and is satisfied as to the general, local and Site conditions that may affect cost, progress, and performance of the Work.
- C. Bidder is familiar with and is satisfied as to all federal, state and local Laws and Regulations that may affect cost, progress and performance of the Work.
- D. Bidder has carefully studied all: (1) reports of explorations and tests of subsurface conditions at or contiguous to the Site and all drawings of physical conditions in or relating to existing surface or subsurface structures at or contiguous to the Site (except Underground Facilities) which have been identified in the Supplementary Conditions as provided in paragraph 4.02 of the General Conditions, and (2) reports and drawings of a Hazardous Environmental Condition, if any, which has been identified in the Supplementary Conditions as provided in paragraph 4.06 of the General Conditions.
- E. Bidder has obtained and carefully studied (or assumes responsibility for having done so) all additional or supplementary examinations, investigations, explorations, tests, studies. and data concerning conditions (surface, subsurface and Underground Facilities) at or contiguous to the Site which may affect costs, progress, or performance of the Work or which relate to any aspect of the means, methods, techniques, sequences, and procedures of construction to be employed by Bidder, including applying the specific means, methods, techniques, sequences, and procedures of construction expressly required by the Bidding Documents to be employed by Bidder, and safety precautions and programs incident thereto.
- F. Bidder does not consider that any further examinations, investigations, explorations, tests, studies, or data are necessary for the determination of this Bid for performance of the Work at the price(s) bid and within the times and in accordance with the other terms and conditions of the Bidding Documents.
- G. Bidder is aware of the general nature of the work to be performed by the County and others at the Site that relates to the Work as indicated in the Bidding Documents.
- H. Bidder has correlated the information known to Bidder, information and observations obtained from visits to the Site, reports and drawings identified in the Bidding Documents, and all additional examinations, investigations, explorations, tests, studies, and data with the Bidding Documents.

NASSAU COUNTY BOARD OF COUNTY COMMISSIONERS Contract Management Department 96135 Nassau Place, Suite 2 Yulee, Florida 32097 904-530-6040 Grayson Hagins ghagins@nassaucountyfl.com

All Proposers
Grayson Hagins, Contract/Purchasing Manager
Addendum #1
Invitation to Bid, Bid Number NC19-027
Stokes Rd. Bridge Repair
January 21, 2020

REMINDER: This addendum must be acknowledged, on the Bid Form Section 00-41-15, Article 3.01.A. Failure to comply may result in disqualification of your submittal.

This addendum is hereby incorporated into the bid documents of the project referenced above. The following items are clarifications, corrections, additions, deletions and/or revisions to, and shall take precedence over, the original documents.

Part 1 – Questions & Answers

Can you tell me if the Board of Commissioners has a budgeted amount established for the above referenced project? I was not able to locate this budgetary number on bid docs or public record.

Answer: The engineer's construction estimate for this project is \$474,505.40

Part 2 - Clarifications

THERE WILL BE NO PRE-BID MEETING FOR THIS PROJECT

ATTACHMENTS:

N/A

NOTE: You are required to acknowledge receipt of this addendum on the Bid Form, Section 00-41-15, Article 3.01.A.

1

End of Addendum #1

- 1. Bidder has given Engineer of Record written notice of all conflicts, errors, ambiguities, or discrepancies that Bidder has discovered in the Bidding Documents, and the written resolution thereof by Engineer of Record is acceptable to Bidder.
- J. The Bidding Documents are generally sufficient to indicate and convey understanding of all terms and conditions for the performance of the Work for which this Bid is submitted.
- 4.01 Bidder further represents that this Bid is genuine and not made in the interest of or on behalf of any undisclosed individual or entity and is not submitted in conformity with any agreement or rules of any group, association, organization or corporation; Bidder has not directly or indirectly induced or solicited any other Bidder to submit a false or sham Bid; Bidder has not solicited or induced any individual or entity to refrain from bidding; and Bidder has not sought by collusion to obtain for itself any advantage over any other Bidder or over the County.
- **5.01** Bidder will complete the Work in accordance with the Contract Documents for the following price(s):

BID TAB [STOKES ROAD BRIDGE REPAIR OVER ST. MARY'S RIVER]

	Summary of Pay Items			
ltem Number	Item Description	Unit	Quantity	Quantity Total
0101-1	Mobilization	LS	1.000	1.000
0102-1	Maintenance of Traffic	LS	1.000	1.000
0104-11	Turbidity Barrier	LF	200.00	200.00
401-70-4	Restore Spalled Area, Portland Cement Grout	CF	10.00	10.00
0457-1-11	Standard Integral Pile Jacket, Non-Structural, Up to 16"	LF	236.00	236.00

BASE BID TOTAL	L	017 000 00	
TOTAL AMOUNT	(PAY ITEMS)	s 217,000.00	
Two +	fundred	Seventeen Thousand Dollars	
		(Use Words)	

All specific cash allowances are included in the price(s) set forth above and have been computed in accordance with paragraph 11.02 of the General Conditions.

Unit prices have been computed in accordance with Paragraph 11.03.B of the General Conditions.

Bidder acknowledges that estimated quantities are not guaranteed, and are solely for the purpose of comparison of Bids. Final payment of all Unit Price Bid Items will be based on actual quantities as determined in the Contract Documents.

6.01 Bidder agrees that the Work will be substantially complete within <u>60</u> calendar days after the date when the Contract Times commence to run as provided in paragraph 2.03 of the General Conditions and completed and ready for final payment in accordance with paragraph 14.07.B of the General Conditions within <u>30</u> calendar days from the date of substantial completion. Total contract time shall be <u>90</u> calendar days; for everyday the work goes beyond substantial completion, a day will be removed from final completion so the total days equal <u>90</u> calendar days.

Invitation to Bid	Stokes Road Bridge Repair over St. Mary's River	BID NC19-027
-------------------	---	--------------

- **6.02** Bidder accepts the provisions of the Agreement as to liquidated damages in the event of failure to complete the Work within the times specified above, which shall be stated in the Agreement.
- 7.01 The following documents are attached to and made a condition of this Bid:
 - A. Bid Security in the form of a certified check of Bid Bond (Section 00 43 15)
 - B. Tabulation of Subcontractors & Suppliers (Section 00 43 35)
 - C. Florida Trench Safety Act Certification (Section 00 44 55)
 - D. Bidder's Qualification Statement (Section 00 45 13)
 - E. Non-collusion Affidavit (Section 00 45 19)
 - F. Drug-Free Workplace Certificate (Section 00 45 20)
 - G. Public Entity Crimes Statement
 - H. Statement of Disputes, Litigation & Surety Completion
 - I. Certificate of Insurance (See Exhibit 1 for coverages)
- **8.01** The terms used in this Bid with initial capital letters have the meanings indicated in the Instructions to Bidders, the General Conditions, and the Supplementary Conditions.

Invitation to Bid	Stokes Road Bridge Repair over St. Mary's River	BID NC19-027
T.	200	
SUBMITTED on 10	-juary , 20 <u>10</u> .	
State Contractor Lice	nse No. CGC 1518320	,
If Bidder is:		
An Individual		
Name (typed	or printed):	
By:	· · · · · · · · · · · · · · · · · · ·	
	(Individual's Signature)	
	(marriadar o orginalar o f	
	56.261	
	ss as:	
Business addi	ress:	
Phone No.:	Fax No.:	
<u>A Partnership</u>		
Partnership N	lame:	
Ву:		
	(Signature of general partner - attach evidence of autho	prity to sign)
Name (typed	or printed):	
	ress:	
Dusiliess duur		
Phone No.:	Fax No.:	
August 1		

ų,

Invitation to Bid	Stokes Road Bridge Repair over St.	Mary's River	BID NC19-027
A Corporation	000		
	Name: CPR Contract	ing 4C	. (SEAL)
	I Business, Professional, Service, Limi	ited Liability): <u>Limt</u>	Ird Liability
Name (typed	(Signature - attach evidence of autors)		
Title: 10	ect Manager MIC	(CORPO	RATE SEAL)
Attest	(Signature of Corporate Secretary))	
Business add		lin Rd. 32226	
Phone No.:	904 - 723 - 3500 Fa	ax No.: <u>904 - 72</u>	23-3505
Date of Quali	fication to do business is $_$ Oc+	. 2009	<u></u>

SYNOVUS Synovus Bank, Mensiber FDIC	OFFICIAL CHECK	100	00291844
		DATE February 04, 2020	<u>64-60</u> 611
WY TEN THOUSAND EIGHT HUNDRED FIFT	TY DOLLARS AND ZERO	CENTS	
o HE Board of County Commissioners ADER Nassau County	5	\$******10,850	.00
REMITTER Cor Contracting, LLC FOR Bid Bond		10 yer	\leq
ayable through synovus bank columbus, georgia		AUTHORIZED SIGNATURE	•
# 1000 29 184 4# 406 1	100606. 30	0135745#	
			O DELLOS SAMTHE

BID NC19-027

DAMAGES FORM

1. Bidder and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to pay to the County upon default of Bidder any difference between the total amount of Bidder's Bid and the total amount of the Bid of the next lowest, responsible Bidder who submitted a responsive Bid as determined by the County for the work required by the Contract Documents, provided that:

- 1.1. If there is no such next Bidder, and the County does not abandon the Project, then Bidder and Surety shall pay to the County the penal sum set forth on the face of this Bond, and
- 1.2. In no event shall Bidder's and Surety's obligation hereunder exceed the penal sum set forth on the race of this Bond.

2. Default of Bidder shall occur upon the failure of Bidder to deliver within the time required by the Bidding Documents (or any extension thereof agreed to in writing by the County) the executed Agreement required by the Bidding Documents and any performance and payment bonds required by the Bidding Documents.

3. This obligation shall be null and void if:

- 3.1. The County accepts Bidder's Bid and Bidder delivers within the time required by the Bidding Documents (or any extension thereof agreed to in writing by the County) the executed Agreement required by the Bidding Documents arid any performance and payment bonds required b) the Bidding Documents, or
- 3.2. All Bids are rejected by the County, or
- 3.3. The County fails to issue a Notice of Award to Bidder within the time specified in the Bidding Documents (or any extension thereof agreed to in writing by Bidder and, if applicable, consented to by Surety when required by Paragraph 5 hereof).

4. Payment under this Bond will be due and payable upon default by Bidder and within 30 calendar days after receipt by Bidder and Surety of written notice of default from the County, which notice will be given with reasonable promptness, identifying this Bond and the Project and including a statement of the amount clue.

5. Surety waives notice of any and all defenses based on or arising out of any time extension to issue Notice of Award agreed to in writing by the County and Bidder, provided that the total time for issuing Notice of Award including extensions shall not in the aggregate exceed 120 days from Bid due date without Surety's written consent.

6. No suit or action shall be commenced under this Bond prior to 30 calendar days after the notice of default required in Paragraph 4 above is received by Bidder and Surety and in no case later than one year after Bid due date.

7. Any suit or action under this Bond shall be commenced only in a court of competent jurisdiction located in the slate in which the Project is located.

8. Notices required hereunder shall be in writing and sent to Bidder and Surety at their respective addresses shown on the face of this Bond. Such notices may be sent by personal delivery, commercial courier, or by United States Registered or Certified Mail, return receipt requested, postage pre-paid, and shall be deemed to be effective upon receipt by the party concerned.

9. Surety shall cause to be attached to this Bond a current and effective Power of Attorney evidencing the authority of the officer, agent, or representative who executed this Bond on behalf of Surety to execute, seal, and deliver such Bond and bind the Surety thereby.

10. This Bond is intended to conform to all applicable statutory requirements. Any applicable requirement of any applicable statute that has been omitted from this Bond shall be deemed to be included herein as if set forth at length. If any provision of this Bond conflicts with any applicable statute, then the provision of said statute shall govern and the remainder of this Bond that is not in conflict therewith shall continue in full force and effect.

11. The term "Bid" as used herein includes a Bid, offer, or proposal as applicable.

Invitation to Bid

BID NC19-027

SECTION 00 43 35

TABULATION OF SUBCONTRACTORS & SUPPLIERS

The undersigned states that the following is a full and complete list of the proposed subcontractors and suppliers on this Project and the class of work to be performed by each, and that such list will not be added to nor altered without written consent to the County through the Engineer.

	SUBCONTRACTOR OR SUPPLIER AND ADDRESS	CLASS OF WORK OR MATERIAL
1.	Five Stur Marine 2910 County Rd #501	Jacket Material
2.		
3.		
4.		
5.		
6.		
7.		

Contracting LLC BIDDER: By: lielw Name: ager 0 Title: Date:

SECTION 00 44 55

FLORIDA TRENCH SAFETY ACT CERTIFICATION

Bidder acknowledges that included in the various items of the proposal and in the Total Bid Price are costs for complying with the Florida Trench Safety Act (90-96, Laws of Florida) as modified October 1, 2008. The Bidder further identifies the costs to be summarized below:

1. Trench Safety Act Compliance

2. Special Shoring

Identify method of compliance for Item #1: __

Identify or attach a copy of Special Shoring requirements for Item #2:

The undersigned certifies that he/she is the Contractor who will perform the trench excavation for this project, and hereby gives written assurance that Contractor will comply with the applicable trench safety standards specifically set forth in Florida's Trench Safety Act, Laws of Florida, 90-96.

BIDDER: CPR Contracting LLC	
By: That to the	
Name: Max Hipm	
Title: Raject Managa	
Sworn to and subscribed before me this day of Contain _, 20_20	
Some	
Notary Public	
My Commission Expires: Sept 14, 2023	~~~
Stacle M Baird My Commission GG 349733 Expires 09/14/2023	Š

questions shall be answered fully. Bidders who have qualified to bid on other projects for this County within the last 12 months need not resubmit this form unless specifically requested by the County. The contents of this form will be considered confidential to the extent allowed by applicable laws and regulations. Name of Bidder: CPR CPR Contracting Mame of Bidder: Image: CPR Street 32226 City Street Street 32226 City State Zip Code 1. Number of years in business as a Contractor under the present: 10 Business Name CPR Centracting 4. As a Sub-Contractor 4. As a Sub-Contractor 6. Class of work you are equipped to perform: 6. General 6. Have you ever failed to qualify as a responsible bidder? 7. No. 16. Have you ever refused to enter into a contract after the award is made to you? 7. No.	Invitation to	Bid Stokes Road Bridge Repair over St. Mary's River BID NC19-027
b: Doard of County Commissingen: Stoker Road Bridge Repair Bid# NC 19-027 bate: WHY 2020 Nassau Co. Bid# NC 19-027 the following experience record, as of date shown, shall be submitted to the County with the Bid Form. All juestions shall be answered fully. Bidders who have qualified to bid on other projects for this County within he last 12 months need not resubmit this form unless specifically requested by the County. The contents of his form will be considered confidential to the extent allowed by applicable laws and regulations. Name of Bidder: CPR Confecting UC Street JackSonville FL Zip Code Number of years in business as a Contractor under the present: 10 Business Name CPR Confecting UC As Principal Contractor As a Sub-Contractor		SECTION 00 45 13
The following experience record, as of date shown, shall be submitted to the County with the Bid Form. All questions shall be answered fully. Bidders who have qualified to bid on other projects for this County within the last 12 months need not resubmit this form unless specifically requested by the County. The contents of this form will be considered confidential to the extent allowed by applicable laws and regulations. Name of Bidder: CPR Conffracting HC Business Address: 11468 New Berlin Rd Street 32226 City Street Jeck Sonville FL Business Name CPR Confracting HC Business Name CPR Confracting HC And Principal Contractor As a Sub-Contractor Class of work you are equipped to perform: Canstal Constitue tion Class of work you usually sublet: N/A Have any members of your concern ever operated under any other business name? NC Mave you ever failed to qualify as a responsible bidder? No Mave you ever refused to enter into a contract after the award is made to you? NS		
Stack Sonville FL 32226 City State Zip Code 1. Number of years in business as a Contractor under the present: 10 Business Name CPR Cantacting 100 Business Name CPR Cantacting 100 Business Name CPR Cantacting 100 As Principal Contractor	o: <u>BOA</u> Date: (24	d of Country Commissiongiest: Stoker Road Bridge Repair M/2020 Nassau Cu. Bid# NC 19-027
Business Address:	questions s the last 12	shall be answered fully. Bidders who have qualified to bid on other projects for this County within months need not resubmit this form unless specifically requested by the County. The contents of
Business Address: <u>11468 New Betlin Rd</u> <u>JackSonuille FL</u> <u>32226</u> City State <u>32226</u> 2 City <u>State</u> <u>32226</u> 2 City <u>State</u> <u>2 ip Code</u> 1. Number of years in business as a Contractor under the present: 10 Business Name <u>CPR Contracting LLC</u> As Principal Contractor <u>As a Sub-Contractor</u> <u>6 on Struction / Contracter</u> 2. Class of work you are equipped to perform: <u>General Con Struction / Contracter</u> 3. Class of work you usually sublet: <u>N/A</u> 4. Have any members of your concern ever operated under any other business name? <u>NC</u> . If so, give details: <u></u> 5. Have you ever failed to qualify as a responsible bidder? <u>NC</u> . If so, give details. <u></u> 5. Have you ever refused to enter into a contract after the award is made to you? <u>NC</u> . If so, give details.	Name of Bi	dder: CPR Contracting LLC
Jacksonville FL 32226 City State Zip Code 1. Number of years in business as a Contractor under the present: 10 Business Name CPR Contractor Under the present: 10 Business Name CPR Contracting LCC As Principal Contractor	Business A	ddress: 11468 New Berlin Rol
City State Zip Code 1. Number of years in business as a Contractor under the present: 10 Business Name CPR Contracting LUC As Principal Contractor		Jacksonville FL 32226
Business Name CPR Contracting_LLC As Principal Contractor		
As Principal Contractor As a Sub-Contractor		
 Class of work you usually sublet:		5
 Have any members of your concern ever operated under any other business name?	2. Cla	ss of work you are equipped to perform: <u>General Construction / (unatete</u>
If so, give details:	. Cla	ss of work you usually sublet:N
Have you ever refused to enter into a contract after the award is made to you? <u>NG</u> . If so, give details.	l. Ha If s	ve any members of your concern ever operated under any other business name? o, give details:
If so, give details.	 5. На	ve you ever failed to qualify as a responsible bidder? If so, give details.
Have you ever failed to complete any work? $\underline{\mathcal{NO}}$. If so, give details:		
	'. Hav	ve you ever failed to complete any work? <u>VO</u> . If so, give details:

	ion to Bid Stol	kes Road Bridge Repair over St. Mary's River	BID NC19-027
8.	Has any surety or finar If so, give details:	ncial institution ever experienced loss o	
9.	Give name and addres projects completed in	s of the County, type of work, and the c the last three years:	contract amount of at least three
	(1) (2)	(3)
Projec	t Owner: FDO	t Foor	St. Peter Varpt Club
Owner Manag Email:	•	Construction Superior Co	male. KCA
Phone		-4240 904.292.42	40 513-871-5331
Addres	· · · · · · · · · · · · · · · · · · ·	ness PK Blud 7072 Busing	
lackso	nville, FL, 32246:		
Contra 10.		s of the County, type of work, and contr	RESACUS Deck Repairs = Rie Ta \$ 485,020.
4	Name	Address	Type of Work Contract Amount
۹	FB. Carace	- Dwed Camb	Restriction \$ 7.7 mil
3	5887	Walton Coninty	Piles ceteta \$ 750,000
	Ocene 21/88	Dured Course	Slog Kostantian \$ 1.8 mil
)[E Hespitel		xt bedoepcosty \$ 685 000.
. 2	Sheritan	Dured Carry E	d. Bdy Rast. \$ 385.000.00
11.	Indicate your experien Questions 9 and 10, ab	ce in the construction of work similar to pove):	o this project (if not demonstrated by
	••••••••••••••••••••••••••••••••••••••		
	Give construction expe	rience of principal individuals of your o	rganization:
.2.	Give construction expe	incrice of principal individuals of your o	Earlization.
.2.	Name	Position Years of Expe	

itat	ion to Bid Stoke	s Road Bridge	Repair over St. Mar	y's River	BID NC19-027				
	B								
	Are there any judgment	s, suits, or cl	aims pending agai	nst you? _	No. If so, give details:				
	Does your organization	operate as a	corporation, parts	nership, oi	rindividual? Conference				
	A. If a corporation, whe	n incorporate	ed:	D9					
	In which state incorpora	ated:	Herride						
	List name, title, and address of all officers:								
	Name		Title		Address				
	(1) Josen Brusen	ut	Manue)146	S New Berlin Rd. 3200				
	,								
	(4)								
	B. If a partnership, date of organization:								
	General, Limited, or Associated?								
	List name, address, and proportional interest of parties:								
	Name	Add	ress		Proportional Interest				
	(1)								
	(3)								
	(5)				Lander 1				
	V-1	•	-unite		at a				

15. If requested prior to award of contract, provide to the County an accurate, up-to-date, condensed financial statement on a separate sheet attached to these qualifications of the individual, co-partnership, or corporation.

The undersigned hereby declares and certifies that the foregoing is a true statement of the experience and condition of the organization, therein first given and that any agency or individual herein named authorized to supply any information as may be deemed necessary to verify this statement.

Signed SCC Title ana Subscribed and sworn to before me this day of 206 Notary Public County, My Commission expires Notary Public State of Florida Stacie M Baird Ay Commission GG 349733 Expires 09/14/2023

Invitation	to	Bid
------------	----	-----

SECTION 00 45 19

NONCOLLUSION AFFIDAVIT

TO: The Owner here	in called the "County."
Pursuant to bidding requirements for the work titled "	NC 19-027
Stokes Rd. Bridge Re	
the enclosed contract documents shall be provided to	the County.
State of Flocida	
County of Nassau	
Max Hirlm	, being first duly sworn,
deposes, and says that:	
A. HeisProject Man	agt (officer's title)

of <u>CPR Constructing LC</u> (company name), the Bidder that has submitted the attached bid;

- Β. He is fully informed respecting the preparation and contents of the attached bid and of all pertinent circumstances respecting such bid;
- C. Such bid is genuine and is not a collusive or sham bid;
- D. Neither the said Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including this affiant, has in any way colluded, conspired, connived, or agreed, directly or indirectly with any other Bidder, firm, or person to submit a collusive or sham bid in connection with the contract for which the attached bid has been submitted or to refrain from bidding in connection with such contract, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached bid or of any other Bidder, or to fix any overhead, profit, or cost element of the bid price or the bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance, or unlawful agreement any advantage against the Uwnec or any person interested in the proposed contract; and
- Ε. The price or prices quoted in the attached bid are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners: employees, or parties in interest, including this affiant.

Invitation to Bid	Stokes Road Bridge Repair over St. Mary's River	BID NC19-027
	(Signed)	Aidin
	MA	x Hjelen
. Son	n to before me y of \underline{KMMM} , 20 \underline{W} .	
Notary Public	Notary Public State of Florida	
My commission exc	Stacle M Baird	

My commissio

Contract CM2831



ATTACHMENT K DRUG-FREE WORKPLACE CERTIFICATION

Preference shall be given to businesses with drug-free workplace programs. Pursuant to Section 287.087, Florida Statutes, whenever two or more competitive solicitations that are equal with respect to price, quality, and service are received by the State or by any political subdivision for the procurement of commodities or contractual services, a response received from a business that certifies that it has implemented a drug-free workplace program shall be given preference in the award process. Established procedures for processing tie responses will be followed if none of the tied providers has a drug free workplace program. In order to have a drug-free workplace program, a business shall:

- 1. Publish a statement notifying employees that the unlawful manufacture, distribution, dispensing, possession, or use of a controlled substance is prohibited in the workplace and specifying the actions that will be taken against employees for violations of such prohibition.
- 2. Inform employees about the dangers of drug abuse in the workplace, the business's policy of maintaining a drug-free workplace, any available drug counseling, rehabilitation, and employee assistance programs, and the penalties that may be imposed upon employees for drug abuse violations.
- 3. Give each employee engaged in providing the commodities or contractual services that are under proposal a copy of the statement specified in Subsection (1).
- 4. In the statement specified in Subsection (1), notify the employees that, as a condition of working on the commodities or contractual services that are under proposal, the employee will abide by the terms of the statement and will notify the employer of any conviction of, or plea of guilty or nolo contendere to, any violation of Chapter 894, Florida Statutes, or of any controlled substance law of the United States or any state, for a violation occurring in the workplace no later than five (5) days after such conviction.
- 5. Impose a sanction on any employee who is so convicted or require the satisfactory participation in a drug abuse assistance or rehabilitation program as such is available in the employee's community.

C P R C O N T R A C T I N G , L L C . 11468 New Berlin Rd Jacksonville, Florida 32226 Ph# 904-723-3500 Fx# 904-723-3505



6. Make a good faith effort to continue to maintain a drug-free workplace through implementation of applicable laws, rules and regulations.

As the person authorized to sign the statement, I certify that this firm complies fally with the above requirements.

JSINESS NAME

PROVIDER'S SIGNATURE

BID NC19-027

SECTION 00 45 30

SWORN STATEMENT UNDER SECTION 287.133(3)(a), FLORIDA STATUTES, ON PUBLIC ENTITY CRIMES

(To be signed in the presence of a notary public or other officer authorized to administer oaths.)

STATE OF Flosida
COUNTY OF Nassau
Before me, the undersigned authority, personally appeared $\underline{Max Helm}$, who being by me first duly sworn, made the following statement:
1. The business address of CPR Contracting, LLC
is 11468 New Berlin Rd Jacksonwille FL 32226
2. My relationship to CPR Contracting LLC
is Project Manager (Civil Services, Inc. of Bidder/Contractor)
(relationship such as sole proprietor, partner, president, vice president)

3. I understand that a public entity crime as defined in Section 287.133 of the Florida Statutes includes a violation of any state or federal law by a person with respect to and directly related to the transaction of business with any public entity in Florida or with an agency or political subdivision of any other state or with the United States, including, but not limited to, any bid or contract for goods or services to be provided to any public entity or such an agency or political subdivision and involving antitrust, fraud, theft, bribery, collusion, racketeering, conspiracy, or material misrepresentation.

4. I understand that "convicted" or "conviction" is defined by the statute to mean a finding of guilt or a conviction of a public entity crime, with or without adjudication or guilt, in any federal or state trial of record relating to charges brought by indictment or information after July 1, 1989, as a result of a jury verdict, nonjury trial, or entry of a plea of guilty or nolo contendere.

5. I understand that "affiliate" is defined by the statute to mean (1) a predecessor or successor of a person or a corporation convicted of a public entity crime; or (2) an entity under control of any natural person with is active in management of the entity and who has been convicted of a public entity crime; (3) those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in the management of an affiliate; or (4) a person or corporation who knowingly entered into a joint venture with a person who has been convicted of a public entity crime in Florida during the preceding 36 months.

6. Neither the Bidder/Contractor nor any officer, director, executive, partner, shareholder, employee, member or agent who is active in the management of the Bidder/Contractor, nor any affiliate of the Bidder/Contractor, has been convicted of a public entity crime subsequent to July 1, 1989.

(Draw a line through Paragraph 6 if Paragraph 7 below applies.)

There has been a conviction of a public entity crime by Bidder/Contractor, or an officer, director, executive, partner, shareholder, employee, member or agent of the Bidder/Contractor who is active in the management of the Bidder/Contractor or an affiliate of the Bidder/Contractor. A determination has been made pursuant to 287.133(3) by order of the Division of Administrative Hearings that it is not in the public interest of the name of the convicted person or affiliate to appear on the convicted vendor list.

The name of the convicted person or affiliate is ______

A copy of the order of the Division of Administrative Hearings is attached to this statement.

(Draw a line through Paragraph 7 if Paragraph 6 above applies.)

Signature)

Sworn to and subscribed before me in the State and County first mentioned above on the H

2070 day of Notary Public chiles 08/14/2023

Roir

My commission

EELEVE DO LOI

A COMM

DIRE W BORK

Public Sh

ffix seal) Notary Public State of Florida Stacle M Baird aion GG 349733 09/14/2023

	Clien	#: 1!	53				CONC	RPRES	-	5. 2
ACORD				TE OF LIAB		Y INSI	JRAN	CE		M/DD/YYYY)
ACORD _{TM} CERTIFICATE OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER. IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the										
certificate holder in lie							5. mm			
PRODUCER Construction Underwi 4168 Southpoint Pkwy					CONTA NAME: PHONE (A/C, N E-MAIL ADDRE	o, Ext): 904-29 ss: rgately	6-3343		904-2	96-3430
Jacksonville, FL 3221	6							FORDING COVERAGE		NAIC #
INSURED					_	ERA : Importum In:	a subject to a			35408 19488
CPR Contra	cting, LLC; JB	1.2				ER B : Amoriaure In ER C : AGCS Marine	••••••••••••••••••••••••••••••••••	ny		22837
	reservation & I	Repa	ir, Ll	_C		ER D : Landmark A		······································		33138
11468 New					INSURE	ER E :				
Jacksonville	-				INSURI	IRF:				L
INDICATED. NOTWITHST CERTIFICATE MAY BE IS	AT THE POLICIES ANDING ANY RE	OF QUIRE PERTA	INSUF	NUMBER: RANCE LISTED BELOW HAV T, TERM OR CONDITION OF THE INSURANCE AFFORDED LIMITS SHOWN MAY HAV	F ANY D BY T	CONTRACT O	THE INSURED R OTHER DO DESCRIBED 1	CUMENT WITH RESPECT HEREIN IS SUBJECT TO /	TO WH	ICH THIS
INSR TYPE OF INSU	JRANCE	ADDL	SUBR	POLICY NUMBER		POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	s	
A X COMMERCIAL GENE				IERD0100208403				EACH OCCURRENCE	\$1,00	0,000
CLAIMS-MADE				EBL				DAMAGE TO RENTED PREMISES (Ea occurrence)	\$300,	000
X Binkt Addi Ins	d			Ongoing&Comp Ops				MED EXP (Any one person)	\$10,0	the second se
X Binkt WOS				Contractual Liab				PERSONAL & ADV INJURY		0,000
GEN'L AGGREGATE LIMIT	[]							GENERAL AGGREGATE		0,000
								PRODUCTS - COMP/OP AGG	\$2,00	0,000
A AUTOMOBILE LIABILITY	· , · · · · · · · · · · · · · · · · · ·			IERD0100208303 Binkt Addi Insd		02/15/2019	02/15/2020	COMBINED SINGLE LIMIT (Ea accident) BODILY INJURY (Per person)	s1,00	0,000
ALL OWNED AUTOS X HIRED AUTOS X	SCHEDULED AUTOS NON-OWNED AUTOS			Binkt WOS \$10,000 PIP				BODILY INJURY (Per accident) PROPERTY DAMAGE (Per accident)	\$ \$	
X 1000 Comp Ded X	1000 Coll Ded								s	
A X UMBRELLA LIAB	X OCCUR			IERD0100208503		02/15/2019	02/15/2020	EACH OCCURRENCE	1	0,000
EXCESS LIAB	CLAIMS-MADE			XS of GL/Auto/WC				AGGREGATE		0,000
D DED X RETENTI B WORKERS COMPENSATIO AND EMPLOYERS' LIABILI	N			LHA082123 WC2086095		02/15/2019 02/15/2019		Excess Liab X PER STATUTE OTH- ER	\$1,00	0,000
AND EMPLOYERS' LIABIL ANY PROPRIETOR/PARTNE OFFICER/MEMBER EXCLUD	RVEXECUTIVE N	N/A		USL&H included				E.L. EACH ACCIDENT	\$100,	
(Mandatory in NH) If yes, describe under DESCRIPTION OF OPERAT	the second se			Binkt WOS				E.L. DISEASE - EA EMPLOYEE		
	IONS below			IIV/0207002/0002		00/45/0040	0014 510000	EL DISEASE - POLICY LIMIT	\$500,	000
C Scheduled Equip C Rented Equip				MXI930798240963 MXI930798240963 Special Form		Contraction of the second contraction of the second		0 See Value Below 0 \$150,000/\$300,000 DED:\$5000Cranes\$1000AOP		
DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)										
CERTIFICATE HOLDER			CANCELLATION					<u></u>		
Info Only						SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.				
						RIZED REPRESE				
				Regina S. Stotely						

@ 1988-2014 ACORD CORPORATION. All rights reserved.

Invitation to Bid

Stokes Road Bridge Repair over St. Mary's River

BID NC19-027

SECTION 00 45 35

BIDDER'S STATEMENT OF DISPUTES, LITIGATION, ARBITRATION, AND SURETY COMPLETION, LAST THREE (3) YEARS

 Name and Phone of

 Name and Address of
 Owner or Engineer
 Date of

 Project
 Owner or Engineer
 Contract
 Amount
 Status

NIA

(Signed) Print Name

Subscribed and sworn to before me 20 20 day of Unuan this Notary Publ My commission expires :

y Public State of Florida e M Baird Co mission GG 349733 09/14/2023

SECTION 00 51 00

NOTICE OF AWARD

TO: <u>CPR Contracting, LLC</u> CONTRACTOR

> 11468 New Berlin Rd ADDRESS

Jacksonville Florida 32226 CITY STATE ZIP

PROJECT: Stokes Road Bridge Repair over St. Mary's River NAME

The Nassau County Board of County Commissioners has considered the recommendation to accept the Bid submitted by <u>CPR Contracting, LLC</u> for the above described work in response to its Invitation to Bid (ITB), <u>Bid No. NC19-027</u>, opened on <u>February 5, 2020</u>.

You are hereby notified that the Bid has been accepted and the Nassau County Board of County Commissioners has executed the enclosed agreement subject to: Receipt of the applicable bonds and Certificate(s) of Insurance, within ten (10) calendar days from the date of this Notice of Award and receipt of the fully executed agreement. The bonds are required to be recorded at cost to the contractor. The bonds must be recorded within the same ten (10) day period referenced herein. The Clerk of Courts does not accept company or personal checks unless the signee is present and can provide identification.

If you fail to furnish the bonds and the Certificate of Insurance within ten (10) calendar days from the date of this Notice, the County will be entitled to consider any rights arising out of the County's acceptance of your Bid as abandoned and void.

You are required to return an acknowledged copy of this Notice of Award, Bonds, and Insurance Certificates to the Nassau County Board of County Commissioners, c/o John A. Crawford, Ex-Officio Clerk, 76347 Veterans Way, Yulee, Florida 32097. A copy must be sent to Nassau County, Procurement Manager, at 96135 Nassau Place, Suite 6, Yulee, Florida 32097.

Dated this 17th day April , 20 20. Nassau County Board of County Commissioners BY: Chairman TITLE:

ACCEPTANCE OF NOTICE

. Josen Baisquet Receipt of the above Notice of Award is hereby acknowledged by Crrc this ______, 20 20 TITLE: MOME BY:

PERFORMANCE BOND

Any singular reference to Contractor, Surety, Owner, or other party shall be considered plural where applicable.

CONTRACTOR (*Name and Address*): CPR Contracing, LLC 11468 New Berlin Rd Jacksonville, FL 32226 (904) 723-3500

OWNER (Name and Address): Nassau County BOCC 96135 Nassau Place Yulee, FL 32097 (904) 530-6010 SURETY (*Name, and Address of Principal Place of Business*): American Southern Insurance Company 365 Northridge Rd, Ste 400 Atlanta, GA 30350 (404) 522-3898

CONTRACT

Effective Date of Agreement: 04/13/2020

Amount: \$217,000.00

Description (Name and Location): Stokes Road Bridge over St. Mary's River Bridge No. 744001

BOND

Bond Number: 67905 Date (*Not earlier than Effective Date of Agreement*): 06/04/2020 Amount: \$217,000.00 Modifications to this Bond Form: N/A

> Inst: 202045016953 Date: 06/05/2020 Time: 10:29AM Page 1 of 6 B: 2366 P: 1, Doc Type: UNK John A. Clawford, Clerk of Court, Nassau County, By: TS, Deputy Clerk



Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth below, do each cause this Performance Bond to be duly executed by an authorized officer, agent, or representative.

CO	N1	FR	ACT	OR	AS	PRIN	ICIPAL
				v ii	20	1 1211.	I SII AL

SURETY

CPR Contracting, LLC	(Seal)	American Southern Insurance Company
Contractor's Name and Corporate Seal		- Surety's Name and Corporate Seal NCE.CO
By: Signature Mean Drusz		By: Signature (Attach Power of Attorney)
Print Name		Print Name
MEMIC / Ome	/	Attorney-in-Fact
Attest:		Attest:
Title		Witness ALARE SKAFF

Note: Provide execution by additional parties, such as joint venturers, if necessary.

EJCDC No. C-610 (2007 Edition)

Originally prepared through the joint efforts of the Surety Association of America, Engineers Joint Contract Documents Committee, the Associated General Contractors of America, and the American Institute of Architects.

> Jason S. Centrella Florida Res. Agent #A300489 P.O. Box 600962 Jacksonville, FL 32260 904-230-1324

> > ć,

Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to Owner for the performance of the Contract, which is incorporated herein by reference.

If Contractor performs the Contract, Surety and Contractor have no obligation under this Bond, except to participate in conferences as provided in Paragraph 2.1.

If there is no Owner Default, Surety's obligation under this Bond shall arise after:

- Owner has notified Contractor and Surety, at the addresses described in Paragraph 9 below, that Owner is considering declaring a Contractor Default and has requested and attempted to arrange a conference with Contractor and Surety to be held not later than 15 days after receipt of such notice to discuss methods of performing the Contract. If Owner, Contractor, and Surety agree, Contractor shall be allowed a reasonable time to perform the Contract, but such an agreement shall not waive Owner's right, if any, subsequently to declare a Contractor Default; and
- Owner has declared a Contractor Default and formally terminated Contractor's right to complete the Contract. Such Contractor Default shall not be declared earlier than 20 days after Contractor and Surety have received notice as provided in Paragraph 2.1; and

Owner has agreed to pay the Balance of the Contract Price to:

Surety in accordance with the terms of the Contract; or

Another contractor selected pursuant to Paragraph 3.3 to perform the Contract.

When Owner has satisfied the conditions of Paragraph 2, Surety shall promptly, and at Surety's expense, take one of the following actions:

Arrange for Contractor, with consent of Owner, to perform and complete the Contract; or

- Undertake to perform and complete the Contract itself, through its agents or through independent contractors; or
- Obtain bids or negotiated proposals from qualified contractors acceptable to Owner for a contract for performance and completion of the Contract, arrange for a contract to be prepared for execution by Owner and contractor selected with Owner's concurrence, to be secured with performance and payment bonds executed by a qualified surety equivalent to the bonds issued on the Contract, and pay to Owner the amount of damages as described in Paragraph 5 in excess of the Balance of the Contract Price incurred by Owner resulting from Contractor Default; or
- Waive its right to perform and complete, arrange for completion, or obtain a new contractor, and with reasonable promptness under the circumstances:

After investigation, determine the amount for which it may be liable to Owner and, as soon as practicable after the amount is determined, tender payment therefor to Owner; or

Deny liability in whole or in part and notify Owner citing reasons therefor.

If Surety does not proceed as provided in Paragraph 3 with reasonable promptness, Surety shall be deemed to be in default on this Bond 15 days after receipt of an additional written notice from Owner to Surety demanding that Surety perform its obligations under this Bond, and Owner shall be entitled to enforce any remedy available to Owner. If Surety proceeds as provided in Paragraph 3.4, and Owner refuses the payment tendered or Surety has denied liability, in whole or in part, without further notice Owner shall be entitled to enforce any remedy available to Owner.

After Owner has terminated Contractor's right to complete the Contract, and if Surety elects to act under Paragraph 3.1, 3.2, or 3.3 above, then the responsibilities of Surety to Owner shall not be greater than those of Contractor under the Contract, and the responsibilities of Owner to Surety shall not be greater than those of Owner under the Contract. To the limit of the amount of this Bond, but subject to commitment by Owner of the Balance of the Contract Price to mitigation of costs and damages on the Contract, Surety is obligated without duplication for:

- The responsibilities of Contractor for correction of defective Work and completion of the Contract;
- Additional legal, design professional, and delay costs resulting from Contractor's Default, and resulting from the actions of or failure to act of Surety under Paragraph 3; and
- Liquidated damages, or if no liquidated damages are specified in the Contract, actual damages caused by delayed performance or non-performance of Contractor.

Surety shall not be liable to Owner or others for obligations of Contractor that are unrelated to the Contract, and the Balance of the Contract Price shall not be reduced or set off on account of any such unrelated obligations. No right of action shall accrue on this Bond to any person or entity other than Owner or its heirs, executors, administrators, or successors.

Surety hereby waives notice of any change, including changes of time, to Contract or to related subcontracts, purchase orders, and other obligations.

Any proceeding, legal or equitable, under this Bond may be instituted in any court of competent jurisdiction in the location in which the Work or part of the Work is located, and shall be instituted within two years after Contractor Default or within two years after Contractor ceased working or within two years after Surety refuses or fails to perform its obligations under this Bond, whichever occurs first. If the provisions of this paragraph are void or prohibited by law, the minimum period of limitation available to sureties as a defense in the jurisdiction of the suit shall be applicable.

Notice to Surety, Owner, or Contractor shall be mailed or delivered to the address shown on the signature page.

When this Bond has been furnished to comply with a statutory requirement in the location where the Contract was to be performed, any provision in this Bond conflicting with said statutory requirement shall be deemed deleted herefrom and provisions conforming to such statutory requirement shall be deemed incorporated herein. The intent is that this Bond shall be construed as a statutory bond and not as a common law bond.

Definitions.

- Balance of the Contract Price: The total amount payable by Owner to Contractor under the Contract after all proper adjustments have been made, including allowance to Contractor of any amounts received or to be received by Owner in settlement of insurance or other Claims for damages to which Contractor is entitled, reduced by all valid and proper payments made to or on behalf of Contractor under the Contract.
- Contract: The agreement between Owner and Contractor identified on the signature page, including all Contract Documents and changes thereto.

Contractor Default: Failure of Contractor, which has neither been remedied nor waived, to perform or otherwise to comply with the terms of the Contract.

Owner Default: Failure of Owner, which has neither been remedied nor waived, to pay Contractor as required by the Contract or to perform and complete or otherwise comply with the other terms thereof.

FOR INFORMATION ONLY – (*Name, Address and Telephone*) Surety Agency or Broker: Owner's Representative (*Engineer or other party*):

> Jason S. Centrella Florida Res. Agent #A300489 P.O. Box 600962 Jacksonville, FL 32260 904-230-1324

AMERICAN SOUTHERN INSURANCE COMPANY

Home Office: 3715 Northside Parkway, NW Suite 4-800 Atlanta, Georgia 30327

Mailing Address: P. O. Box 723030 Atlanta, GA 31139-0030

GENERAL POWER OF ATTORNEY

Know all men by these Presents, that the American Southern Insurance Company had made, constituted and appointed, and by these presents does make, constitute and appoint Stefan E. Tauger of Parker, Colorado; Scott E. Stoltzner of Hoover, Alabama; Arthur S. Johnson of Atlanta, Georgia; Andrew C. Heaner of Atlanta, Georgia; Jeffery L. Booth of Blacklick, Ohio; James E. Feldner of West Lake, Ohio; David R. Brett of Columbia, South Carolina; Melanie J. Stokes of Atlanta, Georgia; Jason S. Centrella of Jacksonville, Florida; Michael J. Brown of Cumming, Georgia; Tamara D. Johnson of Atlanta, Georgia; Omar G. Guerra of Overland Park, Kansas; or Douglas B. Miller, Florida, EACH as its true and lawful attorney for it and its name, place and stead to execute on behalf of the said company, as surety, bonds, undertakings and contracts of suretyship to be given to all obligees provided that no bond or undertaking or contract of suretyship executed under this authority shall exceed in amount of the sum of \$1,000,000 (one million dollars), including but not limited to consents of surety for the release of retained percentages and/or final estimates on construction contracts or similar authority requested by the Department of Transportation, State of Florida; and the execution of such undertakings, bonds, recognizances and other surety obligations, in pursuance of the presents, shall be as binding upon the Company as if they had been duly signed by the President and attested by the Secretary of the Company in their own proper persons.

This Power of Attorney is granted and is signed and sealed by facsimile under and by the authority of the following Resolution adopted pursuant to due authorization by the Executive Committee of the Board of Directors of the American Southern Insurance Company on the 26th day of May, 1998;

RESOLVED, that the Chairman, President or any Vice President of the Company be, and that each or any of them hereby is, authorized to execute Powers of Attorney qualifying the attorney named in the given Power of Attorney to execute in behalf of the American Southern Insurance Company bonds, undertakings and all contracts of suretyship; and that any Secretary or any Assistant Secretary be, and that each or any of them hereby is, authorized to attest the execution of any such Power of Attorney, and to attach thereto the seal of the Company.

FURTHER RESOLVED, that the signature of such officers and the seal of the Company may be affixed to any such Power of Attorney or to any certificate relating thereto by facsimile, and any such Power of Attorney or certificate bearing such facsimile signatures or facsimile seal shall be valid and binding upon the Company when so affixed and in the future. with respect to any bond undertaking or contract of suretyship to which it is attached.

In Witness Whereof, the American Southern Insurance Company has caused its official seal to be hereto affixed, and these presents to be signed by its President and attested by its Secretary this 22nd day of _____ March 2019

OUTHERN INSCORES CORPORTS

Melonie A. Coppola, Secretary STATE OF GEORGIA SS: COUNTY OF FULTON On this 22nd day of <u>March 2019</u>, before me parsonally came Scott G. Thompson to me known, who being by me duly sworn, did depose and say that he resides in Atlanta, in the County of Fulton, State of Georgia, at 421 Hollydale Court; that he is the President of American Southern Insurance Company, the corporation described in and which executed the above instrument; that he knows the seal of the said corporation; that the early and the signed his name thereto pursuant to due authorization. THAN B State of mission OWATHAN BO

STATE OF GEORGIA

Power No.

COUNTY OF FULTON

47087

American Southern Insurance Company

iny, the corporation described in and which executed the above instrument; that he knows the seal of the said corporation; that the foregoing ached Power of Attorney remains in full force and has not been revoked; and, furthermore, that the Resolution of the Executive Committee of the said corporation. and attached Power of Attorney remains in full force and has not been revoked; and, furthermore, that the Resolution of the Executive Committee of the Board of Directors set forth in the Power of Attorney is now in forcer TH_{day of}

Signed and sealed at the City of Atlanta, Dated the

eny a Under lerry A. Underwood **/ice President**

PAYMENT BOND

Any singular reference to Contractor, Surety, Owner, or other party shall be considered plural where applicable.

CONTRACTOR (*Name and Address*): CPR Contracting, LLC 11468 New Berlin Rd Jacksonville, FL 32226 (904) 723-3500

OWNER (Name and Address): Nassau County BOCC 96135 Nassau PI, Yulee, FL 32097 (904) 530-6010 CONTRACT Effective Date of Agreement: 04/13/2020 SURETY (Name, and Address of Principal Place of Business):

American Southern Insurance Company 365 Northridge Rd, Ste 400 Atlanta, GA 30350 (404) 522-3898

Amount: \$217,000.00 Description (Name and Location): Stokes Road Bridge over St. Mary's River Bridge No. 744001

BOND

Bond Number: 67905 Date (Not earlier than Effective Date of Agreement): 06/04/20 Amount: \$217,000.00 Modifications to this Bond Form: This bond is hereby amended so that the provisions and limitations

of Section 255.05 or Section 713.23, Florida Statutes, whichever is applicable, are incorporated herein by reference.

Inst: 202045016954 Date: 06/05/2020 Time: 10:29AM Page 1 of 4 B: 2366 P: 7, Doc Type: UNK John A. Crawford, Clerk of Court, Nassau County, By: TS, Deputy Clerk



Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth below, do each cause this Payment Bond to be duly executed by an authorized officer, agent, or representative.

CONTRACTOR AS PRINCIPAL

SURETY

CPR C	contracting, LLC	(Seal) Ame	rican Southern Insurance Company	(Seal)
Contractor's Name and Corporate Seal		Sure	Surety's Name and Corporate Seal	
By:	min	By:	N	NULLERCO, MA
	Signature		Signature (Attach Power of Attorne	D
	Conson Bursa	int	Jason S. Centrella	
	Print Name	l	Print Name	
	Mana / Dwa		Attorney-in-Fact	<u>3</u>
Attest:	Signature	Attest:	Signature	MANNA
	Manage/		Witness ALANE SKAP	F

Note: Provide execution by additional parties, such as joint venturers, if necessary.

EJCDC No. C-615(A) (2007 Edition)

Originally prepared through the joint efforts of the Surety Association of America, Engineers Joint Contract Documents Committee, the Associated General Contractors of America, the American Institute of Architects, the American Subcontractors Association, and the Associated Specialty Contractors.

> Jason S. Centrella Florida Res. Agent #A300489 P.O. Box 600962 Jacksonville, FL 32260 904-230-1324

1. Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to Owner to pay for labor, materials, and equipment furnished by Claimants for use in the performance of the Contract, which is incorporated herein by reference.

- 1. With respect to Owner, this obligation shall be null and void if Contractor:
 - 1.1 Promptly makes payment, directly or indirectly, for all sums due Claimants, and
 - 1.2 Defends, indemnifies, and holds harmless Owner from all claims, demands, liens, or suits alleging non-payment by Contractor by any person or entity who furnished labor, materials, or equipment for use in the performance of the Contract, provided Owner has promptly notified Contractor and Surety (at the addresses described in Paragraph 12) of any claims, demands, liens, or suits and tendered defense of such claims, demands, liens, or suits to Contractor and Surety, and provided there is no Owner Default.

2. With respect to Claimants, this obligation shall be null and void if Contractor promptly makes payment, directly or indirectly, for all sums due.

- 3. Surety shall have no obligation to Claimants under this Bond until:
 - 3.1 Claimants who are employed by or have a direct contract with Contractor have given notice to Surety (at the address described in Paragraph 12) and sent a copy, or notice thereof, to Owner, stating that a claim is being made under this Bond and, with substantial accuracy, the amount of the claim.

3.2

- 3.3 Claimants who do not have a direct contract with Contractor:
 - 1. Have furnished written notice to Contractor and sent a copy, or notice thereof, to Owner, within 90 days after having last performed labor or last furnished materials or equipment included in the claim stating, with substantial accuracy, the amount of the claim and the name of the party to whom the materials or equipment were furnished or supplied, or for whom the labor was done or performed; and
 - 2. Have either received a rejection in whole or in part from Contractor, or not received within 30 days of furnishing the above notice any communication from Contractor by which Contractor had indicated the claim will be paid directly or indirectly; and
 - 3. Not having been paid within the above 30 days, have sent a written notice to Surety (at the address described in Paragraph 12) and sent a copy, or notice thereof, to Owner, stating that a claim is being made under this Bond and enclosing a copy of the previous written notice furnished to Contractor.

4. If a notice by a Claimant required by Paragraph 4 is provided by Owner to Contractor or to Surety, that is sufficient compliance.

5. Reserved.

6. Surety's total obligation shall not exceed the amount of this Bond, and the amount of this Bond shall be credited for any payments made in good faith by Surety.

7. Amounts owed by Owner to Contractor under the Contract shall be used for the performance of the Contract and to satisfy claims, if any, under any performance bond. By Contractor furnishing and Owner accepting this Bond, they agree that all funds earned by Contractor in the performance of the Contract are dedicated to satisfy obligations of Contractor and Surety under this Bond, subject to Owner's priority to use the funds for the completion of the Work.

8. Surety shall not be liable to Owner, Claimants, or others for obligations of Contractor that are unrelated to the Contract. Owner shall not be liable for payment of any costs or expenses of any Claimant under this Bond, and shall have under this Bond no obligations to make payments to, give notices on behalf of, or otherwise have obligations to Claimants under this Bond.

9. Surety hereby waives notice of any change, including changes of time, to the Contract or to related subcontracts, purchase orders, and other obligations.

10. No suit or action shall be commenced by a Claimant under this Bond other than in a court of competent jurisdiction in the location in which the Work or part of the Work is located or after the expiration of one year from the date (1) on which the Claimant gave the notice required by Paragraph 4.1 or Paragraph 4.2.3, or (2) on which the last labor or service was performed by anyone or the last materials or equipment were furnished by anyone under the Contract, whichever of (1) or (2) first occurs. If the provisions of this paragraph are void or prohibited by law, the minimum period of limitation available to sureties as a defense in the jurisdiction of the suit shall be applicable.

11. Notice to Surety, Owner, or Contractor shall be mailed or delivered to the addresses shown on the signature page. Actual receipt of notice by Surety, Owner, or Contractor, however accomplished, shall be sufficient compliance as of the date received at the address shown on the signature page.

12. When this Bond has been furnished to comply with a statutory requirement in the location where the Contract was to be performed, any provision in this Bond conflicting with said statutory requirement shall be deemed deleted herefrom and provisions conforming to such statutory requirement shall be deemed incorporated herein. The intent is that this Bond shall be construed as a statutory Bond and not as a common law bond.

13. Upon request of any person or entity appearing to be a potential beneficiary of this Bond, Contractor shall promptly furnish a copy of this Bond or shall permit a copy to be made.

14. Definitions

- 14.1 Claimant: An individual or entity having a direct contract with Contractor, or with a firsttier subcontractor of Contractor, to furnish labor, materials, or equipment for use in the performance of the Contract. The intent of this Bond shall be to include without limitation in the terms "labor, materials or equipment" that part of water, gas, power, light, heat, oil, gasoline, telephone service, or rental equipment used in the Contract, architectural and engineering services required for performance of the Work of Contractor and Contractor's subcontractors, and all other items for which a mechanic's lien may be asserted in the jurisdiction where the labor, materials, or equipment were furnished.
- 14.2 Contract: The agreement between Owner and Contractor identified on the signature page, including all Contract Documents and changes thereto.
- 14.3 Owner Default: Failure of Owner, which has neither been remedied nor waived, to pay Contractor as required by the Contract, or to perform and complete or otherwise comply with the other terms thereof.

FOR INFORMATION ONLY – (Name, Address, and Telephone) Surety Agency or Broker: Owner's Representative (Engineer or other):

> Jason S. Centrella Florida Res. Agent #A300489 P.O. Box 600962 Jacksonville, FL 32260 904-230-1324

9
